

Date: 24.12.2021

To,
The Director
Northern Regional Office (MoEF),
Bays No. 24-25, Sector- 31-A,
Dakshin Marg, Chandigarh,
Haryana - 160030

Subject: Submission of half yearly Environment Compliance report for IT/ Information Technology Enabled Services (SEZ) project at Village- Gwal Pahari in Tehsil Wazirabad, District- Gurugram, Haryana by M/s ASF Insignia SEZ Pvt. Ltd.

Reference No: SEIAA/HR/2014/331 Dated: 21/02/2014; and amendment thereto vide letter No. SEIAA/HR/2019/201 dated 22.07.2019 and SEIAA(125)/HR/2021/254 Dated 04.03.2021 and Extension of validity of PC vide memo No. SEIAA/HR/2021/465 Dated 11.05.2021).

Dear Sir,

This is with reference to the above captioned subject; Please find attached Six monthly Environmental Compliance report for the period; **April 2021 – September 2021** on the status of conditions of LC (referred above) granted to us. Along with six monthly report pls find attached the Lab Monitoring reports and necessary annexures.

The hard copy of the report is being sent by Speed Post.

Thanking you,

For ASF INSIGNIA SEZ PVT. LTD.

Authorised Signatory

Encl: As above

CC:

1. Haryana State Pollution Control Board, C-11 Sec-6, Panchkula, Haryana.
2. SEIAA, Haryana Bays No. 55 - 58, Parytan Bhawan, 1st floor, Sector - 2, Panchkula, Haryana.
3. Regional Officer Gurgaon (North) Haryana State Pollution Control Board, Vikas Sadan, 1st floor Near DC Court Gurgaon, Pin code - 122001

ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office : ASF Insignia SEZ (IT/ITES), Vatsal Valley (Gwal Pahari), off Gurugram-Faridabad Road, Gurugram-122003, Haryana

:: +91 124 4777200 :: +91 124 4234110 :: corporate@asfinfrastructure.com :: www.asfinfrastructure.com

Regd. Office : 11, Baber Lane, Bengali Market, New Delhi-110001 :: +91 11 23355511 :: +91 1123739298

Corp. Office : ASF Centre, 362-363, Udyog Vihar, Phase-IV, Gurugram-122016 (India)

CIN U45201DL2005PTC140408

Creating Intelligent Spaces

HALF YEARLY ENVIRONMENT COMPLIANCE REPORT

FOR

IT/ITES SEZ PROJECT “ASF INSIGNIA”

LOCATED AT

**Village Gwal Pahari, Tehsil Wazirabad,
District- Gurugram (Haryana)**

Period: April 2021 – September 2021

BY

M/S ASF INSIGNIA SEZ PVT.LTD.



LIST OF ANNEXURES

S. No	Particulates	Annexure
1.	Environment Clearance Letter Nos <i>SEIAA/IIR/2014/331 DATED 21.02.2014, (to be read with amendments granted vide memo nos. SELAA/HR/2019/201 DATED 22.07.2019 and SEIAA (125)/IIR/2021/254 Dated 04.03.2021).</i>	I
2.	Photograph of first aid room	II
3.	Form IV	III
4.	Diescl bills	IV
5.	DG Stack and Noise test report	V
6.	Ambient air test report	VI
7.	Photograph of RWH Pits	VII
8.	Photograph of Fire equipment	VIII
9.	Photograph of Fire Control Room	IX
10.	CTO of B2	X
11.	CTO of B3	XI
12.	CTO of Housing /Residential	XII
13.	STP Test Report	XIII
14.	Borewell outlet	XIV
15.	Form V	XV
16.	Photograph of sanitation facilities	XVI
17.	Photograph of AAC Blocks	XVII
18.	Audit report attached	XVIII



BRIEF DESCRIPTION OF THE PROJECT

The Environmental Clearance for the project was accorded by the SEIAA, Haryana vide letter no. *SEIAA/HR/2014/331 Dated 21.02.2014 (to be read with amendments granted vide memo nos. SEIAA/IIR/2019/201 Dated 22.07.2019 and SEIAA (125)/HR/2021/254 Dated 04.03.2021)*. The project is partially under operation phase and partially under construction/ development // phase.

OVERALL PROJECT

The IT/ITES – Special Economic Zone (SEZ) project is being developed by M/s ASF Insignia SEZ Pvt. Ltd. located in the Village- Gwal Pahari in Tehsil Wazirabad , District- Gurugram, Haryana on a land admeasuring 47.698 acre (1,92,994.58m²). The proposed project will consist of Processing Zone and Non-Processing zone having IT/ITES buildings B1, B2 and B3, Residential apartments, Commercial office, amenity spaces, Shopping spaces and Training Centre etc.

As the project will be completed and operationalized in stage wise manner, therefore the half yearly environment compliance report is prepared for both Construction/development/ and Operation phases. The key parameters of Environmental Clearance and it's amendments vide memos SEIAA/HR/2014/331 dated 21/02/2014 ,SEIAA/HR/2019/201 DATED 22.07.2019 & SEIAA(125)/IIR/2021/254 Dated 04.03.2021 are as below

1. The total proposed built up area of the project is 7,92,209.65 m²
2. The total envisaged water requirement of the project is 2679 KLD which includes both fresh and treated water.
3. The total envisaged fresh water requirement of the project is 988.8 KLD.
4. The total envisaged waste water generation is 1901.56 KLD
5. The total STP capacity of the project is 2300 KLD
6. The proposed green belt development to be 35.15 % of the project area.
7. The total envisaged solid waste generation will be 8.3 TPD.
8. Total 40 numbers of Rain water harvesting pits for the project area are proposed for recharging the ground water level.
9. The total power requirement for the project will be 40 MVA.
10. The source of the water supply during operation phase will be through the CGWA approved bore wells and HUDA water as and when provided
11. The construction/ development work to be undertaken with the treated water of the STPs.
12. The total proposed parking spaces are 10100 ECS.



PART UNDER OPERATION PHASE

The IT/ITES Buildings (B2 & B3), Amenity Podium Building, Facility Management (BMS) Building and Energy Centre Building in Processing Zone and Residential Building (Tower A, B & C) and Club House in Non Processing Zone are under operation for which the necessary approvals from various authorities had already been obtained and the details of the key parameters are as under:

1. The total built up area of the Buildings under operation phase is approx. 3.59 Lacs Sq. Mtrs.
 2. The green area comprising green belt, grass, peripheral green, developed is 20679 sq.m
 3. The total envisaged water requirement of the operational phase of the project is 775 KLD.
 1. The fresh water requirement is 217 KLD. Pls note that due to COVID 19, most of the staff of our Lessees / Units are operating under their WFH policy, therefore there is less consumption during April 2021 to September 21
 2. The waste water generated is 307 KLD. Pls note that due to COVID 19, most of the staff of our Lessees / Units are operating under their WFH policy, therefore there is less generation during April 2021 to September 21
 3. Total solid waste generation is 0.5 TPD. Pls note that due to COVID 19, most of the staff of our Lessees / Units are operating under their WFH policy, therefore there is less generation during April 2021 to September 21
- The source of the water supply is through CGWA for which approval has already been obtained; however, the proposed HUDA water is not available till date and once the HUDA water is available these bore wells shall be used for the standby or to meet the deficit.
4. The wastewater is being treated in the STP of 310 KLD installed for Building B2 and STP of 530 KLD installed for Building B3, the waste water is being treated in the STPs and the treated water is being used for the construction/ development, flushing, HVAC, Anti smog gun and landscape work of the project.
 5. So far, 21 Nos of Rain water harvesting pits have been made for recharging the ground water and are operational.
 6. The available power connection from DIIVBN till date is 4800 KW for the operation and 500 KVA for the construction/ development phase
 7. The total parking provided is 1718 ECS

PART OF THE PROJECT UNDER DEVELOPMENT/ CONSTRUCTION PHASE

The IT/ITES Buildings (B1), Amenity Podium Building, and 66 KV Sub Station Building in Processing Zone and Residential Buildings, Commercial / Retail Buildings, Training Centre Building, Energy Centre Building and other Amenities Building etc in Non-Processing Zone are under development / construction



phase. Proposed Built-up area for buildings under development / construction phase is approx. 4.33 Lacs Sq. Mtrs. Details of the key parameters are as under:

- The balance fresh water requirement of the project will be about 713.8 KLD. This is based on the assumption that as per consumption provided in earlier 6 monthly reports during pre Covid period, our daily consumption of fresh water used to be about 275 KLD.
- The balance solid waste generation will be about 7.10 TPD. This is based on the assumption that as per earlier 6 monthly reports during pre Covid period, our daily generation of solid waste used to be about 1.20 TPD.
- The source of the water supply during operation phase will be through the CGWA approved bore wells and HUDA water (HUDA water connection is yet to be provided by Authorities).
- The construction/ development work is being done with the treated water of the STPs.
- Another 19 nos. of Rain water harvesting pits are proposed for recharging the ground water level.
- The parking requirement as per the Haryana bye laws and as per MoEFCC is 8382 ECS.



Conditions of Environment Clearance No. SEIAA/HR/2014/331 dtd 21.02.2014 (to be read with amendments granted vide memo nos. SEIAA/HR/2019/201 DATED 22.07.2019 read with SEIAA (125)/HR/2021/254 Dated 04.03.2021).		Compliance Status
PART - A		
[1]	<p>"Consent To Establish" shall be obtained from Haryana State Pollution Control Board under air and water act and a copy shall be submitted to the SEIAA, Haryana before the start of any construction work at site.</p>	<p>Complied.</p> <p>The Consent To Establish for the Existing IT/ITES project had been obtained vide letter no. HSPCB/TAC/2011/663 dated 07.03.2011 from Haryana State Pollution Control Board which was submitted to SEIAA, Haryana.</p> <p>The Consent to Establish no. HSPCB/Consent/:2808615GUNOCTE1390645 dated 27.02.2015 was obtained.</p> <p>The Consent To Establish for the Expansion Phase had been obtained vide letter no. HSPCB/Consent/:320303318GUNOCTE5008171 dated 07.03.2018 valid up to 20.02.2021</p> <p>The Consent To Establish for the Project obtained vide letter no. HSPCB/Consent/:320303321GUNOCTE12599143 dated 23.06.2021 valid up to 20.02.2024</p>
[2]	<p>A first aid room will be provided in the project both during construction and operation of the project.</p>	<p>Complied.</p> <p>First Aid Facilities are attached as an Annexure II</p>



[3]	Adequate drinking water and sanitary facilities should be provided for construction workers at the site. Provision should be made for mobile toilets. Open defecation is strictly prohibited. The safe disposal of waste water and solid wastes generated during the construction phase should be ensured.	Complied. Drinking water, sanitary facilities, mobile toilets are provided for the construction workers at the site. No open defecation is being allowed. Safe disposal of waste water and solid waste is being ensured.
[4]	All the topsoil excavated during construction activities should be stored for use in horticulture/landscape development within the project site.	Ensured
[5]	The project proponent shall ensure that the building material required during construction phase is properly stored within the project area and disposal of construction waste should not create any adverse effect in the neighbouring communities and should be disposed of after taking necessary precautions for general health and safety aspects of people, only in approved sites with the approval of competent authority.	Complied. Building material is properly stored at the designated areas of the site and construction waste / Debris is mainly used in the internal fillings and surplus disposed-off at the approved sites of MCG
[6]	Construction spoils, including bituminous material and other hazardous materials, must not be allowed to contaminate watercourses and the dump sites for such materials must be secured so that they should not leach into the ground water and any Hazardous waste generated during the construction phase, should be disposed as per applicable rules and norms with necessary approval of the Haryana State Pollution Control Board	Complied.
[7]	The diesel generator set to be used during construction phase should be of ultra-low sulphur diesel type and should conform to Environment (Protection) Rules prescribed for air and noise emissions standards.	Complied. Receipts of diesel bills attached as per Annexure -IV



[8]	The Diesel required for operating DG set shall be stored in underground tanks and if required, clearance from chief controller of Explosive shall be taken.	Complied. We have construction power sanctioned from DHVBN. For DG sets provided for construction phase, diesel is stored in 200 Ltrs drums
[9]	Ambient noise level should conform to residential standards both during day and night. Incremental pollution loads on the ambient air and noise quality should be closely monitored during construction phase. Adequate measures should be taken to reduce ambient air and noise level during construction phase, so as to conform to the stipulated standards.	Complied. Ambient air monitoring report for the month of June 2021 is enclosed ref. Annexure – VI
[10]	Fly ash should be used as building material in the construction as per the provision of Fly Ash Notification of September, 1999 and amended as on 27 th August, 2003.	Complied AAC Blocks having fly ash content of about 50 to 70% are being used for block works
[11]	Storm water control and its reuse as per CGWB and BIS standards for various applications should be ensured	Ensured. For complete project, 40 nos of RWH pits are envisaged. Out of which 21 nos of RWH pits are operational. Photographs of RWH Pits are attached in Annexure – VII
[12]	Water demand during construction should be reduced by use of pre-mixed concrete, curing agents and other best practices referred.	Complied.
[13]	In view of the several constraints in water supply augmentation in the region and sustainability of water resources, the developer will submit the NOC from CGWA specifying water extraction quantities and assurance from HUDA/ utility provider indicating source of water supply and quantity of water with details of intended use of water – potable and non-potable. Assurance is required for both construction and operation stages separately. It shall be submitted to the SEIAA and RO, MoEF Chandigarh, before the start of construction	Complied. Fresh water requirement is being met through ground water for which NOC from CGWA had been obtained. For Construction activities, treated water from in house STP is available. In addition, surplus treated water if required is being provided from nearby CSTP for which assurance from HUDA has been obtained.



[14]	Roof should meet prescriptive requirements as per Energy Conservation Building Code by using appropriate thermal insulation material	Complied. Overdeck thermal insulation provided for all the buildings
[15]	Opaque wall should meet prescriptive requirements as per Energy Conservation Building Code which is proposed to be mandatory for all conditioned spaces while it is desirable for non air- conditioned spaces by use of appropriate thermal insulation material to fulfill requirement.	Ensured.
[16]	The approval of the competent authority shall be obtained for structural safety of the building due to earthquake, adequacy of firefighting equipment's, etc. as per National Building Code including protection measures from lightening etc. If any Forest Conservation Act shall be taken from Competent Authority.	Complied. Structure stability certificate has been obtained. Structure, firefighting are being constructed as per National Building Code and lightning protection measures are being provided
[17]	Overexploited ground water and impending severe shortage of water supply in the region requires the developer to redraw the water and energy conservation plan. Developer shall reduce the overall footprint of the proposed development. Project proponent shall incorporate water efficiency/ savings measures as well as water reuse/ recycling within 3 month and before start of construction to the SELAA, Haryana and RO, MoEF, GOI, Chandigarh	Complied
[18]	The project proponent as stated in the proposal shall construct 40 rain water harvesting pits for recharging the ground water within the project premises. RWH pits shall be designed to make provisions for silting chamber and removal of floating matter before entering harvesting pit. Maintenance budget and persons responsible for Maintenance must be provided. Care shall also be taken that contaminated water do not enter any RWH pit.	Complied. 21 Nos of RWH pits has been designed and constructed in accordance with the approved plans.




[19]	The project proponent shall provide for adequate fire safety measure and equipment's as required by Haryana Fire Service Act, 2009 and instructions issued by the local Authority Directorate of fire from time to time. Further the project proponent shall take necessary permission regarding fire safety scheme/NOC form competent Authority as required.	Complied. Adequate fire safety measure and equipment's are provided as per the provision of Haryana Fire Service Act, 2009 and relevant norms. Necessary Fire NOC is being taken.
[20]	The project proponent shall obtain assurance from the DHBVN for supply of 40 MVA of power supply before the start of construction. In no case project will be operational solely on generators without any power supply from any external power utility.	Complied.
[21]	Detail calculation of power load and ultimate power load of the project shall be submitted to DHBVN under intimation to SEIAA Haryana before the start of construction. Provisions shall be made for electrical infrastructure in the project area.	Complied.
[22]	The project proponent shall not raise any construction in the natural land depression/Nallah/ water course and shall ensure that the natural follow from the Nallah/water course is not obstructed.	Noted
[23]	The project proponent shall keep the plinth level of the building blocks sufficiently above the level of the approach road to the project as per prescribed by laws. Levels of the other areas in the projects shall also be kept suitably so as to avoid flooding.	Complied.
[24]	Construction shall be carried out so that density of population does not exceed norms approved by Director General Town and Country Department Haryana.	Complied. All Building plans are being approved by The Unit Approval Committee Chaired by Development Commissioner, NSEZ, Noida in consultation with Town and Country Department Haryana.



[25]	The project proponent shall submit an affidavit with the declaration that ground water will not be used for construction and only treated water should be used for construction	Complied. Affidavit copy of the same had been provided earlier.
[26]	The project proponent shall not cut any existing tree and project landscaping plan should be modified to include those trees in green area.	Complied
[27]	The project proponent shall ensure that EBC norms for composite climate zone are met. In particular building envelope, HVAC service, water heating, pumping, lighting and electrical infrastructure must meet ECBC norms.	Complied.
[28]	The project proponent shall provide 3 meter high barricade around the project area, dust screen for every floor above the ground, proper sprinkling and covering of stored material to restrict dust and air pollution during construction.	Complied. Every listed measure and any further guidelines released on dust and air pollution controls applicable to construction activities are being adhered. Deployed Anti-smog gun immediately after the guidelines by HSPCB were issued.
[29]	The project proponent shall construct a sedimentation basin in the lower level of the project site to trap pollutant and other wastes during rains.	Complied
[30]	The project proponent shall provide proper Rasta of proper width and proper strength for each project before the start of construction.	Complied
[31]	The project proponent shall ensure that the U-value of the glass is less than 3.177 and Maximum solar heat gain co-efficient is 0.25 for vertical fenestration.	Noted
[32]	The project proponent shall adequately control construction dusts like silica dust, non-silica dust, and wood dust. Such dusts shall not spread outside project premises project Proponent shall provide respiratory protective equipment to all construction workers.	Complied. Adequate control measures including protective equipment for construction workers are in place



[33]	The project proponent shall provide one refuse area till 24 meter, one till 39 meter and one after every 15 meter as per National Building Code. The project proponent shall not convert any refuse area in the habitable space and it should not be sold out/commercialized.	Complied The applicable refuse areas will be provided at designated heights of the building as per NBC.
[34]	The project proponent shall provide fire control room and fire officer for building above 30 meters as per National Building Code.	Complied. Photograph of fire control room is attached as an Annexure IX
[35]	The project proponent shall obtain permission of Mines and Geology Department for excavation of soil before the start of construction	Complied.
[36]	The project proponent shall seek specific prior approval from concerned local Authority/HUDA regarding provision of storm drainago and sewerage system including their integration with external services of IIUDA / Local authorities beside other required services before taking up any construction activity.	Noted
[37]	The site for solid waste management plan is earmarked on the layout plan and the detailed project for setting up the solid waste management plan shall be submitted of the Authority within one month.	Noted.
[38]	Vertical fenestration shall not exceed 40% of total wall area.	Noted.
[39]	The project proponent shall discharge excess of treated waste water/ storm water in the public drainage system and shall seek permission of IIUDA before the start of construction.	Noted.
[40]	The project proponent shall seek NOC from Town and country department regarding height of the building allowed in the skyline of that area.	Complied.
[41]	The project proponent shall ensure that structural stability to withstand earthquake of magnitude 8.5 on richter scale.	Ensured. Ensured as per NBC Norms.



[42]	The project proponent shall ensure that no construction activity is undertaken either on surface or below or above surface of revenue rasta passing through the project area.	Ensured.
[43]	The project proponent shall indicate the width and length of revenue Rasta passing through the project area on sign board and shall display the same at both the ends of revenue Rasta stretch, for awareness of public, sign board also display the message that the is public rasta / road and any citizen can use it. There shall not be any gate with or without guards on revenue rasta.	Noted.
[44]	The project proponent shall ensure that natural flow of existing nallah is never obstructed and shall seek NOC from Irrigation Department regarding this before the start of construction.	Noted
[45]	The project proponent shall ensure that in case of excessive flow of water in nallah, the structural integrity of buildings alongside the nallah is not breached in any circumstances.	Noted.
[46]	The project proponent shall ensure that there should not be any water logging on the bed of nallah even in case of excessive rain.	Noted.
[47]	The project proponent shall ensure that sewerage pipe line should not cross over the nallah and project proponent shall maintain separate STP in the plot area across the nallah.	Noted.
[48]	The project proponent shall ensure that sewerage system and storm drainage system shall be planned by taking into account the natural slope of original land and approval from HUDA and irrigation department shall be taken before the start of construction.	Ensured.
[49]	The project proponent shall ensure that bed of nallah is not encroached in any manner, while constructing the culvert over the nallah.	Noted.



[50]	The project proponent shall ensure plinth level of the building block is 1.5 meter above 100 years flood level.	Complied.
[51]	The project proponent shall provide pervious surface instead of impervious and hard surface in order to reduce overflow of water in nallah.	Noted.
[52]	The project proponent shall ensure proper drainage in the project area as the project area is uneven and undiluted.	Ensured.
B. Operational Phase		
[a]	“Consent to Operate” shall be obtained from Haryana State Pollution Control Board under Air and Water Act and a copy shall be submitted to the SEIAA, Haryana.	<p>Complied. The Consent to Operate has already been obtained and submitted.</p> <p>The consent to operate renewal for Building B2 has been obtained via HSPCB/Consent/: 320303321GUNOCTO 15794928 dated 04.10.2021 valid up-to 30.09.2022 and attached as an Annexure X.</p> <p>The consent to operate renewal for Building B3 has been obtained via HSPCB/Consent/: 320303317GUNOCTO4398636 dated 09.08.2017 valid up to 30.09.2022 and attached as an Annexure XI.</p> <p>The consent to operate for Housing /Residential has been obtained via Certificate No. HSPCB/consent/: 13116320GUNOCTO6503967 Dated 09.03.2020 Valid up to 31.03.2022 and attached as an Annexure XII.</p>
[b]	The Sewage Treatment Plant (STP) shall be installed for the treatment of the sewage to prescribed including odor and treatment effluent shall be recycled. The installation of STP should be certified by an independent expert and a report in this regard should be submitted to the SEIAA, Haryana before the project is commissioned for operation. Tertiary treatment of waste water is mandatory. Discharge of treated sewage shall	<p>Complied.</p> <p>The STP of 530, 310 KLD and 50 KLD capacities for B3 , B2 and Housing /Residential respectively has been installed. STP feasibility report and photographs of the same has already been submitted. Report of independent expert along with STP inlet and outlet test report are attached as an Annexure.-XIII</p>



	conform to the norms and standards of HSPCB, Panchkula project proponent shall implement such STP Technology which does not required filter backwash	
[c]	Separation of the grey and black water should be done by use of dual plumbing line. Treatment of 100% grey water by decentralized treatment should be done ensuring that the re-circulate water should have BOD level less than 10mg/liter. And the recycled water will be used for flushing, gardening and DG set cooling etc. to achieve zero exit discharge.	Complied: Dual plumbing lines have been provided. Tertiary treatment of grey water is being carried out. Treated water is being used for flushing, gardening and HVAC cooling. We have zero exit discharge.
[d]	For disinfection of the treated wastewater ultra-violet radiation or ozonization process should be used.	Ensured.
[c]	Diesel power generating sets proposed as source of back power for lifts, common area illumination and for domestic use should be of enclosed type and conform to rules made under the Environment (Protection) Act, 1986. The location of the DG sets should be in the basement as promised by the project proponent with appropriate stack heights as per the CPCB norms. The diesel used for the DG sets shall be ultra-low sulphur diesel(35ppm sulphur), instead of low sulphur diesel.	Complied. DG Sets used in the project site for various purposes are placed in a acoustic treated area which is as per CPCB norms. The stack heights are as per CPCB norms.
[f]	Ambient Noise level should be controlled to ensure that it does not exceed the prescribed standards both within and at the boundary of the Proposed IT/ITES project.	Complied




[g]	The project proponent as stated in the proposal should maintain at least 35.15 % as green cover area for tree plantation especially all around the periphery of the project and on the road sides preferably with local species which can provided protection against noise and suspended particulates matter, the open spaces inside the project should be preferably landscaped and covered with Vegetation/grass, herbs & shrubs. Only locally available plant species shall be used.	<p>Complied.</p> <p>We have provided for green cover as per EC conditions. Locally available plant species have been planted. Tree plantation around the periphery of the project has been done in the operational phase.</p>
[h]	The project proponent shall strive to minimize water in irrigation of landscape by minimizing grass area, using native variety, xeriscaping and mulching, utilizing efficient irrigation system. Scheduling irrigation only after checking evapo-transpiration data.	<p>Complied.</p> <p>Provided efficient irrigation system with Pop up sprinklers. The operation of irrigation system is done as per a schedule thus ensuring efficient and only required amount of irrigation.</p>
[i]	Rain water harvesting for roof run-off and surface run-off, as per plan submitted should be implemented. Before recharging the surface run off, pre-treatment through sedimentation tanks must be done to remove suspended matter, oil and grease. The bore well for rainwater recharging shall be kept at least 5 mts, above the highest ground water table. Care shall be taken that contaminated water do not enter any RWH pit. The project proponent shall avoid Rain water harvesting of first 10 minutes of rain fall. Roof top of the building shall be without any toxic material or which can contaminate rain water. Wire mesh and filters should be used wherever required.	<p>Ensured</p>
[j]	The ground water level and its quality should monitor regularly in consultation with Central Ground Water Authority.	<p>Complied.</p> <p>Ground water level and its quality are being monitored at regular intervals. Reports on water level and quality are being sent to the competent authorities on regular basis.</p> <p>Test reports of Bore well Outlet are attached as an Annexure - XIV</p>




[k]	A report on the energy conservation measure conforming to energy conservation norms finalized by Bureau of Energy Efficiency should be prepared incorporating details about building materials & Technology, R & U factors etc and submitted to the SEIAA, Haryana in three months' time.	Ensured. Energy Audit report on Energy Conservation prepared as per the norms by Bureau of Energy Efficiency. The Copy of the same had been provided earlier
[l]	Energy conservation measure like installation of LED for lighting the areas outside the building should be integral part of the project design and should be in place before project commission. Use of solar panels must be adapted to the maximum energy conservation	Ensured. Energy conservation methods adopted like installation of LED lights, Solar Panels for heating of water, VFDs, Double Glass Units, Shadings etc.
[m]	The project proponent shall use zero ozone depleting potential material in insulation, refrigeration, air- conditioning and adhesive; project proponent shall also provide Halon free fire suppression system	Ensured.
[n]	The solid waste generated should be properly collected and segregated as per the requirement of the MSW Rules, 2000 and as amended from time to time. The bio-degradable waste should be treated by appropriate technology at the site ear-marked with in the project area and dry/inert solid waste should be disposed off to the approved sites for land filling after recovering recyclable material.	Ensured.
[o]	The provision of the solar water heating system shall be as per norms specified by HAREDA and shall be made operational in each building block.	Complied.



[p]	The traffic plan and the parking plan proposed by the project proponent should be adhered to meticulously with further scope of additional parking for future requirement. There should be no traffic congestion near the entry and exit points from the roads adjoining the proposed project site. Parking should be fully internalized and no public space should be used	Ensured. Parking facility had been provided within the premises as per the norms. There is no traffic congestion on the site.
[q]	The project shall be operationalized only when HUDA / local authority will provides domestic water supply system in the area.	Complied. Currently, HUDA has no provision of water supply in this area or neighbourhood. NOC for the regularization of existing tube well has been obtained from the nominated agency of Central Ground Water Authority (CGWA). The copy of the same attached. Also, assurance to provide domestic water supply when available with HUDA in Gwal Pahari is available.
[r]	Operation and maintenance of STP, Solid waste management and electrical infrastructure, pollution control measure shall be ensured even after the completion of project.	Noted
[s]	Different type of wastes should be disposed off as per provisions of municipal solid waste, biomedical waste, hazardous waste, e-waste, batteries & plastic rules made under Environmental Protection Act, 1986, Particularly E-waste and battery waste shall be disposed of as per existing E-waste Management Rules 2011 and Batteries Management Rules 2001, The project proponent should maintain a collection centre for E-waste and it should be disposed of to only registered and authorized dismantler / recycler.	Complied. All kind of wastes are handled and disposed-off as per applicable Rules.
[t]	Standards for discharge of environmental pollutants as enshrined in various schedules of rules 3 of Environmental Protection Rules 1986 shall be strictly Complied with.	Complied



[u]	The project proponent shall make provision for guard pond and other provisions for safety against failure in the operation of wastewater treatment facilities. The project proponent shall also identify acceptable outfall for treated effluent.	Noted STPs of B 2 and B 3 are interconnected so that in case of any breakdown in one STP, the sewerage of the same could be diverted to the other STP.
[v]	The project proponent shall ensure that the stack height of DG sets is as per the CPCB guide lines and also ensure that the emission standards of noise and air are within the CPCB prescribed limits. Noise and Emission level of DG sets greater than 800KVA shall be as per CPCB latest standards for high capacity DG Sets.	Ensured and made all provisions as per CPCB norms.
[w]	All electric supply exceeding 100amp, 3 phases shall maintain the power factor between 0.98 lag to 1 at the point of connection.	Complied.
[x]	The project proponent shall minimize heat island effect through shading and reflective or pervious surface instead of hard surface.	Ensured.
[y]	The project proponent shall use only treated water instead of fresh water for HVAC and DG cooling. The project proponent shall also use evaporative cooling technology and double stage cooling system for HVAC in order to reduce water consumption. Further temperature, relative humidity during summer and winter seasons should be kept at optimal level. Variable speed drives, best Co-efficient of Performance (CoP), as well as optimal Integrated Point Load Value and minimum outside fresh air supply may be restored for conservation of power and water. Coil type cooling DG sets shall be used for saving cooling water consumption for water cooled DG sets.	Complied. Treated water of STP being used for cooling of equipment.



[z]	The project proponent shall ensure that the transformer is constructed with high quality grain oriented, low loss silicon steel and virgin electrolyte grade copper. The project proponent shall obtain manufacturer's certificate also for that.	Complied.
[aa]	Water supply shall be metered among different users and different utilities.	Ensured. Flow meters provided at various outlets.
[ab]	The project proponent shall ensure that exit velocity from stack should be sufficiently high. Stack shall be designed in such a way that there is no stack down -water under any meteorological conditions	Ensured.
[ac]	The project proponent shall provide water sprinkling system in the project area to suppress the dust in addition to the already suggested mitigation measures in the Air Environment chapter of EMP.	Ensured.
[ad]	The project proponent shall ensure proper Air Ventilation and light system in the basements area for comfortable living of human being and shall ensure that number of Air Changes per hour/(ACH) in basement never falls below 15. In case of emergency capacity for increasing ACH to the extent of 30 must be provided by the project proponent.	Ensured.
[ae]	The project proponent shall get the inspection of nallah before the onset of monsoon season every year from Irrigation department.	Noted.
[af]	The project proponent shall not discharge untreated water in the nallah and also shall not throw any solid waste in the nallah.	Ensured.
PART-B GENERAL CONDITIONS		



B [i]	The project proponent shall ensure the commitments made in Form-1, Form-1A, EIA/EMP and other documents submitted to the SEIAA for the protection of environment and proposed environmental safeguards are Complied with in letter and spirit. In case of contradiction between two or more documents on any point, the most environmentally friendly commitment on the point shall be taken as commitment by project proponent.	Complied. All the commitments made in the Form-1, Form-1A, EIA/EMP and other documents submitted to the SEIAA had been and are being complied strictly during the construction as well as the operation phase of the project.
B [ii]	The project proponent shall also submit six monthly reports on the status of compliance of the stipulated EC conditions including results of monitored data(both in hard copies as well as e-mail) to the northern regional office of MoEF, the respective Zonal office of CPCB, HSPCB and SEIAA Haryana.	Complied. Six monthly compliance reports on the status of compliance of the stipulated EC conditions including results of monitored data is being submitted to the HSPCB, Northern Regional office-MoEF, SEIAA-Haryana and Regional office of CPCB as per the stipulated conditions.
B [iii]	STP outlet after stabilization and stack emission shall be monitored monthly. Other environmental parameters and green belt shall be monitored on quarterly basis. After every 3 months, the project proponent shall conduct environmental audit and shall take corrective measure, if required without delay.	Noted
B [iv]	The SEIAA, Haryana reserves the right to add additional safeguard measures subsequently, if found necessary, Environmental Clearance granted will be revoked if it is found the false information has been given for getting approval of this project. SEIAA reserves the right to revoke the clearance if conditions stipulated are not implemented to the satisfaction of SEIAA/MoEF.	Noted
B [v]	The project proponent shall not violate any judicial orders/pronouncements issued by any court/Tribunal.	Noted



B [vi]	All other statutory clearance such as the approvals for storage of diesel from Chief Controller of Explosive, Fire Department, Civil Aviation Department, Forest Conservation Act, 1980 and Wildlife (Protection) Act, 1972, P.I.P.A, 1900, Forest Act 1927 etc shall be obtained, as applicable by project proponent from the respective authorities prior to construction of the project	Ensured Obtained all the approvals required from the competent authorities.
B [vii]	The project proponent should inform the public that the project has been accorded Environment Clearance by the SEIAA and copies of the clearance letter are available with the state pollution control board & SEIAA. This should be advertised within 7 days from the date of issue of the clearance letter at least in two local newspapers that are widely circulated in the region and copy of the same should be forwarded to SEIAA Haryana. A copy of Environmental Clearance conditions shall also be put on project proponent's web site for public awareness.	Complied.
B [viii]	Under the provision of Environment (Protection) Act, 1986, legal action shall be initiated against the project proponent if it was found that construction of the project has been started before obtaining prior Environmental Clearance.	Noted.
B [ix]	Any appeal against the this Environmental Clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under section 16 of the National Green Tribunal Act, 2010.	Noted.
B [x]	The project proponent shall put in place corporate Environment Policy as mentioned in MoEF, GOI OM No. J-11013/41/2006-IA II (I) dated 26.4.2012 within 3 months period. Latest corporate Environmentally Policy should be	Complied



	submitted to SEIAA within 3 months of issuance of this letter.	
B [xi]	The fund ear-marked for environment protection measures should be kept in separate account and should not be diverted for other purposes and year wise expenditure shall be reported to the SEIAA/RO MoEF GOI under rules prescribed for Environment audit.	Noted.
B [xii]	The project proponent shall ensure the compliance of Forest Department, Haryana Notification no. S.O.121/PA2/1900/S.4/97 dated 28.11.1997	Complied. NOC from the deputy conservator of forest had been obtained vide letter No. 1627-G dated 05-03-2010. The copy of the same was submitted earlier.
B [xiii]	The project proponent shall ensure that no vehicle during construction/operation phase enter the project premises without valid "Pollution Under Control" certificate from competent authority.	Noted
B [xiv]	The project proponent is responsible for compliance of all conditions in Environmental Clearance letter and project proponent cannot absolve himself / herself for the responsibility by shifting it to any contractor engaged by project proponent.	Noted.
B [xv]	The project proponent shall seek fresh environmental clearance if at any stage there is change in the planning of the proposed project.	Noted.



B [xvi]	<p>The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely, PM_{2.5}, PM₁₀, SO_x, NO_x, Ozone, Lead, CO, Benzene, Ammonia, Benzopyrine, arsenic and nickel. (Ambient levels as well as stack emissions) or critical sectoral parameters, indicated for the project shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.</p>	Noted.
B [xvii]	<p>The environmental statement for each financial year ending 31st March in Form -V as is mandated to be submitted by the project proponent to the HSPCB Panchkula as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of the EC conditions and shall also be sent to the respective Regional Offices of MoEF by e-mail.</p>	<p>Noted. Form V is attached as an Annexure XV</p>
B [xviii]	<p>The project proponent shall conduct environment audit at every three months interval and thereafter corrected measures shall be taken without any delay. Details of environmental audit and corrective measures shall be submitted in monitoring report.</p>	<p>Noted. Latest Audit report attached as an Annexure XVIII</p>



STATE ENVIRONMENT IMPACT ASSESSMENT AUTHORITY HARYANA
Bay No. 55-58, Prayatan Bhawan, Sector-2, GANCKHULA

No. SEIAA/HR/2014/331

Dated: 21.08.2014

To

M/s ASF Insignia SEZ Pvt. Ltd.
(formally known as M/S Canton Buildwell Pvt. Ltd.)
Mr. P.K. Gupta, Senior Vice President,
11, Habar Lane, Bengali market,
New Delhi - 110 001

Subject: Environmental Clearance for Expansion of (phase-II) IT/Information Technology Enable Services (SEZ) at Village- Gwal Pahari in Solna Block, District-Gurgaon.

Dear Sir,

This letter is in reference to your application no. CBPL/01/09/001/520 dated 21.03.2011 addressed to M.S. SEIAA, Haryana received on 22.03.2011 and subsequent letters dated 17.08.2012, 22.08.2012, 30.08.2012, 18.09.2012, 23.04.2013 & 09.07.2013 seeking prior Environmental Clearance for the above project under the EIA Notification, 2006. The proposal has been appraised as per prescribed procedure in the light of provisions under the EIA Notification, 2006 on the basis of the mandatory documents enclosed with the application viz., Form-I, Form-I-A & Conceptual Plan, EIA/EMP on the basis of approved TOR and additional clarifications furnished in response to the observations of the State Expert Appraisal Committee (SEAC) constituted by MOEF, GOI vide their Notification 23.3.2012, in its meetings held on 20.07.2012, 05.09.2012, 08.04.2013, 06.06.2013 and 26.08.2013 awarded "Gold" grading to the project.

It is inter-alia, noted that the project involves the construction of expansion of (phase-II) IT/ITES (SEZ) at Village- Gwal Pahari in Solna Block, District- Gurgaon on a plot area of 192994.58 sqmt (47.698 Acres) Notified by Ministry of Industry and commerce Government of India. The Existing area of Phase-I is 401616.56 sqmt (25.11 Acres) and the proposed Phase-II plot area is 91378.02 sqmt (22.58 Acres). The total built up area after expansion shall be 489390 sqmt (Existing approved area of Phase-I 276249 sqmt + Expansion area of Phase-II 213141 sqmt). The total built up area for the processing zone after expansion shall be 354083 sqmt (Existing phase-I 201409 + proposed Phase-II under Expansion 152674 sqmt). The total built up area for the non-processing zone after expansion shall be 135307 sqmt (Existing phase I 74840 + proposed Phase-II under Expansion 60467 sqmt). The proposed phase-II project shall have of IT/ITES buildings and commercial building in the processing zone and in the non-processing zone phase-II the project proponent has proposed housing and service

apartment, commercial-office amenity and shopping spaces and training center. The maximum height of the building shall be approximately 90 meters. The total water requirement shall be 1843.2 M³/day (Phase-I 965.6 M³/day + 877.6 Phase-II). The fresh water requirement shall be 988.8 M³/day (Phase-I 531.7 M³/day + 457.1 Phase-II) which will be sourced from existing bore wells and permission of competent authority has been obtained. The total waste water generation shall be 949.4 M³/day (Phase-I 482.12 M³/day + 467.3 Phase-II), which will be treated in the 3 STPs of 350 M³/day capacity. The total power requirement shall be 40 MVA (phase-I 19.5 MVA + phase-II 20.5 MVA) which will be supplied by DHBVN through 66 KV grid line from sector-56 of Gurgaon for the connection load sanctioned of 50 MVA. The Project Proponent has proposed to develop 35.15% of project area for tree plantation (20.33%), landscape (9.81%) and water bodies (5.01%). The Project Proponent proposed to construct 40 rain water harvesting pits. The solid waste generation will be 8.3TPD (phase-I 4.3 TPD + phase-II 4TPD). The bio-degradable waste will be treated in the project area by adopting appropriate technology. The total parking spaces proposed are 10100 ECS.

[3] The State Expert Appraisal Committee, Haryana after due consideration of the relevant documents submitted by the project proponent and additional clarification furnished in response to its observations, have recommended the grant of environmental clearance for the project mentioned above, subject to compliance with the stipulated conditions. Accordingly, the State Environment Impact Assessment Authority in its meeting held on 24.01.2014 decided to agree with the recommendations of SEAC to accord necessary environmental clearance for the project under Category 8(b) of EIA Notification 2006 subject to the strict compliance with the specific and general conditions mentioned below:-

PART A-
SPECIFIC CONDITIONS:-

Construction Phase:-

- [1] "Consent for Establish" shall be obtained from Haryana State Pollution Control Board under Air and Water Act and a copy shall be submitted to the SEIAA, Haryana before the start of any construction work at site.
- [2] A first aid room as proposed in the project report shall be provided both during construction and operational phase of the project.
- [3] Adequate drinking water and sanitary facilities shall be provided for construction workers at the site. Provision should be made for mobile toilets. Open defecation by the labourers is strictly prohibited. The safe disposal of waste water and solid wastes generated during the construction phase should be ensured.
- [4] All the topsoil excavated during construction activities shall be stored for use in horticulture/landscape development within the project site.

- [5] The project proponent shall ensure that the building material required during construction phase is properly stored within the project area and disposal of construction waste should not create any adverse effect on the neighboring communities and should be disposed of after taking necessary precautions for general safety and health aspects of people, only in approved sites with the approval of competent authority.
- [6] Construction spoils, including bituminous material and other hazardous materials, must not be allowed to contaminate watercourses and the dump sites for such material must be secured so that they should not leach into the ground water and any hazardous waste generated during construction phase, should be disposed off as per applicable rules and norms with necessary approval of the Haryana State Pollution Control Board.
- [7] The diesel generator sets to be used during construction phase shall be of ultra low sulphur diesel type and should conform to Environment (Protection) Rules prescribed for air and noise emission standards.
- [8] The diesel required for operating DG sets shall be stored in underground tanks and if required, clearance from Chief Controller of Explosives shall be taken.
- [9] Ambient noise levels shall conform to the residential standards both during day and night. Incremental pollution loads on the ambient air and noise quality should be closely monitored during construction phase. Adequate measures should be taken to reduce ambient air pollution and noise level during construction phase, so as to conform to the stipulated residential standards of CPCB/MoEF.
- [10] Fly ash shall be used as building material in the construction as per the provisions of Fly Ash Notification of September 1999 and as amended on 27th August 2003.
- [11] Storm water control and its re-use as per CGWB and BIS standards for various applications should be ensured.
- [12] Water demand during construction shall be reduced by use of pre-mixed concrete, curing agents and other best practices.
- [13] In view of the severe constrains in water supply augmentation in the region and sustainability of water resources, the developer will submit the NOC from CGWA specifying water extraction quantities and assurance from HUDA/ utility provider indicating source of water supply and quantity of water with details of intended use of water - potable and non-potable. Assurance is required for both construction and operation stages separately. It shall be submitted to the SEIAA and RO, MOEF, Chandigarh before the start of construction.
- [14] Roof must meet prescriptive requirement as per Energy Conservation Building Code by using appropriate thermal insulation material.

- [15] Opaque wall must meet prescriptive requirement as per Energy Conservation Building Code which is proposed to be mandatory for all air conditioned spaces while it is desirable for non-air-conditioned spaces by use of appropriate thermal insulation material to fulfill requirement.
- [16] The approval of the competent authority shall be obtained for structural safety of the building on account of earthquake, adequacy of fire fighting equipments, etc. as per National Building Code including protection measures from lightning etc. If any forest land is involved in the proposed site, clearance under Forest Conservation Act shall be obtained from the competent Authority.
- [17] Overexploited groundwater and impending severe shortage of water supply in the region requires the developer to redraw the water and energy conservation plan. Developer shall reduce the overall footprint of the proposed development. Project proponent shall incorporate water efficiency /savings measures as well as water reuse/recycling within 3 months and before start of construction to the SEIAA, Haryana and RO, MOEF, GOI, Chandigarh.
- [18] The Project Proponent as stated in proposal shall construct 40 nos. rain water harvesting pits for recharging the ground water within the project premises. Rain water harvesting pits shall be designed to make provisions for silting chamber and removal of floating matter before entering harvesting pit. Maintenance budget and persons responsible for maintenance must be provided. Care shall also be taken that contaminated water do not enter any RWH pit.
- [19] The project proponent shall provide for adequate fire safety measures and equipments as required by Haryana Fire Service Act, 2009 and instructions issued by the local Authority/Directorate of fire from time to time. Further the project proponent shall take necessary permission regarding fire safety scheme/NOC from competent Authority as required.
- [20] The Project Proponent shall obtain assurance from the DHBVN for supply of 40 MVA of power supply before the start of construction. In no case project will be operational solely on generators without any power supply from any external power utility.
- [21] Detail calculation of power load and ultimate power load of the project shall be submitted to DHBVN under intimation to SEIAA Haryana before the start of construction. Provisions shall be made for electrical infrastructure in the project area.
- [22] The Project Proponent shall not raise any construction in the natural land depression / Nallah/water course and shall ensure that the natural flow from the Nallah/water course is not obstructed.

- [23] The Project Proponent shall keep the plinth level of the building blocks sufficiently above the level of the approach road to the Project. Levels of the other areas in the Projects shall also be kept suitably so as to avoid flooding.
- [24] Construction shall be carried out so that density of population does not exceed norms approved by Director General Town and Country Department Haryana.
- [25] The Project Proponent shall submit an affidavit with the declaration that ground water will not be used for construction and only treated water should be used for construction.
- [26] The project proponent shall not cut any existing tree and project landscaping plan should be modified to include those trees in green area.
- [27] The project proponent shall ensure that ECBC norms for composite climate zone are met. In particular building envelope, HVAC service, water heating, pumping, lighting and electrical infrastructure must meet ECBC norms.
- [28] The Project Proponent shall provide 3 meter high barricade around the project area, dust screen for every floor above the ground, proper sprinkling and covering of stored material to restrict dust and air pollution during construction.
- [29] The project proponent shall construct a sedimentation basin in the lower level of the project site to trap pollutant and other wastes during rains.
- [30] The project proponent shall provide proper rasta of proper width and proper strength for the project before the start of construction.
- [31] The project proponent shall ensure that the U-value of the glass is less than 3.177 and maximum solar heat gain co-efficient is 0.25 for vertical fenestration.
- [32] The project proponent shall adequately control construction dusts like silica dust, non-silica dust, wood dust. Such dusts shall not spread outside project premises. Project Proponent shall provide respiratory protective equipment to all construction workers.
- [33] The project proponent shall provide one refuse area till 24 meter, one till 39 meter and one each after 15 meter as per National Building Code. The project proponent shall not convert any refuse area in the habitable space and it should not be sold out/commercialized.
- [34] The project proponent shall provide fire control room and fire officer for building above 30 meter as per National Building Code.
- [35] The project proponent shall obtain permission of Mines and Geology Department for excavation of soil before the start of construction.
- [36] The project proponent shall seek specific prior approval from concerned local Authority/HUDA regarding provision of storm drainage and sewerage system including their integration with external services of HUDA/Local authorities beside other required services before taking up any construction activity.

- [37] The site for solid waste management plant be earmarked on the layout plan and the detailed project for setting up the solid waste management plant shall be submitted to the Authority within one month.
- [38] Vertical fenestration shall not exceed 40% of total wall area.
- [39] The project proponent shall discharge excess of treated waste water/storm water in the public drainage system and shall seek permission of HUDA before the start of construction.
- [40] The project proponent shall seek NOC from Town and Country department regarding height of the building allowed in the skyline of that area.
- [41] The project proponent shall ensure that structural stability to withstand earthquake of magnitude 8.5 on Richter scale.
- [42] The project proponent shall ensure that no construction activity is undertaken either on surface or below or above surface of revenue rasta passing through the project area.
- [43] The project proponent shall indicate the width and length of revenue rasta passing through the project area on sign board and shall display the same at both the ends of revenue rasta stretch, for awareness of public. Sign board shall also display the message that this is public rasta/road and any citizen can use it. There shall not be any gate with or without guards on revenue rasta further project proponent shall not encroach revenue rasta and shall not cross internal roads over revenue rasta.
- [44] The project proponent shall ensure that natural flow of existing nallah is never obstructed and shall seek NOC from Irrigation Department regarding this before the start of the construction.
- [45] The project proponent shall ensure that in case of excessive flow of water in, nallah, the structural integrity of buildings along-side the nallah is not breached in any circumstances.
- [46] The project proponent shall ensure that there should not be any water logging on the bed of nallah even in case of excessive rain.
- [47] The project proponent shall ensure that sewerage pipe line should not cross over the nallah and project proponent shall maintain separate STP in the plot area across the nallah.
- [48] The project proponent shall ensure that sewerage system and storm drainage system shall be planned by taking into account the natural slope of original land and approval from HUDA and Irrigation department shall be taken before the start of construction.

- [49] The project proponent shall ensure that bed of nallah is not encroached in any manner, while constructing the culvert over the nallah.
- [50] The project proponent shall ensure plinth level of the building block is 1.5 meter above 100 years flood level.
- [51] The project proponent shall provide pervious surface instead of impervious and hard surface in order to reduce overflow of water in nallah.
- [52] The project proponent shall ensure proper drainage in the project area as the project area is uneven and undiluted.

Operational Phase:

- [a] "Consent to Operate" shall be obtained from Haryana State Pollution Control Board under Air and Water Act and a copy shall be submitted to the SEIAA, Haryana.
- [b] The Sewage Treatment Plant (STP) shall be installed for the treatment of the sewage to the prescribed standards including odour and treated effluent will be recycled to achieve zero exit discharge. The installation of STP shall be certified by an independent expert and a report in this regard shall be submitted to the SEIAA, Haryana before the project is commissioned for operation. Tertiary treatment of waste water is mandatory. The project proponent shall remove not only Ortho-Phosphorus but total Phosphorus to the extent of less than 2mg/liter. Similarly total Nitrogen level shall be less than 2mg/liter in tertiary treated waste water. Discharge of treated sewage shall conform to the norms and standards of CPCB/ HSPCB, whichever is environmentally better. Project Proponent shall implement such STP technology which does not require filter backwash.
- [c] Separation of the grey and black water should be done by the use of dual plumbing line. Treatment of 100% grey water by decentralized treatment should be done ensuring that the re-circulated water should have BOD level less than 5 mg/litre and the recycled water will be used for flushing, gardening and DG set cooling etc.
- [d] For disinfection of the treated wastewater ultra-violet radiation or ozonization process should be used.
- [e] Diesel power generating sets proposed as source of back-up power for lifts, common area illumination and for domestic use should be of enclosed type and conform to rules made under the Environment (Protection) Act, 1986. The location of the DG sets shall be in the basement as promised by the project proponent with appropriate stack height above the highest roof level of the project, as per the CPCB norms. The diesel used for DG sets shall be ultra low sulphur diesel (35ppm sulphur), instead of low sulphur diesel.

- [f] Ambient Noise level should be controlled to ensure that it does not exceed the prescribed standards both within and at the boundary of the Proposed ITITES Project.
- [g] The project proponent as stated in the proposal shall maintain at least 35.15% as green cover area for tree plantation especially all around the periphery of the project and on the road sides preferably with local species which can provide protection against noise and suspended particulate matter. The open spaces inside the project shall be preferably landscaped and covered with vegetation/grass, herbs & shrubs. Only locally available plant species shall be used.
- [h] The project proponent shall strive to minimize water in irrigation of landscape by minimizing grass area, using native variety, xeriscaping and mulching, utilizing efficient irrigation system, scheduling irrigation only after checking evapo-transpiration data.
- [i] Rain water harvesting for roof run-off and surface run-off, as per plan submitted should be implemented. Before recharging the surface run off, pre-treatment through sedimentation tanks must be done to remove suspended matter, oil and grease. The bore well for rainwater recharging shall be kept at least 5 mts. above the highest ground water table. Care shall be taken that contaminated water do not enter any RWH pit. The project proponent shall avoid Rain Water Harvesting of first 10 minutes of rain fall. Roof top of the building shall be without any toxic material or paint which can contaminate rain water. Wire mesh and filters should be used wherever required.
- [j] The ground water level and its quality should be monitored regularly in consultation with Central Ground Water Authority.
- [k] A report on the energy conservation measures conforming to energy conservation norms finalized by Bureau of Energy Efficiency should be prepared incorporating details about building materials & technology, R & U Factors etc and submitted to the SEIAA, Haryana in three months time.
- [l] Energy conservation measures like installation of LED only for lighting the areas outside the building and inside the building should be integral part of the project design and should be in place before project commissioning. Use of solar panels must be adapted to the maximum energy conservation.
- [m] The Project Proponent shall use zero ozone depleting potential material in insulation, refrigeration, air-conditioning and adhesive. Project Proponent shall also provide halon free fire suppression system.
- [n] The solid waste generated should be properly collected and segregated as per the requirement of the MSW Rules, 2000 and as amended from time to time. The bio-degradable waste should be treated by appropriate technology at the site ear-marked

within the project area and dry/inert solid waste should be disposed off to the approved sites for land filling after recovering recyclable material.

- [o] The provision of the solar water heating system shall be as per norms specified by HAFEDA and shall be made operational in each building block.
- [p] The traffic plan and the parking plan proposed by the Project Proponent should be meticulously adhered to with further scope of additional parking for future requirement. There should be no traffic congestion near the entry and exit points from the roads adjoining the proposed project site. Parking should be fully internalized and no public space should be used.
- [q] The Project shall be operationalized only when HUDA/local authority will provide domestic water supply system in the area.
- [r] Operation and maintenance of STP, solid waste management and electrical infrastructure, pollution control measures shall be ensured even after the completion of project.
- [s] Different type of wastes should be disposed off as per provisions of municipal solid waste, biomedical waste, hazardous waste, e-waste, batteries & plastic rules made under Environment Protection Act, 1986. Particularly E-waste and Battery waste shall be disposed of as per existing E-waste Management Rules 2011 and Batteries Management Rules 2001. The project proponent shall maintain a collection center for E-waste and it shall be disposed of to only registered and authorized dismantler / recycler as per existing E-waste Management Rules 2011.
- [t] Standards for discharge of environmental pollutants as enshrined in various schedules of rule 3 of Environment Protection Rule 1986 shall be strictly complied with.
- [u] The project proponent shall make provision for guard pond and other provisions for safety against failure in the operation of wastewater treatment facilities. The project proponent shall also identify acceptable outfall for treated effluent.
- [v] The project proponent shall ensure that the stack height of DG sets is as per the CPCB guide lines and also ensure that the emission standards of noise and air are within the CPCB latest prescribed limits. Noise and Emission level of DG sets greater than 800 KVA shall be as per CPCB latest standards for high capacity DG sets.
- [w] All electric supply exceeding 100 amp, 3 phase shall maintain the power factor between 0.98 lag to 1 at the point of connection.
- [x] The project proponent shall minimize heat island effect through shading and reflective or pervious surface instead of hard surface.
- [y] The project proponent shall use only treated water instead of fresh water for HVAC and DG cooling. The Project Proponent shall also use evaporative cooling

technology and double stage cooling system for HVAC in order to reduce water consumption. Further temperature, relative humidity during summer and winter seasons should be kept at optimal level. Variable speed drive, best Co-efficient of Performance (CoP), as well as optimal Integrated Point Load Value and minimum outside fresh air supply may be resorted for conservation of power and water. Coil type cooling DG Sets shall be used for saving cooling water consumption for water cooled DG Sets.

- [z] The project proponent shall ensure that the transformer is constructed with high quality grain oriented, low loss silicon steel and virgin electrolyte grade copper. The project proponent shall obtain manufacturer's certificate also for that.
- [aa] Water supply shall be metered among different users and different utilities.
- [ab] The project proponent shall ensure that exit velocity from the stack should be sufficiently high. Stack shall be designed in such a way that there is no stack down-wash under any meteorological conditions.
- [ac] The project proponent shall provide water sprinkling system in the project area to suppress the dust in addition to the already suggested mitigation measures in the Air Environment Chapter of EMP.
- [ad] The project proponent shall ensure proper Air Ventilation and light system in the basements area for comfortable living of human being and shall ensure that number of Air Changes per hour/(ACH) in basement never falls below 15. In case of emergency capacity for increasing ACH to the extent of 30 must be provided by the project proponent.
- [ae] The project proponent shall get the inspection of nallah before the onset of monsoon season every year from Irrigation Department.
- [af] The project proponent shall not discharge untreated water in the nallah and also shall not throw any solid waste in the nallah.

PART-B. GENERAL CONDITIONS:

- [i] The Project Proponent shall ensure the commitments made in Formo-I; Formo-1A, EIA/EMP and other documents submitted to the SEIAA for the protection of environment and proposed environmental safeguards are complied with in letter and spirit. In case of contradiction between two or more documents on any point, the most environmentally friendly commitment on the point shall be taken as commitment by project proponent.
- [ii] The project proponent shall also submit six monthly reports on the status of compliance of the stipulated EC conditions including results of monitored data (both in hard copies as well as by e-mail) to the northern Regional Office of MoEF, the respective Zonal Office of CPCB, HSPCB and SEIAA Haryana.

- [iii] STP outlet after stabilization and stack emission shall be monitored monthly. Other environmental parameters and green belt shall be monitored on quarterly basis. After every 3 (three) months, the project proponent shall conduct environmental audit and shall take corrective measure, if required, without delay.
- [iv] The SEIAA, Haryana reserves the right to add additional safeguard measures subsequently, if found necessary. Environmental Clearance granted will be revoked if it is found that false information has been given for getting approval of this project. SEIAA reserves the right to revoke the clearance if conditions stipulated are not implemented to the satisfaction of SEIAA/MoEF.
- [v] The Project proponent shall not violate any judicial orders/pronouncements issued by any Court/Tribunal.
- [vi] All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department, Forest Conservation Act, 1980 and Wildlife (Protection) Act, 1972, Forest Act, 1927, PLPA 1900, etc. shall be obtained, as applicable by project proponents from the respective authorities prior to construction of the project.
- [vii] The Project proponent should inform the public that the project has been accorded Environment Clearance by the SEIAA and copies of the clearance letter are available with the Haryana State Pollution Control Board & SEIAA. This should be advertised within 7 days from the date of issue of the clearance letter at least in two local newspapers that are widely circulated in the region and the copy of the same should be forwarded to SEIAA Haryana. A copy of Environment Clearance conditions shall also be put on project proponent's web site for public awareness.
- [viii] Under the provisions of Environment (Protection) Act, 1986, legal action shall be initiated against the Project Proponent if it was found that construction of the project has been started before obtaining prior Environmental Clearance.
- [ix] Any appeal against the this Environmental Clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.
- [x] The project proponent shall put in place Corporate Environment Policy as mentioned in MoEF, GoI OM No. J-11013/41/2006-IA II (I) dated 26.4.2012 within 3 months period. Latest Corporate Environment Policy should be submitted to SEIAA within 3 months of issuance of this letter.
- [xi] The fund ear-marked for environment protection measures should be kept in separate account and should not be diverted for other purposes and year wise expenditure shall be reported to the SEIAA/RO MoEF, GoI under rules prescribed for Environment Audit.
- [xii] The project proponent shall ensure the compliance of Forest Department, Haryana Notification no. S.O.121/PA2/1900/S.4/97 dated 28.11.1997.

- [xiii] The Project Proponent shall ensure that no vehicle during construction/operation phase ~~enter~~ the project premises without valid 'Pollution Under Control' certificate from competent Authority.
- [xiv] The project proponent is responsible for compliance of all conditions in Environmental Clearance letter and project proponent can not absolve himself /herself of the responsibility by shifting it to any contractor engaged by project proponent.
- [xv] The project proponent shall seek fresh Environmental clearance if at any stage there is change in the planning of the proposed project.
- [xvi] The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely; PM_{2.5}, PM₁₀, SO_x, NO_x, Ozone, Lead, CO, Benzene, Ammonia, Benzopyrene, arsenic and Nickel. (Ambient levels as well as stack emissions) or critical sectoral parameters, indicated for the project shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.
- [xvii] The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the HSPCB Panchkula as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of the EC conditions and shall also be sent to the respective Regional Offices of MoEF by e-mail.
- [xviii] The project proponent shall conduct environment audit at every three months interval and thereafter corrective measures shall be taken without any delay. Details of environmental audit and corrective measures shall be submitted in the monitoring report.


 Member Secretary,
 State Level Environment Impact
 Assessment Authority, Haryana, Panchkula.

Endst. No. SEIAA/HR/2013

Dated: 

A copy of the above is forwarded to the following:

1. The Additional Director (IA Division), MOEF, G.O. CGO Complex, Lodhi Road, New Delhi.
2. The Regional office, Ministry of Environment & Forests, Govt. of India, Sector 31, Chandigarh.
3. The Chairman, Haryana State Pollution Control Board, Pkdt.


 Member Secretary,
 State Level Environment Impact
 Assessment Authority, Haryana, Panchkula.

State Environment Impact Assessment Authority, Haryana,
Bays No.55-58, Prayatan Bhawan, Sector-2 Panchkula.

Telephone No. 0172-2565232

Memo No: SEIAA/HR/2019/331

Date: 22.07.19

To

M/s ASF Insignia SEZ Pvt Ltd,
11, Bahadran, Bengali Market,
New Delhi- 110001

Subject:- Amendment in Environmental Clearance for expansion of (phase-II) IT/Information Technology Enable Services (SEZ) at village-Gwal Pahari in Sohna block, District Gurgaon Haryana.

Please refer to your application dated 01.03.2019 submitted for seeking amendment in EC granted for expansion of (phase-II) IT/Information Technology Enable Services (SEZ) at village-Gwal Pahari in Sohna block, District Gurgaon Haryana vide SEIAA/HR/2014/331 dated 21.02.2014.

Your application was considered by SEAC in its 178th meeting held on 11.04.2019 and recommended to SEIAA for amendment with a total built up area of 792209.65 sq. mtrs in EC letter no. SEIAA/HR/2014/331 dated 21.02.2014 (including already approved area of 489390 sq. mtrs + an area of 302819.65 sq. mtrs pertaining to basements).

Recommendations of SEAC was considered in 118th meeting of SEIAA held on 12.06.2019 and Authority decided to agree with the recommendation of SEAC and allow the amendment of Environment Clearance letter subject to compliance of the conditions already imposed in the Environment Clearance letter dated 21.02.2014.


Chairman, SEIAA
Haryana

STATE ENVIRONMENT IMPACT ASSESSMENT AUTHORITY HARYANA
 Bay No. 55-58, Prayatan Bhawan, Sector-2, PANCHKULA.

Tel: 0172-2565232

E-mail Id: seiaa.hry@gmail.com

No. SEIAA(125)/HR/2021/254

Dated: 04/03/2021

To

M/s ASF Insignia SEZ Pvt. Ltd,
 # 11, Babar lane, Bengali Market,
 New Delhi- 110001

Subject: Amendment in Environment Clearance for "ASF Insignia IT/ITES (SEZ)" project located at Village Gwal Pahari, Tehsil - Wazirabad, District Gurugram, Haryana.

[1] This letter is in reference to your application dated 09.07.2020 addressed to Member Secretary, SEIAA, Haryana received on 14.07.2020 and subsequent letter dated 30.08.2020 seeking prior Amendment in Environmental Clearance for the above project under the EIA Notification, 2006. The proposal has been appraised as per prescribed procedure in the light of provisions under the EIA Notification, 2006 on the basis of the mandatory documents enclosed with the application viz., Form-4 and additional clarifications furnished in response to the observations of the State Expert Appraisal Committee (SEAC) constituted by MoEF & CC, GoI vide their Notification dated 30.01.2019, in its meetings held on 30.08.2020.

[2] It is inter-alia, noted that the project involves "ASF Insignia IT/ITES (SEZ)" project located at Village Gwal Pahari, Tehsil-Wazirabad, District Gurugram, Haryana. The details of the project as given below:

Sr. No.	Particulars	Existing/ Phase I	Expansion/ Phase II	Total	Amended
Online Project Proposal Number		SIA/HR/MIS/162790/2020			
1.	Waste Water Generated (KLD)	482.12	467.3	949.42	1901.56 (80% of fresh water + 100 % of Flushing + Blow Down of Cooling Tower of HVAC + Filter Backwash Water)
2.	STP Capacity (KLD)	1050 (3 X 350)			2300

[3] The State Expert Appraisal Committee, Haryana after due consideration of the relevant documents submitted by the project proponent and additional clarification furnished in response to its observations, have recommended the grant of amendment in environmental clearance for the project mentioned above, subject to no pollution load shall be increased due to

the amendment. Accordingly, the State Environment Impact Assessment Authority in its 125th meeting held on 07.10.2020 decided to agree with the recommendations of SEAC to accord necessary amendment in earlier Environmental Clearance for the project under Category 8(a) of EIA Notification 2006 with strict compliance of the stipulations imposed in earlier granted Environment Clearance vide letter No. SELAA/HR/2014/331 dated 21.02.2014 & amendment thereto vide letter no. SELAA/HR/2019/201 dated 22.07.2019 along-with the following additional stipulations:-

1. No pollution load shall be increased due to the amendment.
2. "Zero Liquid Discharge" would be achieved and will install all the necessary equipment to treat the residual water".




Chairman,
State Level Environment Impact
Assessment Authority, Haryana, Panchkula.

Enclst. No. SELAA(125)/HR/2021/

Dated: ___/03/2021

A copy of the above is forwarded to the following:

1. Director (IA Division), MoEF & CC, GoI, Indra Paryavaran Bhavan, Zor bhag Road- New Delhi-110003.
2. Regional office, Ministry of Environment, Forests & Climate Change, Govt. of India, Bay's no. 24-25, Sector 31-A, Dakshin Marg, Chandigarh-160013.
3. Chairman, Haryana State Pollution Control Board, C-11, Sector-6, Panchkula.
4. Director General, Town & Country Planning Haryana, Plot No. 3, Sector - 18A, Madhya Marg, Chandigarh- 160018.
5. Concerned File/ Office Copy



Chairman,
State Level Environment Impact
Assessment Authority, Haryana, Panchkula.

State Environment Impact Assessment Authority, Haryana,
Bays No.55-58, Prayatan Bhawan, Sector-2 Panchkula.

Telephone No. 0172-2565232
E-mail ID: sciaa_hy@gmail.com

Memo No: SEIAA/HR/2021/465

Date: 11/05/2021

To

M/s ASF Insignia SEZ Private Limited,
11, Babar Lane, Bengali Market,
New Delhi-110001

Subject: Extension of validity of Environment Clearance for "ASF Insignia IT/ITES (SEZ)" project located at Village Gwali Pahari, Tehsil-Wazirabad, District Gurugram, Haryana.



With reference to your application No. Nil dated 18.03.2021 received in this office on 26.03.2021 for seeking Extension of Validity of Environment Clearance granted for "ASF Insignia IT/ITES (SEZ)" project located at Village Gwali Pahari, Tehsil-Wazirabad, District Gurugram, Haryana vide letter dated 21.02.2014. The Validity of your Environment Clearance was up to 20.02.2021 as per MoEF & CC, GoI dated 14.09.2006 & its subsequent Amendment dated 29.04.2015 & 14.09.2016 whereas, due to COVID-19 pandemic the validity of EC was automatically extended for six month from the date of expiry of validity i.e. 20.08.2021 vide MOEF & CC, GOI Notification No. S.O.4254 (E) dated 27.11.2020.

The case was examined in the light of MoEF & CC, GoI Amended Notification dated 14.09.2016 & its subsequent amendment Notification dated 27.11.2020.

Keeping in view of above, the Authority decided to grant Extension for Validity of Environment Clearance for further 3 years from the date of expiry of validity of earlier EC subject to compliance of the conditions already imposed in the Environmental Clearance letter dated 21.02.2014 granted by SEIAA, Haryana.

(Signature),
SEIAA, Haryana.

Medical Room

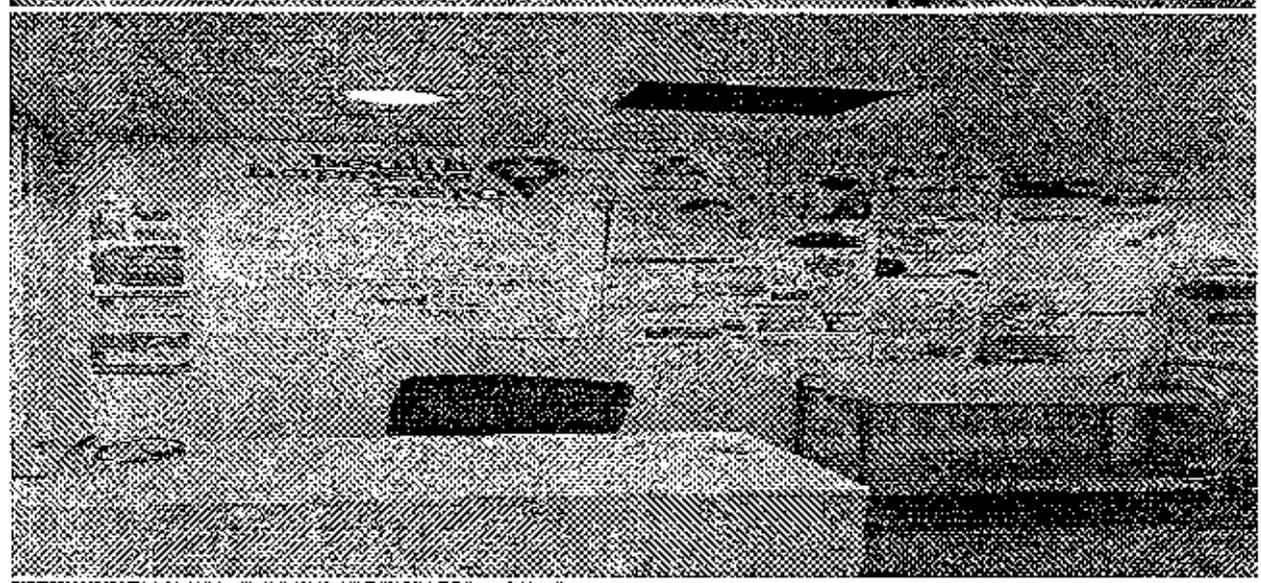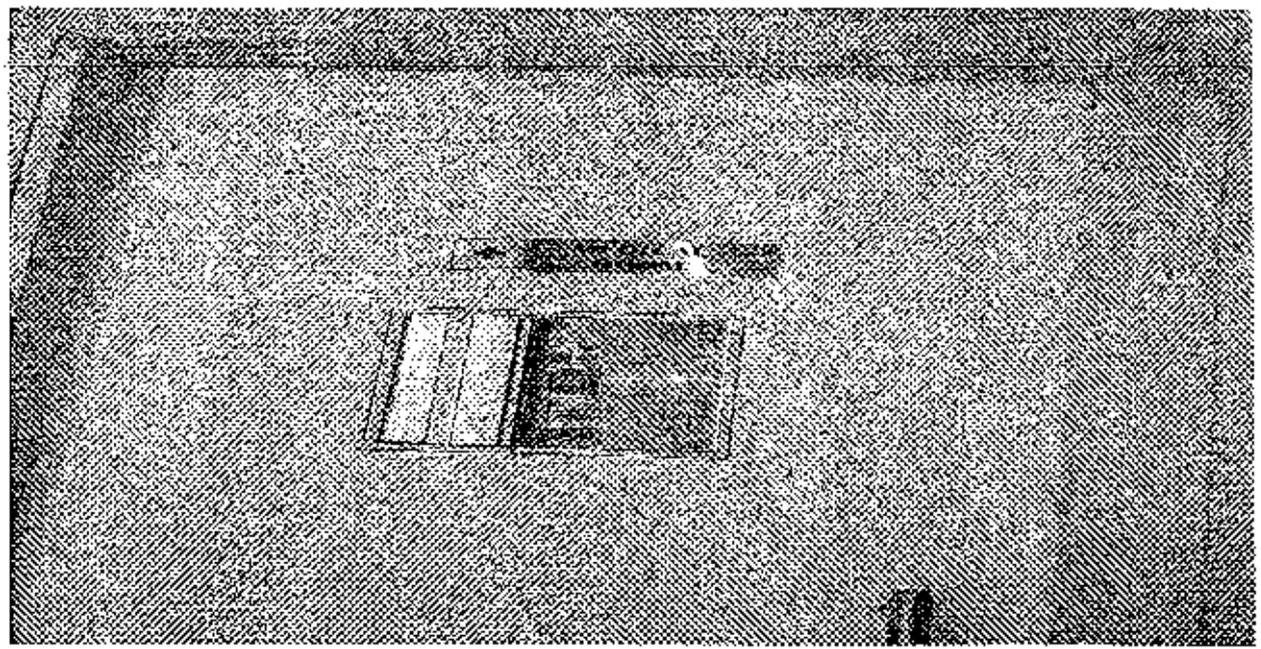



ole

14 April 2021

To,

The Regional Officer,
Haryana State Pollution Control Board
Gurgaon

Sub.: Submission of Form - IV for the period 01.04.2020 to 31.03.2021 -
Annual Return.

Dear Sir,

We are enclosing herewith Form - IV for the period from 01.04.2020 to 31.03.2021 i.e. Annual Return for Hazardous Wastes for the financial year 2020 to 2021 for our site at Village Gwal Pahari, Tehsil Wazirabad Distt. Gurgaon (Haryana).

Thanking you,
Yours faithfully,


For ASF INSIGNIA SEZ PVT. LTD.



Authorized Signatory

Encl: AS Above

CC: The Chairman
Haryana State Pollution Control Board,
C-11, Sector-6, Panchkula

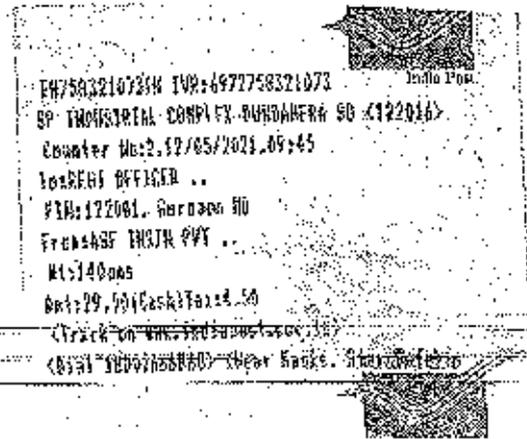

EN75032107204 INR:4977758321073
SP INDUSTRIAL COMPLEX BUNDAPURA SO (122016)
Counter No:2,12/05/2021.09:45
POSTAGE OFFICER ..
PIN:122001, Gurgaon Haryana
Fresh ASF INSIGNIA PVT ..
Rs:140000
Date:29,09/2021
Track on www.indpost.gov.in
(833) 1007058800 Near Kanki, Sector 6, Panchkula

EN75032105410 INR:4977758321056
SP INDUSTRIAL COMPLEX BUNDAPURA SO (122016)
Counter No:2,12/05/2021.09:40
POSTAGE OFFICER ..
PIN:122001, Panchkula Sector 6 S.O
Fresh ASF INSIGNIA PVT ..
Rs:140000
Date:27,09/2021

ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office : ASF Insignia SEZ (T/ITes), Vatsal Valley (Gwal Pahari), off Gurugram-Faridabad Road, Gurugram-122008, Haryana
t: +91 124 4777200 f: +91 124 4234110 e: corporate@asfinfrastructure.com w: www.sezinfrastructure.com
Regd. Office : 11, Babar Lane, Bengali Market, New Delhi-110001 t: +91 11 23835511 f: +91 11 23739299
Corp. Office : ASF Centre, 362-363, Udyog Vihar, Phase-IV, Gurugram-122016 (India)

CIN U45201DL2005PTC140408

Creating Intelligent Spaces


FORM 4

[See rules 5(6) and 22 (2)]

**FORM FOR FILING ANNUAL RETURNS
BY THE OCCUPIER OR OPERATOR OF FACILITY
For the period from 1st April, 2020 to 31st March, 2021**

[To be submitted by occupier/operator of disposal facility to State Pollution Control Board/
Pollution Control Committee by 30th June of every year for the preceding period April to March]

1.	Name and address of the generator/ operator of facility	: ASF Insignia SEZ Private Limited Village Gwal Pahari, Sub-Tehsil Wazirabad Distt. Gurgaon, Haryana			
2.	Name of the authorized person and full address with telephone and fax number	: Shri Anil Mendiratta ASF Center Plot No. 362-363, Gate No 4 , Udyog Vihar, Phase-IV, Gurgaon, Haryana Tel. No.: 0124-4777205 Fax No.: 0124-4234110			
3.	Description of hazardous waste	: Physical form with description		: Chemical form	
		: Used Lube Oil generated from Generator Sets			
4.	Quantity of hazardous (in MTA)	: Type of hazardous waste		: Quantity (in Tonnes/KL)	
		: Used Oil (Haz. Waste Category: 5.1)		: 6.160	
5.	Description of Storage	: Stored in closed labeled PVC drums in designated area with concrete flooring			
6.	Description of Treatment	: None			
7.	Details of transportation	Name & address of consignee	Mode of packing	Mode of transportation	Date of transportation
		M/s. Shiv Shakti Oil & Lubricants F-557; RIICO Ind. Area Chopanki, Post Tapukara, Tehsil- Tizara, Distt- Ajwar-301017, Rajasthan	Closed Drums	RJ40GA2066	26.05.2020
		M/s. Shiv Shakti Oil & Lubricants F-557; RIICO Ind. Area Chopanki, Post Tapukara, Tehsil- Tizara, Distt- Ajwar-	Closed Drums	RJ40GA1658 RJ40GA1420	25.01.2021 25.01.2021



		301017, Rajasthan			
8	Details of disposal of hazardous waste	Name & address of consignee	Mode of packing	Mode of transportation	Date of transportation
		Given to approved vendor/recycler (M/s. Shiv Shakti Oil & Lubricants)			
9.	Quantity of useful materials sent back to the manufacturers* and others#	Name and type of Manufacturers*	Quantity in Tonnes/KL material sent back to		
		Others# (Used Oil)	Nil	6.160 KL (M/s Shiv Shakti Oil & Lubricants)	

* delete whichever is not applicable# enclose list of other agencies

Signature  Executive Director

Date : 12th April 2021
Place : Gurgaon, Haryana



OK

Date: 01.06.2020

The Regional Office
Haryana State Pollution Control Board
Gurgaon, Haryana

Sub.: Disposal of Hazardous Waste M/S Shiv Shakti Oil Lubricants - F 557; RIICO Ind,
Area Chopanki P.O. Tapukara, Tehsil Tizara, Distt. Alwar (Rajasthan) PIN.
301017

Dear Sir,

We have sent 2860 liters Of used lube oil (Hazardous Liquid Waste) to M/S Shiv Shakti
Oil Lubricants - F 557; RIICO Ind, Area Chopanki P.O. Tapukara, Tehsil Tizara, Distt. Alwar
(Rajasthan) PIN. 301017 and enclosing herewith copies of the following relevant
documents for your records:-

- 1) Invoice No. AF 1020500001 Dated. 26.05.2020
- 2) Outward Gate Pass No. 001 Dated. 26.05.2020
- 3) Bill of Entry No. 2000009 Dated. 03.03.2020
- 4) Form-10 [See Rule 19 (1)]
- 5) Registration certificate-cum-Pass Book

Thanking you,


Yours faithfully,

For ASF INSIGNIA SEZ PVT. LTD.



AUTHORISED SIGNATORY

Encl. As above



ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office : ASF Insignia SEZ (IT/ITES), Village Gwalpohari, off Gurgaon-Faridabad Road, Gurugram-122003, Haryana

t: +91 124 4777200 f: +91 124 4284110 e: corporate@asfinfrastructure.com w: www.asfinfrastructure.com

Regd. Office : 11, Bahar Lane, Bangsli Market, New Delhi-110001 t: +91 11 23855511 f: +91 11 26733208

Corp. Office : ASF Centre, 362-363, Udyog Vihar, Phase-IV, Gurugram-122010 (India)

CIN : U45201DL2005PTC140400

Creating Intelligent Spaces[®]

GOODS/MATERIAL GATE PASS



ASF INSIGNIA SEZ PRIVATE LIMITED

VILL. GWAL PAHARI, SUB TEHSIL WAZIRABAD, DISTT. GURUGRAM-122003 (HR.)

GST No. : 06AAGCC7148L1ZG

GATE PASS NO. : 001

DATE 26/05/2020 H/c ASF Gwal Pahari

TIME

TO

M/s. Shiv Shakti Oil & Lubricants,
F-557, RDC Ind.
Alwar, Rajasthan

RETURNABLE	<input type="checkbox"/>
NON RETURNABLE	<input checked="" type="checkbox"/>

MODE OF TRANSPORT

VEHICLE NO.	RJ406 A/2066
-------------	--------------

SL. No.	DESCRIPTION OF GOODS/MATERIAL	UNIT	QTY	REMARKS
1	Used lubricating oil with drum 13 Drum x 220 Ltr	Ltr	2860	
	BOEN No 2000009, 03/03/20			
	Thermax AF102050000, dt. 26/05/2020			
	2000003 3912049757/2 dt. 26/05/2020			
		Ltr	2860	

PREPARED BY (SIGN & NAME)
[Signature]

AUTHORISED SIGNATORY
[Signature]

Consignee: M/s ASF Insignia SEZ Pvt. Ltd. Village Gwal Pahar, Tehsil Sohna District Gurgaon (Haryana) GSTIN # 08AACCG7148L1ZG	Invoice No. AF1020500001 Dated 26.06.2020
	Order No. 91600124 Date
Delivery: At SEZ Site Payment: Advance	

Buyer/Consignee: M/s SHIV SHAKTI OIL & LUBRICANTS F-557; RICO Ind. Area Chopanki Post Tapuktra, Tilzara Distt Alwar, Rajasthan- 301017. GST No.: 08ABFFS4464G1ZZ PAN No. ABFFS4464G	Buyer (if other than consignee) Same as consignee
---	--

Marka/Nos./Kind of packages	Description of goods	Quantity (Ltrs)	Rate Rs.	Amount Rs.
13 Drums (220 Ltrs each)	Used Lubricating Oil (Waste Oil with drum) H.S. Code: 27109900	2860.00	19.72	68402.08
N. Wt: 2860 ltrs G. Wt: 2860 Ltrs	ASF Insignia SEZ Pvt. Ltd INWARD/OUT WARD ENTRY Sl No. Time In. Time Out. Date: 26/06/2020 Sign. (Security)	2860		56402.08
	BOD 5.00%	2820.10	50/17-147	
	SWS 10.00%	202.01		
		0.00		
	Customs Duty	3102.11		
	IGST 18.00%	10710.75	III-93	
	Add: TOTAL Duty	13812.86		13,812.86
	Value including Duty / Tax			70214.92
				70214.92

Net Invoice Value

Total: Rupees Seventy Thousand Two Hundred Fourteen & Ninety two paisa Only.

We certify that the above particulars are true & correct.
 We further declare that the goods are dispatched / to be
 dispatched to a bonafied user.

For ASF Insignia SEZ Pvt. Ltd.
 For ASF INSIGNIA SEZ Pvt. Ltd.

 Authorised Signatory



E-WAY BILL SYSTEM



e-Way Bill



E-Way Bill No: 3912 0497 5712
 E-Way Bill Date: 26/05/2020 02:01 PM
 Generated By: 06AAC007148L1ZG - ASF INSIGNIA SEZ PVT LTD
 Valid From: 26/05/2020 02:01 PM [42Kms]
 Valid Until: 27/05/2020

Part - A

GSTIN of Supplier: 06AAC007148L1ZG, ASF INSIGNIA SEZ PVT LTD
 Place of Dispatch: HARYANA-122001
 GSTIN of Recipient: 08ABF84404G1ZZ, SHIV SHAKTI OIL & LUBRICANTS
 Place of Delivery: CHOPANKI, BHIWADI, RAJASTHAN-301018
 Document No.: AP1020500001
 Document Date: 26/05/2020
 Transaction Type: Regular
 Value of Goods: ₹ 76214.92
 HSN Code: 27109900 - USED LUBRICATING OIL
 Reason for Transportation: Outward - Supply
 Transporter: 08ABF84404G1ZZ & SHIV SHAKTI OIL LUBRICANTS

Part - B

Mode of Transport	Vehicle No.	Project	Entered Date	Entered By	CCWB No.	MGID
Doc No & Dt.						
Road	RJADGA2068		26-05-2020 02:01 PM	06AAC007148L1ZG	-	-



361204975712

STATEMENT OF ENTRY FOR HOME CONSUMPTION (SEE TO DETERMINE)

APPLICANT: **AGP INVESTMENT SEC PVT LTD (INVEST)**
 ACCOUNT NO: **33083208**
 DATE: **20/03/2023**
 TYPE: **SELF**
 ACCOUNT TYPE: **SAVINGS**
 ACCOUNT NO: **33083208**
 DATE: **20/03/2023**
 TYPE: **SELF**

DATE	DESCRIPTION	AMOUNT	CURRENCY	ACCOUNT	STATEMENT NO	STATEMENT DATE	STATEMENT PERIOD	STATEMENT TYPE	STATEMENT DATES	STATEMENT TYPE	STATEMENT DATES	STATEMENT TYPE	STATEMENT DATES
20/03/2023	AGP INVESTMENT SEC PVT LTD (INVEST)	1000000.00	USD	AGP INVESTMENT SEC PVT LTD (INVEST)	33083208	20/03/2023	20/03/2023	SELF	AGP INVESTMENT SEC PVT LTD (INVEST)	33083208	20/03/2023	20/03/2023	SELF

AGP INVESTMENT SEC PVT LTD (INVEST) - FOURTEEN THOUSAND TWO HUNDRED AND THIRTY NEW CITY

DATE	DESCRIPTION	AMOUNT	CURRENCY	ACCOUNT	STATEMENT NO	STATEMENT DATE	STATEMENT PERIOD	STATEMENT TYPE	STATEMENT DATES	STATEMENT TYPE	STATEMENT DATES	STATEMENT TYPE	STATEMENT DATES
20/03/2023	AGP INVESTMENT SEC PVT LTD (INVEST)	1000000.00	USD	AGP INVESTMENT SEC PVT LTD (INVEST)	33083208	20/03/2023	20/03/2023	SELF	AGP INVESTMENT SEC PVT LTD (INVEST)	33083208	20/03/2023	20/03/2023	SELF

AGP INVESTMENT SEC PVT LTD (INVEST) - FOURTEEN THOUSAND TWO HUNDRED AND THIRTY NEW CITY

Performa Invoice

Supplier/Exported/Consignor M/s ASF Insignia SEZ Pvt. Ltd. Village Gwal Pahari, Tehs./ Sohna District Gurgaon (Haryana) GSTIN # 06AACCC7148L1ZG	Invoice No./Date PI/AISPL/SEZ/DYA/09/19-20 Dated 19.02.2020
Buyer/Consignee M/s SHIV SHAKTI OIL & LUBRICANTS P-557; RICO Ind. Area Chopanki Post Tapukara, Tizara Distt Alwar, Rajasthan- 301017. GST No.: 08ABFFS4464G1ZZ PAN No. ABFFS4464G	Order No _____ Date _____ Delivery: At SEZ Site Payment: Advance Buyer: (if other than consignee) Same as consignee

Marks/Nos./Kind of packages	Description of goods	Quantity (Ltrs)	Rate Re.	Amount Rs.
13 Drums (220 Ltrs each)	Used Lubricating Oil (Waste Oil with drum) <u>H.S. Code: 27109900</u>	2860.00	19.72	56402.00
N. wt: 2860 Ltrs G. wt: 2860 Ltrs	TOTAL	2860		56402.00
	BCD 5.00%	2820.10	6017-147	
	SWS 10.00%	282.01		
		0.00		
	Customs Duty	3102.41		
	IGST 18.00%	10710.75	11-35	
	Add: TOTAL Duty	13812.86		13812.86
	Value including Duty / Tax			70214.92

Net Invoice Value	R/o	<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td style="text-align: right;">1.92</td> </tr> <tr> <td style="text-align: right;">70213.00</td> </tr> </table>	1.92	70213.00
1.92				
70213.00				
Total: Rupees Seventy Thousand Two Hundred Thirteen Only.				
We certify that the above particulars are true & correct. We further declare that the goods are dispatched / to be dispatched to a benefited user.	For ASF Insignia SEZ Pvt. Ltd. Authorised Signatory			

FORM 10

[See Rule 19 (1)]

MANIFEST FOR HAZARDOUS AND OTHER WASTE

1.	Sender's name and mailing address (including Phone no. and e-mail)	ASF Insignia SEZ Pvt. Ltd Gurgaon- Faridabad Road, Vill- Gwal Pahari, Teh-Bohna District Gurgaon (Haryana)
2.	Sender's Authorisation No.	
3.	Manifest Documents No.	SSOL / HW / 01 / 2019 / ASF / Dt. 26.05.20
4.	Transporter's name and address: (including Phone No. and e-mail)	
5.	Type of vehicle	(Truck/Tankers/Special Vehicle)
6.	Transporter's registration No.	
7.	Vehicle registration No.	RJ-40 GA - 2066
8.	Receiver's name and mailing address (including Phone No. and e-mail)	SHIV SHAKTI OIL & LUBRICANTS F-657 & F-699 (Unit 3), RICO Industrial Area Chopanki, Post: Tapukara Teh. Tijara, Distt. Alwar - 301707 (Rajasthan) INDIA Ph.: +91-9819093339, 9950003399 E: shivshakti_hub07@yahoo.co.in
9.	Receiver's Authorisation No.	RSPCB / HWM / 2018-2019 / HSW / HSW / 21 RSPCB / HWM / 2018-2019 / HSW / HSW / 106 (Unit 3)
10.	Waste description	Used Lube Oil, Used Cutting Oils, Used Hydraulic Oil, Used Transformer Oil, Waste of Recycled Containers/ Barrels/ Drums Contaminated with Hazardous Chemicals, Waste Hazardous Waste (Cat. 5.1) ✓ (Cat. 6.2) X (Cat. 33.1) (Unit-3) ✓
11.	Total quantity No. of Containers	2850 Cr. m ³ or MT 07 empty drums Nos.
12.	Physical form	(Solid/Semi-Solid/Sludge) OILY / Tany / Slurry / Liquid
13.	Special handling instructions and additional information: (Handle with Care)	Disposed/ sale as per Precautions/ Rules of Central Pollution Control Board/ MOEF/ SPCB to the Authorized Reg. Re-recycler/ Re-processor.
14.	Sender's Certificate	I hereby declare that the contents of the consignment are fully and accurately described above by proper shipping name and are categorised, packed, marked, and labelled and are in all respects in proper condition for transport by road according to applicable national government regulations.
		Month Day Year 05 26 2020
	Name & stamp: Signature	
15.	Transporter acknowledgement of receipt of Wastes	
		Month Day Year 05 26 2020
	Name & stamp: Signature	
15.	Receiver's certification for receipt of hazardous and other waste	
		Month Day Year 05 26 2020
	Name & stamp: Signature	

COPY 1 of 7

White Copy To be forwarded by the sender to the State Pollution Control Board

IL-101 Pass-Book

Authorisation Cum-Passbook for Re-refining/Recycling of Hazardous Waste



राजस्थान राज्य प्रदूषण नियंत्रण बोर्ड
RAJASTHANI STATE POLLUTION CONTROL BOARD
Udipi Road, Area, Chhatrapati Sagar, Jaipur
दूषण नियंत्रण बोर्ड, राजस्थान

IInd Pass-book

Authorisation Cum-Passbook for Re-refining/Recycling of Hazardous Waste

1.1

Name and Address of the Industry : M/s Shiv Shakti oil & Lubricants
F-557, RIA Chopanki, Bhimadi,
Tehsil - Tijara, Alwar

Telephone/Fax No. : 09212601330

E-Mail Address : shivshakti_lub_07@yahoo.co.in

Authorisation No. : F(HSW)/Alwar (Tijara)/1245(U)/2014-15/535-537/25/04/2010


Date of issue : 04/02/2020

Validity period : 04/02/2020 To 31/03/2023

Type & quantity of the Hazardous Waste (S) permitted for procurement and recycling.

S. No.	Hazardous Waste (Used/Waste Oil) Type	Quantity (Kilolitres/Metric ton per annum)
1.	<u>Used or spent oil</u>	<u>2000 KLA</u> <u>(Two Thousand Kilo liter per Annum)</u>




 Authorized Signatory & Seal


**Endorsement by the Auctioneer/Seller (except column no. 6 & 7)
(Condition No.3 of the Authorisation)**

Authorisation No. : _____ Date : _____

Waste(s) Type : _____ Permitted Quantity : _____

S. No.	Date	Address of the Auctioneer/Seller	Type & Quantity of HW sold /Auctioned	Signature & Seal of the Auctioneer/Seller with date	Date of arrival in Recyclers premises & Chellan No.	Balance Quantity (Registered - procured till date)
(1)	(2)	(3)	(4)	(5)	(6)	(7)
04	26/05/2020	ASEE Dindur SEZ PLS Grand Park Gurgaon	2860kg			

to be filled by the Recycler

ASF
INSIGNIA

o/c

Date: 28.01.2021

The Regional Office
Haryana State Pollution Control Board
Gurgaon, Haryana

Sub.: Disposal of Hazardous Waste M/S Shiv Shakti Oil Lubricants - F 557; RIICO Ind,
Area Chopanki P.O. Tapukara, Tehsil Tizara, Distt. Alwar (Rajasthan) PIN. 301017

Dear Sir,

We have sent 2640 + 660 liters Total 3300 liters Of used lube oil (Hazardous Liquid Waste) to M/S Shiv Shakti Oil Lubricants - F 557; RIICO Ind, Area Chopanki P.O. Tapukara, Tehsil Tizara, Distt. Alwar (Rajasthan) PIN. 301017 and enclosing herewith copies of the following relevant documents for your records:-

- 1) Invoice No. AF 1020500015 & AF 1020500016 Dated. 25.01.2021
- 2) Outward Gate Pass No. C40 & 041 Dated. 25.01.2021
- 3) Bill of Entry No. 2000039 Dated. 28.11.2020
- 4) Form-10 [See Rule 19 (1)]
- 5) E-way bill No. 8712 7996 7962 Dated. 25.01.2021 04:18 PM
- 6) Registration certificate-cum-Pass Book

Thanking you,
Yours faithfully,

For ASF INSIGNIA SEZ PVT. LTD.



AUTHORISED SIGNATORY

Encl. As above

Stamp of the Haryana State Pollution Control Board, Gurgaon, Haryana, dated 28.01.2021. The stamp includes the text: 'HARYANA STATE POLLUTION CONTROL BOARD', 'GURGAON, HARYANA', and '28.01.2021'. There is also a handwritten signature over the stamp.

ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office: ASF Insignia SEZ (IT/Ties), Vasant Vohay (Eva) Phase, off Gurugram-Faridabad Road, Gurugram-122002, Haryana
t: +91 124 4777800 f: +91 124 4284110 e: corporate@asfinfrastructure.com or www.asfinfrastructure.com
Reg. Office: 11, Babar Lane, Bengali Market, New Delhi-110001 t: +91 11 22955511 f: +91 1128728232
Corp. Office: ASF Centre, 362-368, Udyog Vihar, Phase-W, Gurugram-122016 (India)
CIN U45201DI2005PTC140408

Creating Intelligent Spaces[®]

GOODS/MATERIAL GATE PASS



ASF INSIGNIA SEZ PRIVATE LIMITED

VILL. GYAL FAHARI, SUB TENSIL WAZIRABAD, DISTT. GURUGRAM-122003 (HR.)

GST No. : 06AACCC7148L1ZG

GATE PASS NO. : 040

DATE : 25/01/2021 *A/c Facility*

TIME

TO

Ms. Shiv Station Oil & Lubricants
East; RPLCO Ind. Area,
Tilana, Okhla, Rajasthan

RETURNABLE	<input type="checkbox"/>
NON RETURNABLE	<input checked="" type="checkbox"/>

MODE OF TRANSPORT

VEHICLE NO.	RJ406A/14528
-------------	--------------

SL. No.	DESCRIPTION OF GOODS/MATERIAL	UNIT	QTY	REMARKS
01	Disposal of used oil 12 Drum	Ltr	2640	
	12-Drum X 220 Ltr = 2640 Ltr			
	BD No - 2000039 dt. 28/11/2020			
	Inv. No - AF/02050015, 25/01/21			
	Rs. 64810.19/-			
	Log # 371279967962, 25/01/2021			
		Ltr	2640	

PREPARED BY *[Signature]*

AUTHORISED SIGNATORY *[Signature]*

GOODS/MATERIAL GATE PASS



ASF INSIGNIA SEZ PRIVATE LIMITED

VILL. GWAL PARALI, SUB TEHSIL WAZIRABAD, DISTT. GURUGRAM-122003 (HR.)

GST No. : 06AACC07148L1ZG

GATE PASS NO. : 041

DATE

25/01/2021

Atc Facility

TIME

TO


Mr. Shiv Shakti Singh & Associates
 1st Floor, K.P. Dada Road, Durg
 Chopara, Ghazipur, Bihar, India


RETURNABLE	<input type="checkbox"/>
NON RETURNABLE	<input checked="" type="checkbox"/>

MODE OF TRANSPORT

VEHICLE NO.	RT406A/142
-------------	------------

Sl. No.	DESCRIPTION OF GOODS/MATERIAL	UNIT	QTY	REMARKS
01	Used oil with Drum	Ltr	660	/
	03 Drums x 220 Ltr			
	= 660 Ltr			
	BOEING 32005039 dt. 28/11/2020			
	Inv No = AF102 05/01/2021			
	Rs. 16202.63/-			
		Ltr	660	

PREPARED BY (SIGN & NAME)


AUTHORISED SIGNATORY


Tax Invoice

Supplier Company ASF INSIGNIA SEZ PRIVATE LIMITED ASF INSIGNIA SEZ IT&S, Village GwalPahar, Gurgaon Faridabad Road District - SubTeh Wazirabad, Gurgaon PinCode - 122003 GSTIN - 06AACC07148L1ZG Place of Supply, Haryana Name of State (State Code): Haryana(07)				Invoice No: ASF1020500015 SAP Document Number: 81390244 Date of Issue: 25.01.2021 Vehicle No: RJ40GA-1658			
Recipient: SHIV SHAKTI OIL & LUBRICANTS F-657, RIICO Ind. Area Chopanki, post Tapokara, Tizara Alwar 301017 GSTIN - 06ABFFS4484G1ZZ Whether TAX is Payable on Reverse Charge - No				Order No. Date Permission No. 91600132 Dated 18.11.2020 Delivery: 91700275 Buyer (if other than consignee) Same As Consignee			
Mark/Nos / Kind of packages	Description of goods	HSN / SAC	Quantity	UOM	Rate Rs.	Amount Rs.	
1	Disposal of Used Oil with Drum	27109900	2,640.000	L	19.72	52,060.80	
N. Wt:	0.000 KG						
G. Wt:	0.000 KG						
TOTAL			2,640.000			52,060.80	
	BCD			5.00 %		2,603.04	
	SWS			10.00 %		260.30	
	CGST						
	SGST						
	IGST			18.00 %		9,886.35	
	Net Invoice Value					64,810.49	
Total: RUPEES SIXTY FOUR THOUSAND EIGHT HUNDRED TEN Rupees FORTY NINE Paise ONLY.							
We certify that the above particulars are true & correct. ASF Insignia SEZ Pvt. Ltd INWARD/OUTWARD ENTRY SI No. 38				For ASF INSIGNIA SEZ PVT LTD For ASF INSIGNIA SEZ PVT LTD Signature / DSC Auth. Signatory			

Time In:
 Time Out: 12:40
 Date: 25/01/21
 Sign. (Security):

Tax Invoice

Supplier
Company
ASF INSIGNIA SEZ PRIVATE LIMITED
ASF INSIGNIA SEZ (TeS, Miliago GwaiPahanGurgaon
 Faridabad Road
 District - SubTeh Wazirabad, Gurgaon
 Pin Code - 122003
 GSTIN - 06AAGG07148L1Z0
 Place of Supply: Haryana
 Name of State (State Code): Haryana(07)

Invoice No. AP102960018
 SAP Document Number: 91502245
 Date of Issue: 23.01.2021
 Vehicle No: RJ40GA-1420

Order No. _____ Date _____
 Permission No. 91600132 Dated 18.11.2020
 Delivery: 91700276

Recipient: SHIV SHAKTI OIL & LUBRICANTS F-557, RFOO Ind.
 Area Chapanki, post Tapokari, Tizara Abwar
 301017
 GSTIN - 06ABFF84484B1Z2

Buyer (if other than consignee)
 Same As Consignee

Whether TAX is Payable on Reverse Charge - No

Mark/Nos./Kind of packages	Description of goods	HSN / SAC	Quantity	UOM	Rate Rs.	Amount Rs.
1	Disposal of Used Oil with Drum	27109000	660.000	L.	19.72	13,015.20
R wt:	0.000 Kgs					
G. wt:	0.000 KG					
TOTAL			660.000			13,015.20
				5.00 %		650.76
				10.00 %		65.08
				18.00 %		2,471.69
						16,202.63
	Net Invoice Value					

Total: RUPEES SIXTEEN THOUSAND TWO HUNDRED TWO Rupees SIXTY THREE Paise ONLY.

We certify that the above particulars are true & correct.

ASF Insignia SEZ Pvt Ltd
INWARD/OUTWARD ENTRY


SI No. 26
 Time In 13:30
 Time Out 13:30
 Date 23/01/21
 Sign. (Secretary) _____

For ASF INSIGNIA SEZ PRIVATE LTD
 For ASF INSIGNIA SEZ PRIVATE LTD

Signature / DSO Secretary



E - WAY BILL SYSTEM



e-Way Bill



E-Way Bill No. 3712 7998 7962

E-Way Bill Date: 26/01/2021 04:15 PM

Generated By: 06AAC00714 RL12G - ASF KSRINIA SEZ PVT LTD

Valid From: 26/01/2021 04:18 PM [42Kms]

Valid Until: 26/01/2021

Part - A

GSTIN of Supplier: 06AAC00714RL12G,ASF KSRINIA SEZ PVT LTD

Place of Dispatch: HARYANA-122001

GSTIN of Recipient: 08AHPF84464GZZ & SHIV SHAKTI OIL & LUBRICANTS

Place of Delivery: CHOPANKI, BHUWAI, RAJASTHAN-301018

Document No: 6F102050015

Document Date: 26/01/2021

Transaction Type: Regular

Value of Goods: 14810.00

HSN Code: 27109000 - USED OIL WITH DRUM

Reason for Transportation: Outward - Supply

Transporter: 08AHPF84464GZZ & SHIV SHAKTI OIL LUBRICANTS

Part - B

Mode	Vehicle Type Doc No & IS	From	Expiry Date	Enter-By	Capacity (Tonnage)	Multi-Vehicle ID (MVI)
Truck	RH-0361858	06/01/2021 04:18 PM	26/01/2021 04:18 PM	06/01/2021 04:18 PM		



FORM 10

[See Rule 19 (1)]

MANIFEST FOR HAZARDOUS AND OTHER WASTE

1	Sender's name and mailing address (including Phone No. and e-mail)	M/S Shiv Shakti Oil & Lubricants Village: Gopalpahari, Gurgaon Fazalabad Road, Gurgaon			
2	Sender's Authorisation No.				
3	Manifest Document's No.	SSOL / HW / 01 / M/S Shiv Shakti Oil & Lubricants / DD-01/2019/219			
4	Transporter's name and address (including Phone No. and e-mail)	M/S Shiv Shakti Oil & Lubricants			
5	Type of vehicle	(Truck/Tankers/Special Vehicle)			
6	Transporter's registration No.	RUPR/HWM/2018-19/992/102/160			
7	Vehicle registration No.	RT 406A 165B / RT 4061420			
8	Receiver's name and mailing address (including Phone No. and e-mail)	SHIV SHAKTI OIL & LUBRICANTS F-557 & F-693 (Unit 3), RICO Industrial Area, Chopanki, Post: Durgam, Teh. Tijara, Distt. Alwar - 301701 (Rajasthan) - INDIA Ph: (91) 9310003339, 9350081331 E: shivshakti@rediffmail.com			
9	Receiver's Authorisation No.	RSPCB / HWM / 2018-2019 / HSW / HSW / 21 RSPCB / HWM / 2018-2019 / HSW / HSW / 103 (Unit 3)			
10	Waste description	Used Lube Oil, Used Cutting Coolant Oil (Cat 6.1) ✓ Used Hydraulic Oil, Used Transformer Oil (Cat 5.2) ✓ Waste or Residues Containing Oil (Cat 5.2) ✓ Containers/ Barrels/ Drums Contaminated with Hazardous Chemicals/ Waste (Cat 33.1) (Unit-3) ✓ Hazardous Waste			
11	Total quantity No. of Containers	530 litres m ³ or MT (1000) Nos.			
12	Physical form	(Solid/Semi-Solid/Sludge) OILY / Tarry / Slurry / Liquid			
13	Special handling instructions and additions: information to handle with care)	Disposed/ sale as per Precautional Rules of Central Pollution Control Board/ MOEF/ SPCB to the Authorized Reg. Re-recycler/ Re-processor			
14	Sender's Certificate	I hereby declare that the contents of the consignment are fully and accurately described above by proper shipping name and are categorised, packed, marked and labelled and are in all respects in proper condition for transport by road according to applicable national government regulations			
	Name & stamp	Signature	Month	Day	Year
15	Transporter acknowledgement of receipt of Wastes		01	21	2019
	Name & stamp	Signature	Month	Day	Year
16	Receiver's certification for receipt of hazardous and other waste		01	21	2019
	Name & stamp	Signature	Month	Day	Year
	Shiv Shakti Oil & Lubricants		01	21	2019

Authorised Signatory

COPY 1 of 7

White Copy

To be forwarded by the sender to the State Pollution Control Board

IInd Pass-book

Authorisation Cum-Passbook for
Handling/Recycling of Hazardous Waste



राजस्थान राज्य प्रदूषण नियंत्रण बोर्ड

RAJASTHAN STATE POLLUTION CONTROL BOARD

4, Jyoti Chauri, Sector, Market, Durgam, Jaipur
www.environment.rajasthan.gov.in

2nd Pass-book

Authorisation Cum-Passbook for
Re-refining/Recycling of Hazardous Waste

11

Name and Address of the Industry : M/s Shiv Shakti oil & Lubricants
F-557, RIA Chopanki, Bhimadi,
Tehsil - Tijara, Alwar

Telephone/Fax No. : 09212601330

E-Mail Address : shivshakti_lub_01@yahoo.co.in


Authorisation No. F(HW)/Alwar (Tijara) 1845(D)/2014-15/535-537/25/04/2018

Date of issue : 04/02/2020

Validity period : 04/02/2020 To 31/03/2023

Type & quantity of the Hazardous Waste (S) permitted for procurement and recycling

S. No.	Hazardous Waste (Used/Waste Oil) Type	Quantity (Kilolitres/Metric ton per annum)
1.	<u>Used or spent oil</u>	<u>2000 KLA</u> <u>(Two Thousand Kilo</u> <u>Liter per Annum)</u>



Authorized Signatory & Seal

[Handwritten signature]

Conditions of the Authorisation:-

1. The Authorisation shall cease to be valid in case of expiry of the validity of suspension or cancellation of any of the existing consents under Water (Prevention & Control of Pollution) Act, 1974 and Air (Prevention & Control of Pollution) Act, 1986 and Authorization under Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016 and as amended issued by the Rajasthan State Pollution Control Board (RSPCB) and shall remain invalid till consents/authorization are obtained.
2. The Re-refiner/Recycler shall submit copies of the valid consents and authorization also to the auctioneer/seller at the time of each procurement.
3. The Re-refiner/Recycler shall be responsible to ensure that the quantity of the waste(s) procured each time is endorsed in this Pass-Book by the authorized seller/auctioneer.
4. The Re-refiner/Recycler shall obtain a copy of the analysis report of the used oil/waste oil from the generator at the time of each procurement and submit the same to RSPCB.
5. The authorized Re-refiner/Recycler shall maintain the record of above mentioned Recyclable Waste procured for re-refining/recycling and submit the Annual Return regarding utilization of such wastes to the RSPCB as per Form-4 of the Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016 by 30th June of every year for the preceding period April to March.
6. This Authorisation is subject to the conditions and the procedure of the time to time as may be notified or any other authorisation by the Ministry of Environment, Forest and Climate Change (MoEF&CC)/Central Pollution Control Board (CPCB) or Rajasthan State Pollution Control Board (RSPCB).
7. The Re-refiner/Recycler shall not rent/lend/sell/transfer this Authorisation certificate.
8. Any change in the Re-refining/Recycling technology, disposal facility and equipment as given in the application shall only be carried out with prior permission of RSPCB.

9. Transportation, processing, treatment and disposal of wastes shall be carried out strictly as per the Guidelines on "Management Handling of Hazardous Wastes 1991" issued by MoEF and in accordance with the Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016.
10. The hazardous wastes generated from the recycling process including the residue generated in re-refining of used oil shall be disposed of as per the Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016.
11. The unit shall submit quarterly report giving details of used oil/waste oil procured, quantity of the products manufactured and sold (supported with Central Excise/Sales Tax details), quantity of waste generation and its mode of disposal, to RSPCB.
12. The unit should take appropriate and adequate measures to control fugitive emissions such that the work zone standards are met.
13. The unit should carry out stack emission of Ambient Air Quality (AAQ) monitoring for PM₁₀, PM_{2.5}, SO₂, NO_x and monitoring reports should be submitted by the unit to the RSPCB, as per the consent conditions.
14. Application (in triplicate) for renewal of authorisation shall be made well in advance, at least three months before expiry, in Form 1 along with each of the documents as per requirement of Rule 6(a)(i) of Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016 and as desired by the RSPCB from time to time.
15. At the time of submission of the application for renewal of authorisation, the unit should submit a copy of the "Authorisation-Cum-Passbook" along with a statement showing past year compliance status of the above conditions. This information should be supported with supported with Central Excise/Sales Tax details.
16. The authorisation may be cancelled or suspended by RSPCB as per Rule 7 (1) of the HW Rules, in case the Re-refiner/Recycler fails to comply with any of the conditions of the authorisation or with any of the provisions of the Environment (Protection) Act, 1986 as amended or Rules made there under.

**Endorsement by the Auctioneer/Seller (except column no. 6 & 7)
(Condition No.3 of the Authorisation)**

Authorisation No: 11150 / 11150 / 11150 / 11150 / 11150 Date: 25/04/2021

Waste(s) Type: Waste Oil Permitted Quantity: 2000 KL

S. No.	Date	Address of the Auctioneer/Seller	Type & Quantity of HW sold /Auctioned	Signature & Seal of the Auctioneer/Seller with date	Date of arrival in Recycler's premises & Challan No.	Balance Quantity (Registered - procured till date)
(1)	(2)	(3)	(4)	(5)	(6)	(7)
55	18/01/21	Waste Municipal Industrial Waste	Waste Oil 8140 kg		18/01/21 Challan No. 132054	2000 KL
56	22/01/21	The K. Tech Cross St. R.R. Road	Waste Oil 4180 kg		22/01/21 Challan No. 1362152	1782 KL
57	28/01/21	ASP S.S. Road Villupuram Chennai	Waste Oil 3300 kg		25/01/21 Challan No. 130011	1452 KL
58						
59						
60						


*to be filled by the Recycler

DRIVER - JV

Indian Oil Corporation Limited

Registered under the Goods and Services Tax Act, 2017

We hereby certify that the goods covered by this document have suffered legal title. Taxes on clearance.



TAX INVOICE

Invoice No: AC/ 81A
SAP Entry no: 745341663
Date: 27-Aug-21
Time: 09:57

Supplier: Indian Oil Corporation Ltd, Mathura
Consignee: ASE INDIANA SEZ PRIVATE LIMITED, Gurgaon

S.O. No INR. 001153/00/5609521/2021-001

Table with columns: Item, Material Code, Material Description, Quantity, Unit, Rate, Unit, HSN Code, Total

Table with columns: Item, Material Code, Material Description, Quantity, Unit, Rate, Unit, HSN Code, Total

Summary table with columns: Particulars, Amount

Handwritten notes and signatures on the left side of the invoice.

ASE INDIANA SEZ PVT. LTD. Invoice No: 522, Date: 27/08/21

Signature and stamp of the consignee.

This document is digitally signed

Signer: SHIV CHARAN SINGH CHOUHAN, Date: Fri, Aug 27, 2021 09:58:21 IST


Bottom section containing checkboxes for 'IMPROVED IN GOOD CONDITION', 'CUSTOMER'S SIGNATURE/SEAL', and 'RECEIVED BY'.



Indian Oil Corporation Limited

INVOICE CREDITED TO THE ACCOUNT OF THE BUYER

We hereby certify that the goods covered by this document have suffered application of taxes on clearance



Doc No: **TAX INVOICE**

Form No: **AO4 31A**
Del Mode: **Speed**
Com Code: **1914348**

SAP Entry no: **746691679**
T.T. No: **UP95BT080**
Den @ 16: **824.30**

Date: **29 Jun-21**
Time: **11:27**
From: **Office/Inn**

Conc Name & Add: **1025 (CONL) 2320 16M 11809001511364**
Dest: **Mathura Terminal 1025**
C.E. Pkg: **AAACH801GXM154**
C.E. Name: **MATHURA REFINERY MATHURA**
C.E. Division: **A-18, KADAMB VIHAR, MATHURA**
C.E. Commissionerate: **113A SARJAY PLACE AGRA**
PAN: **AAACH801G**

Supplier: **1025 (CONL) 2320 16M 11809001511364**
CIN: **252016M11809001511364**
GSTIN: **09G02548 DT 20 LST: 00002100006**
SAP TAN: **DEL1006020**

CONSIGNEE: **25354 (Mob No: 989095276)**
ASF INSIGNIA SEZ PRIVATE LIMITED
EARLIER CARTON DULLSVELL PVT. LTD
BHAL PANARI, DURGAON-PARIDABAD
DURGACON: **122018**
12008
MAYANK
MAYANK

Doc No: **1914348**
Date: **29 Jun 2021**
S.L.N.
0962545

Item	Material Code / Material Description	Quantity	Unit	Rate	Unit	HSN code	Total
10	50730 160 - BR M	12.000	KL			2710 44	
	ZWL: Transport Value	12.000	KL	4366.000	KL		51732.00
	NET TRANS FOR US DMS CHARGES				INR		1970.87
	Tank no: 102520.01.2021					Total of 0.00000	53457.87
	Sample no: 102520.01.2021						
	Bay no: 30						
	ZIND: Branding Difference						0.00
Total							53458.00

1025	160	100
1025	160	100
1025	160	100

ASF Insignia SEZ Pvt. Ltd.
INWARD/OUTWARD ENTRY
 SI No: 1318
 Time In: 07:15M
 Time Out: 07:15M
 Gate: 20
 Sign. (Security): [Signature]

D.K. or/for
7/6/21
 ASF Insignia SEZ Pvt. Ltd.
 ENTRY NO: 360
 DATE: 29/06/21
 SIGNATURE: [Signature]

Provisional Balance of 53458.00 to be credited on 29/06/21 (SI)

Location: **DEL1006020**
CIN: **252016M11809001511364**
GSTIN: **09G02548 DT 20 LST: 00002100006**

AKS 10038

Doc No: **1914348**
Date: **29 Jun 2021**
This document is digitally signed

Signer: **SHIV CHARAN GUPTA CHOLMAN**
Date: **Tue, Jun 29, 2021 11:27:03 IST**

RECEIVED IN GOOD CONDITION	PLANNED BY	PAGE No: 1 / 1
<i>[Signature]</i>	02119841	
CUSTOMER'S SIGNATURE / SEAL	APPROVED BY	FOR: INDIAN OIL CORPORATION LIMITED


Receipt and the parties are given above the date and content of it by means of indelible ink and represent the price actually charged and that there is no flow of additional or modification or cells or remedy use VHS Boyar SERIAL NUMBER CARRIED BY



Indian Oil Corporation Limited

Delivered (INVOICE) Bill of Sale and Receipt

We hereby certify that the goods covered by this document have suffered applicable Taxes on clearance



Doc Name: TAX INVOICE

749669941

Form No: AQ4 STA

SAF Entry no: 749669941

Date: 29-May-21

Del Mode: Road

Delivered

UTI No.

UP06AT6399

Time: 10:00

Cont Code: 11010050

Qty@16

834.30

Rem Date/Time

Cono Name & Address

1525 (CIN:L25201MH189900011558)
Mathura Terminal
1525

Cono

253534 (CIN:U650505275)
ASPI INSIGNIA SEZ PRIVATE LIMITED
SASURJI CAN FOR PLOT OWELL FIVE LT
GWAL-I/II-II GURGAON-FARIDABAD
GURGAON 120018

Tr: 0681678934

12035

Haryana

S.O. No: SHT-134130007-542937-12-00-2021

C.E. Regt
C.E. Range

AAAG100100174
MATHURA DEPT/MATHURA

C.E. Division

A-6, SADANSI VHAFF, MATHURA

C.E. Commissioner

1139, SANJAY PLACE AGRA

AAAG1885000154

AAAG16870

PAN

GST: LS2506504A DT 26, LSS 055210109

AAAG07148L

GSTIN: TAX: DEL060505

TAXIN: 253534-ASPI-INSIGNIA-SEZ-PRIVATE-LIMITED

Item	Material Code / Material Description	Quantity	Unit	Rate	Unit	HSN code	Tax	
10	30700 1535 03VI	17.000	KG			2720 1200		
	ZAVI Transportation Value	32.000	%	39923.559	KG	191	12780.12	
	NET TRANSPORTATION CHARGES							
	Tank no: 104B (Capacity: 15, 004, 300)							
	Sample no: 1535-29.05.2021							
	Buy No: 07							
	ZRH0 Bonding filled up							
Total								495709.89

Shortage book

Item	Rate	Qty	Value
104	112.0	8.00	916.00
102	117.0	3.00	351.00
103	118.0	3.00	354.00
105	117.0	4.00	468.00

Chamber no 1 - 7.5 kg
Chamber no 4 - 25 kg
Total = 32.5 kg

ASPI INSIGNIA SEZ PVT. LTD.
ENTRY NO. 1033
DATE 29/05/21
Signature: [Handwritten]

ASPI INSIGNIA SEZ PVT. LTD.
ENTRY NO. 1033
DATE 29/05/21
Signature: [Handwritten]

Pre-paid Balance Subject to availability: 1157000.00

29/05/21

Doc No: 300000000
Delivery no: 0521005079 Doc. Date: 20210529
DO NOT DESTROY THIS DOCUMENT
DUTY PAYABLE: 0.000
Export ref. no: 12910001070
This document is digitally signed
Signer: MOHIT DWIVEDI
Date: Sat, May 29, 2021 10:05:25 IST


<p>REGISTRATION NO: AAAG100025</p> <p>29/5/21</p> <p>REGISTRATION NO: AAAG100025</p> <p>REGISTRATION NO: AAAG100025</p>	<p>REGISTRATION NO: AAAG100025</p> <p>REGISTRATION NO: AAAG100025</p>	<p>REGISTRATION NO: AAAG100025</p> <p>REGISTRATION NO: AAAG100025</p>	<p>REGISTRATION NO: AAAG100025</p> <p>REGISTRATION NO: AAAG100025</p>
---	---	---	---



Indian Oil Corporation Limited

INVOICE UNDER RULE 111 of Central Excise Act

We hereby certify that the goods covered by this invoice have suffered applicable Taxes on clearance



Doc Name & number: FAX INVOICE

Form No: ACP 31A, SAP Entry no: 744480548, Date: 27-Jul-21, Del Mode: Road, T.T.No: UP85BT5141, Time: 10:41, Cont Code: 11047537, Don @ 15: 820.00, Item Date/Time

Supplier: MATHURA REFINERY, MATHURA, U.P. 281005. Consignee: ASF INDIAN OIL PRIVATE LIMITED, LAJPURAH CANTON BUILDING, 11 SWAL PAHARI, GURGAON, HARYANA 122016. PAN: AAAC07148L

S.O. No: 100/2021/2021/2021/2021

Supplier TAN: DEJ098826, PAYOR: 80534 ASF INDIAN OIL PRIVATE LIMITED

Table with columns: Item, Material Code / Material Description, Quantity, Unit, Rate, Unit, HSN code, Total. Includes items like ZAVL Transformer Value and NEY TRANSPORTATION CHARGES.

Summary table with columns: HSN, ITP, Qty, Value

Handwritten notes and signatures: D.K. A. A. T. and ASF INDIAN OIL PRIVATE LIMITED. Includes fields for ENTRY NO, DATE, and SIGNATURE.

Handwritten notes: ASF INDIAN OIL PRIVATE LIMITED, INWARD/OUTWARD ENTRY, SI No, Time In, Time Out, Date, Sign.

Provisional Refund Subject to reconciliation: 25450.00 (CP)

Control No, Date of issue, Date of entry

Handwritten amount: 1000000

File No: 200011206, Delivery no: 05234152 / Sales Crick: 000071385, PO No: 210721153/MC22, DUTY PAYABLE: 0.000

This document is digitally signed


Signor: SHY CHAMAN SINGH CHOCHAN, Date: Tue, Jul 27, 2021 10:42:15

Form with sections: RECEIVED IN GOOD CONDITION, PREPARED BY, PAGE No: 1 / 1, CUSTOMER'S SIGNATURE, TAXES, ATTACHED BY, RELEASED BY, and Indian Oil Corporation Ltd logo.



Indian Oil Corporation Limited

We hereby certify that the goods covered by this document have suffered applicable taxes on clearance.



TAX INVOICE

Doc No: AC4 31A
E. number: 14214560

SAP Entry no: 741641353
L.I. No: HP85B7790B
Date: 29-Apr-21
Time: 10:53

Rep. Date/Time

Code Name & Address:

1526 (GIRL) 28221 MH 155900-01-569)
Mallapuram Terminal
1526
Indian Oil Corporation Ltd
Mallapuram 291006

Supplier

255534 (Mch No: 9552366275)
ASF INSIGNIA SEZ PRIVATE LIMITED
EAPLEER CARTON BUILDING, 5V1, 1T
BVAL PALAZI, GURGAON FARIDABAD
GURGAON 122018
Haryana

G.C. No: 101192007-202007-18us-2021

2983288

G.T. Regn. G.E. Range

AAAG1081GXM154
MATHURA REGION/RY/MATHURA

G.E. Division

A-B, KADAMU VIHARI, MATHURA

G.E. Commissioner's Office

1134, SANJAY PLACE AGRA

PAN

AAAG1081GXM156

AAAG1081G

AACCC7145L

Supplier TAN: DEJ2885503

PAYEE: 0524 ASF INSIGNIA SEZ PRIVATE LIMITED

Item	Material Code	Material Description	Quantity	Unit	Rate	Unit	HSN Code	Total
10	5070	ISSD - DG V4	12.000	KL			2710 59 44*	
	2691	Transportation Value	12.000	KG	31425.750	KG		377105.76
		NET TRANSPORTATION CHARGES						32570.90
		Tank no: 1068 Date: 29/04/2021						
		Sample no: 15529004-2021						
		BSY No: 15						
		ZFRD (Rounding Difference)						0.76
Total								443067.40

OT	OT	OT
1000	11.00	3.00
1001	1.00	2.00
1002	1.00	3.00
1003	1.00	3.00

Handwritten notes and stamps: 958, 13.00, 29/04/21, DIP AR, 29/04/21, 29/04/21, 29/04/21.

Professional E-mail Subject: 14214560 (2021) (2021)

Signature: SHIV CHANDAN SINGH CHAUDHARI
Date: Thu, Apr 29, 2021 10:53:18 IST


PREPARED BY	RECEIVED IN GOOD CONDITION	DATE	PAGE No: 1/1
SIGNATURE			
APPROVED BY	SIGNATURE	DATE	RECEIVED BY



Indian Oil Corporation Limited

INDIAN OIL CORPORATION LIMITED

We hereby certify that the goods covered by this document have suffered applicable Taxes on clearance



TAX INVOICE

Doc Name & Number
Form No AC4 31A
Del Mode Head
Cont Code 11047854

SAP Entry No. 740277743
T.E.No. 0985071750
Dn @ 15 820.30

Date 27-Sep-21
Time 11.28
Rem Date/Time

Supplier		CONSIGNEE	
Code	1515 (UNL2320) MATHURAPUR (11388)	253034 (Job No. 0650506275)	
Name & Address	Mathura Terminal 1325 Indian Oil Corporation Ltd Mathura 281005	ASF INSIGMA SEZ PRIVATE LIMITED EARLIER CANTON DULOWALI, PVT. LT GWA. PAHARI, GURGAON-PARDABAI GURGAON 122016	
Dist.		12025	Hariana
C.C. Regn	AAAC1081GXM154		
C.E. Range	MATHURA REFINERY, MATHURA		
C.T. Division	A-5, KADAMB VILLAGE, MATHURA		
C.E. Commission	133M, SANJAY PLACE AGRA		
PAN	AAAC1081GXM154 AAAC1081G	AAC00746L	
	CS / LW5068049 UT 28 LSI: 09552100036		
	Supplier TAN: DEL-090526		
		PMTA - 20134451 INSIGMA SEZ PRIVATE LIMITED	

Item	Material Code / Material Description	Quantity	Unit	Rate	Unit	HSN code	Total
10	SLAG 43D - BS V	20000	KG			2740 10 44	
	ZWL Transaction Value	20000	KG	4700.00	INR		94000.00
	Net TRANSPORTATION CHARGES				INR		2515.02
	Total no. TMA freely @ 10: 001.900						
	Sample no. 10202109.2021						
	Reg No.: 09						
	ZIND Bonding Difference						0.26
Total							911247.00

Sl. No.	Sp. No.	Qty. -
1000	1155	4.00
1011	1255	4.00
1012	1355	4.00
1013	1455	4.00
1014	1555	4.00
1015	1655	4.00

ASF Insigma SEZ Pvt. Ltd.
INWARD/OUTWARD ENTRY
Sl. No. 2981
Type of 09100
Trans. No. 28/09/21
Date 28/09/21
Sign (Security) [Signature]

ASF INSIGMA SEZ PVT. LTD.
ENTRY NO. 60
DATE 28/09/21
SIGNATURE [Signature]

Shreejee Bank
Change no - 4 - 5 LPA
Change no - 5 - 15 LPA

Pre-debit Balance Refused to appropriation: 21850.00 (04)

AMOUNT RECEIVED
CASH 1000
BY BANK

Call no. 022485722 / Sales Order 031707192
PO no. 2109/11101/0078
CITY HAZRAT : 3030

This document is digitally signed

Sign: BHV CHARAN SINGH CHOUHAN
Date: Mon, Sep 27, 2021 11:29:45 IST

INTK is the address of the user's Organization only.	RECEIVED IN GOOD CONDITION	PREPARED BY	PAGE No 1 / 1	Weighted by Sign
Notified that the particular area above mentioned will be held and the related financial records will be held and only charged and will issue a bill of material certificate directly or not with the user.	CUSTOMERS INQUIRY SYSTEM	TRANSPORTS WITH NET SIGNATURES	NOT CHARGED BY RELEASED BY	For INDIAN OIL CORPORATION LTD.



EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory
(an ISO 9001:2015 Certified Company)

Office / Laboratory : Plot 1, Sector 104, Gurgaon, Haryana, India. (Near IITG, Sector 104, Gurgaon, Haryana, India)
Contact No. : 0122654477, 9111310378, 9826344487. Email : info@ekoengineers.com, eko@ekoengineers.com

TEST REPORT

Stack Emission Analysis

Test Report No. : EKO/126/070621

Issue Date : 12/06/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahari,
Gurgaon Faridabad Road
Gurugram Haryana- 122003

Sample Description	: Stack Emission
Sample Drawn on	: 07/06/2021
Sample Drawn by	: EPEPL (Mr. Anuj kumar)
Sample Received on	: 07/06/2021
Time of Sampling (minutes)	: 30.0
Sampling Location	: BLDG-02
Sampling Plan & Procedure	: SOP-SE/09
Analysis Duration	: 07/06/2021 To 11/06/2021
Source of Emission	: St. Att. To DG Set No.6 (Engine No. 33182535)
Capacity	: 2000 KVA
Operating Load	: Normal
Normal Operation Schedule	: As per requirement
Type of Stack	: Metal/Circular
Diameter of Stack (meter)	: 0.4
Height of Stack from Ground Level (meter)	: 31.0
Height of Stack from Roof Level (meter)	: 18.0
Height of Sampling Location (meter)	: 12.5 From Ground Level
Type of Fuel Used	: HSD
Fuel Consumed per hour	: -
Ambient Temperature (°C)	: 37.0
Stack Temperature (°C)	: 250.0
Average Velocity of Flue Emission (m/sec)	: 13.8
Average Flow Rate (lpm)	: 37.9
Control Measures (if any)	: Nil
Remark (if any)	: NA

RESULTS

S.No.	Parameters	Test Methods	Results	Units	Limits as per EPA-1986, (SI-96 Schedule-I)
1	Particulate Matter (as PM)	IS: 11255 (P-1)	46.8	mg/Nm ³	75.0
3	Oxide of Nitrogen (as NOx)	IS: 11255 (P-7)	230.1	ppmv	710.0
3	Carbon Monoxide (as CO)	USEPA (P-10)	50.4	mg/Nm ³	150.0
4	NMHC	IS : 5182 (P-21)	20.6	mg/Nm ³	100.0


Remark- PM, NOx, NMHC & CO at 15% O₂ Correction.

Notes :

- The results given above are related to the tested sample, for various parameters, as observed at the time of Sampling. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the involved amount only.

** End of Report **

For EKO PRO ENGINEERS PVT. LTD.





Office & Laboratory : 2011, South Gate of D. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 001 (Uttarakhand) INDIA
 Contact No. : 01826-271997 / 2719999, 2719999 / Fax No. : 01826-2719999, 2719999 / E-mail : eko@ekoengineers.com, eko@ekoengineers.com, eko@ekoengineers.com

TEST REPORT

Stack Emission Analysis

Test Report No. : EKQ138/080421

Issue Date : 12/06/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
 Village - Gwal Pahar,
 Gurgaon Faridabad Road
 Gurugram Haryana - 122003

Sample Description : Stack Emission
 Sample Drawn on : 07/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj Kumar)
 Sample Received on : 08/06/2021
 Time of Sampling (minutes) : 30.0
 Sampling Location : BLDG-02
 Sampling Plan & Procedure : SOP-SE/09
 Analysis Duration : 08/06/2021 To 12/06/2021
 Source of Emission : St. Att. To DG Set No.7 (Engine No. 33181793)
 Capacity : 2000 KVA
 Operating Load : Normal
 Normal Operation Schedule : As per requirement
 Type of Stack : Metal/Circular
 Diameter of Stack (meter) : 0.4
 Height of Stack from Ground Level (meter) : 31.0
 Height of Stack from Roof Level (meter) : 15.0
 Height of Sampling Location (meter) : 12.5 From Ground Level
 Type of Fuel Used : HSD
 Fuel Consumed per hour : -
 Ambient Temperature (°C) : 37.0
 Stack Temperature (°C) : 258.0
 Average Velocity of Flue Emission (m/sec) : 13.9
 Average Flow Rate (lpm) : 19.6
 Control Measures (if any) : Nil
 Remark (if any) : NA

RESULTS

S.No.	Parameters	Test Methods	Results	Units	Limits as per EPA-1986, (SL-90 Schedule-I)
1	Particulate Matter (as PM)	IS: 11255 (P-1)	49.1	mg/Nm ³	75.0
3	Oxide of Nitrogen (as NOx)	IS: 11255 (P-7)	238.1	ppmv	710.0
3	Carbon Monoxide (as CO)	USEPA (P-10)	64.9	mg/Nm ³	150.0
4	NMHC	IS : 5182 (P-21)	19.1	mg/Nm ³	100.0

Remark- PM, NOx, NMHC & CO @ 15% O₂ Correction.

Notes :

- The results given above are related to the tested sample, for various parameters, as observed at the time of Sampling. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the invoiced amount only.

** End of Report **

For EKO PRO ENGINEERS PVT. LTD.

FORNIMA KULJIAN
 TECHNICAL MANAGER
 (Authorized Signatory)



Office & Laboratory: B-141, South Side of G.P. Road, UNCCO Industrial Area, Ghaziabad - 201 001 (near Metro Park,
Gurgaon No. 201200427, Ghaziabad, Uttar Pradesh. Email: info@ekopro.com, ekopro@ekopro.com, website: www.ekopro.com

TEST REPORT

Stack Emission Analysis

Test Report No. : EKO/127/070621

Issue Date : 12/06/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahari,
Gurgaon Faridabad Road
Gurugram Haryana- 122003

Sample Description : Stack Emission
Sample Drawn on : 07/06/2021
Sample Drawn by : EPE:PL (Mr. Anuj kumar)
Sample Received on : 07/06/2021
Time of Sampling (minutes) : 30.0
Sampling Location : BLDG-02
Sampling Plan & Procedure : SOP-SE/09
Analysis Duration : 07/06/2021 To 11/06/2021
Source of Emission : St. Att. To DG Set No.8 (Engine No. 33184129)
Capacity : 2000 KVA
Operating Load : Normal
Normal Operation Schedule : As per requirement
Type of Stack : Metal/Circular
Diameter of Stack (meter) : 0.4
Height of Stack from Ground Level (meter) : 31.0
Height of Stack from Roof Level (meter) : 18.0
Height of Sampling Location (meter) : 12.5 From Ground Level
Type of Fuel Used : HSD
Fuel Consumed per hour : -
Ambient Temperature (°C) : 37.0
Stack Temperature (°C) : 258.0
Average Velocity of Flue Emission (m/sec) : 14.1
Average Flow Rate (lpm) : 18.8
Control Measures (if any) : Nil
Remark (if any) : NA

RESULTS

S.No.	Parameters	Test Methods	Results	Units	Limits as per EPA-1986, (SL-96 Schedule-I)
1	Particulate Matter (as PM)	IS: 11255 (P-1)	42.9	mg/Nm ³	75.0
3	Oxide of Nitrogen (as NOx)	IS: 11255 (P-7)	249.6	ppmv	710.0
3	Carbon Monoxide (as CO)	USEPA (P-10)	52.4	mg/Nm ³	150.0
4	NMHC	IS : 5182 (P-21)	20.1	mg/Nm ³	100.0

Remark- PM, NOx, NMHC & CO at 15% O₂ Correction.

Notes :

- The results given above are related to the tested sample, for various parameters, as observed at the time of Sampling. The customer asked for the above test(s) only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the invoiced amount only.

** End of Report **

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA KUMAR
TECHNICAL MANAGER
(Authorized Signatory)



Office & Laboratory : 22nd Fl., South Side of D-1 Road, UPPCOS Industrial Area, Gurgaon - 201 003 (Delhi State), India.
 Contact No. : 0124254827, 0124254828, 0124254829 Fax : 0124254829, 0124254830, 0124254831, 0124254832
 E-mail : eco@ekopro.com, ekopro@ekopro.com, ekopro@ekopro.com, ekopro@ekopro.com

TEST REPORT**Stack Emission Analysis**

Test Report No. : EKO/139/000621

Issue Date : 12/06/2021

Issued To

: ASP INSIGNIA SEZ PVT. LTD.
 Village - Gwal Bahari,
 Gurgaon Faridabad Road
 Gurgaon Haryana- 122003

Sample Description : Stack Emission
 Sample Drawn on : 07/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj Kumar)
 Sample Received on : 08/06/2021
 Time of Sampling (minutes) : 30.0
 Sampling Location : BLDG-02
 Sampling Plan & Procedure : SOP-SE/03
 Analysis Duration : 08/06/2021 To 12/06/2021
 Source of Emission : St. Att. To DG Set No.9 (Engine No. 33184356)
 Capacity : 2000 KVA
 Operating Load : Normal
 Normal Operation Schedule : As per requirement
 Type of Stack : Metal/Circular
 Diameter of Stack (meter) : 0.4
 Height of Stack from Ground Level (meter) : 21.0
 Height of Stack from Roof Level (meter) : 18.0
 Height of Sampling Location (meter) : 12.5 From Ground Level
 Type of Fuel Used : HSD
 Fuel Consumed per hour : -
 Ambient Temperature (°C) : 37.0
 Stack Temperature (°C) : 260.0
 Average Velocity of Flue Emission (m/sec) : 14.1
 Average Flow Rate (lpm) : 19.8
 Control Measures (if any) : Nil
 Remark (if any) : NA

RESULTS

S.No.	Parameters	Test Methods	Results	Units	Limits as per EPA-1986, (SL-96 Scheduled-I)
1	Particulate Matter (as PM)	IS: 11285 (P-1)	50.8	mg/Nm ³	75.0
3	Oxide of Nitrogen (as NOx)	IS: 11255 (P-7)	342.6	ppmv	710.0
3	Carbon Monoxide (as CO)	USEPA (P-10)	58.1	mg/Nm ³	150.0
4	NMHC	IS: 5182 (P-21)	19.8	mg/Nm ³	100.0

Remark: PM, NOx, NMHC & CO at 15% O₂ Correction.

Notes :

- The results given above are related to the tested sample, for various parameters, as observed at the time of Sampling. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the invoiced amount only.

** End of Report **

For EKO PRO ENGINEERS PVT. LTD.

FORNIMAL KISHAN
 TECHNICAL MANAGER
 (Authorized Signature)



Office & Laboratory : 33/11, Sector No. 14, Gurgaon, Haryana, India. (Near IFCO Industrial Area, Gurgaon - 122 002 (near NCR) State
 Contact No. 9911810742, 9910299521, 9925544400. Email: info@eko-pro.com, ekopro@eko-pro.com, ekopro@eko-pro.com

TEST REPORT

Stack Emission Analysis

Test Report No. : EKO/136/080621

Issue Date : 12/06/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
 Village - Gwal Pahari,
 Gurgaon Faridabad Road
 Gurgaon Haryana - 122103

Sample Description : Stack Emission
 Sample Drawn on : 07/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj Kumar)
 Sample Received on : 06/06/2021
 Time of Sampling (minutes) : 30.0
 Sampling Location : HDG-03
 Sampling Plan & Procedure : SOP-SE/09
 Analysis Duration : 08/06/2021 To 12/06/2021
 Source of Emission : St. Ati. To DG Set No.11 (Engine No. 33191516)
 Capacity : 2000 KVA
 Operating Load : Normal
 Normal Operation Schedule : As per requirement
 Type of Stack : Metal/Circular
 Diameter of Stack (meter) : 0.4
 Height of Stack from Ground Level (meter) : 31.0
 Height of Stack from Roof Level (meter) : 18.0
 Height of Sampling Location (meter) : 12.5 From Ground Level
 Type of Fuel Used : HSD
 Fuel Consumed per hour : -
 Ambient Temperature (°C) : 37.0
 Stack Temperature (°C) : 260.0
 Average Velocity of Flue Emission (m/sec) : 14.2
 Average Flow Rate (lpm) : 18.9
 Control Measures (if any) : Nil
 Remark (if any) : NA

RESULTS

S.No.	Parameters	Test Methods	Results	Units	Limits as per EPA-1986, (SL-08 Schedule-I)
1	Particulate Matter (as PM)	IS: 11255 (P-1)	48.4	mg/Nm ³	75.0
3	Oxide of Nitrogen (as NOx)	IS: 11255 (P-7)	236.6	ppmv	710.0
3	Carbon Monoxide (as CO)	USEPA (P-10)	60.4	mg/Nm ³	150.0
4	NMHC	IS: 5182 (P-21)	19.4	mg/Nm ³	100.0

Remark- PM, NOx, NMHC & CO at 15% O₂ Correction.

Notes :

- The results given above are related to the tested sample, for various parameters, as observed at the time of Sampling. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the invoiced amount only.

** End of Report **

For EKO PRO ENGINEERS PVT. LTD.

SPURDIPAL CHAUHAN
 TECHNICAL MANAGER
 (Authorized Signature)



Client's Laboratory : 0241, South Side of P. T. Road, District Industrial Area, Gurgaon - Dist. Haryana (Gurgaon) India.
Contact No: 991-49567, 9910730670, 990164497. Email: eko@eko-pro.com, eko@eko-pro.com, web-site: www.eko-pro.com

TEST REPORT

Stack Emission Analysis

Test Report No. : EKO/125/070621

Issue Date : 12/06/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahar,
Gurgaon Faridabad Road
Gurgaon Haryana- 122003

Sample Description : Stack Emission
Sample Drawn on : 07/06/2021
Sample Drawn by : CPEPL (Mr. Anuj kumar)
Sample Received on : 07/06/2021
Time of Sampling (minutes) : 30.0
Sampling Location : BLDG-03
Sampling Plan & Procedure : SOP-SE/08
Analysis Duration : 07/06/2021 To 11/06/2021
Source of Emission : St. Att To DG Set No.12 (Engine No. 33191592)
Capacity : 2000 KVA
Operating Load : Normal
Normal Operation Schedule : As per requirement
Type of Stack : Metal/Circular
Diameter of Stack (meter) : 0.4
Height of Stack from Ground Level (meter) : 31.0
Height of Stack from Roof Level (meter) : 18.0
Height of Sampling Location (meter) : 12.5 From Ground Level
Type of Fuel Used : HSD
Fuel Consumed per hour : -
Ambient Temperature (°C) : 37.0
Stack Temperature (°C) : 260.0
Average Velocity of Flue Emission (m/sec) : 14.1
Average Flow Rate (lpm) : 18.5
Control Measures (if any) : Nil
Remark (if any) : NA

RESULTS

S.No.	Parameters	Test Methods	Results	Units	Limits as per EPA-1986, (SL-98 Schedule-I)
1	Particulate Matter (as PM)	IS: 11255 (P-1)	44.8	mg/Nm ³	75.0
3	Oxide of Nitrogen (as NO _x)	IS: 11255 (P-7)	235.1	ppmv	710.0
3	Carbon Monoxide (as CO)	USEPA (P-10)	54.8	mg/Nm ³	100.0
4	NMHC	IS: 5182 (P-21)	19.1	mg/Nm ³	100.0

Remark: PM, NO_x, NMHC & CO at 16% O₂ Correction.

Notes :

- The results given above are related to the tested sample, for various parameters, as observed at the time of Sampling. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the invoiced amount only.

** End of Report **

For EKO PRO ENGINEERS PVT. LTD.

ANUJ KUMAR
TECHNICAL MANAGER
(Additional Signature)



SRO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory
 (An ISO 9001:2015 Certified Company)

Plot 2, 1st Floor, 12711, South West of D-1, Phase 1, Sector 10, Gurgaon - 122003 (Delhi/NCR) India
 Contact No. 992042424, 992042424, 992042424. Email: info@sropro.com, sropro@gmail.com, sropro@protonmail.com

TEST REPORT

Stack Emission Analysis

Test Report No. : EKO/143/080621

Issue Date : 12/06/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
 Village - Gwal Pahari,
 Gurgaon Faridabad Road
 Gurugram Haryana- 122003

Sample Description : Stack Emission
 Sample Drawn on : 07/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj kumar)
 Sample Received on : 08/06/2021
 Time of Sampling (minutes) : 30.0
 Sampling Location : BLDG-03
 Sampling Plan & Procedure : SOP-SE/09
 Analysis Duration : 08/06/2021 To 12/06/2021
 Source of Emission : St. Att. To DG Set No.13 (Englne.No. 25394204)
 Capacity : 2000 KVA
 Operating Load : Normal
 Normal Operation Schedule : As per requirement
 Type of Stack : Metal/Circular
 Diameter of Stack (meter) : 0.4
 Height of Stack from Ground Level (meter) : 31.0
 Height of Stack from Roof Level (meter) : 10.0
 Height of Sampling Location (meter) : 12.6 From Ground Level
 Type of Fuel Used : HSD
 Fuel Consumed per hour : -
 Ambient Temperature (°C) : 37.0
 Stack Temperature (°C) : 271.0
 Average Velocity of Flue Emission (m/sec) : 15.1
 Average Flow Rate (lpm) : 18.9
 Control Measures (if any) : Nil
 Remark (if any) : NA

RESULTS

S.No.	Parameters	Test Methods	Results	Units	Limits as per EPA-1996, (SI-96 Schedule-I)
1	Particulate Matter (as PM)	IS: 11256 (P-1)	52.8	mg/Nm ³	75.0
3	Oxide of Nitrogen (as NOx)	IS: 11258 (P-7)	344.3	ppmv	710.0
3	Carbon Monoxide (as CO)	USEPA (P-10)	79.1	mg/Nm ³	160.0
4	NMHC	IS: 5182 (P-21)	17.9	mg/Nm ³	100.0


Remark:- PM, NOx, NMHC & CO at 15% O₂ Correction.

Notes :

- The results given above are related to the tested sample, for various parameters, as observed at the time of Sampling. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the invoiced amount only.

** End of Report **

For SRO PRO ENGINEERS PVT. LTD.





Office & Laboratory : 204/1, 2nd Floor of E-1, Road, UPSIDC, Industrial Area, Okhla Phase - 2, New Delhi (Delhi) - 110024, India
 Contact No: 011-26103741, 26103742, 26103743, 26103744, 26103745 | Fax: 011-26103746, 26103747, 26103748, 26103749, 26103750, 26103751, 26103752

TEST REPORT

Stack Emission Analysis

Test Report No. : EKO/124/070621

Issue Date : 12/06/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
 Village - Gwal Pahari,
 Gurgaon Faridabad Road
 Gurgaon Haryana- 122003

Sample Description : Stack Emission
 Sample Drawn on : 07/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj Kumar)
 Sample Received on : 07/06/2021
 Time of Sampling (minutes) : 30.0
 Sampling Location : BLDG-03
 Sampling Plan & Procedure : SOP-SE/09
 Analysis Duration : 07/06/2021 To 11/06/2021
 Source of Emission : St. AIL To DG Set No.14 (Engine No. 25394443)
 Capacity : 2000 KVA
 Operating Load : Normal
 Normal Operation Schedule : As per requirement
 Type of Stack : Metal/Circular
 Diameter of Stack (meter) : 0.4
 Height of Stack from Ground Level (meter) : 31.0
 Height of Stack from Roof Level (meter) : 18.0
 Height of Sampling Location (meter) : 12.5 From Ground Level
 Type of Fuel Used : HSD
 Fuel Consumed per hour : -
 Ambient Temperature (°C) : 37.0
 Stack Temperature (°C) : 250.0
 Average Velocity of Flue Emission (m/sec) : 14.6
 Average Flow Rate (lpm) : 10.8
 Control Measures (if any) : Nil
 Remark (if any) : NA

RESULTS

S.No.	Parameters	Test Methods	Results	Units	Limits as per EPA-1986, (SL-96 Schedule-I)
1	Particulate Matter (as PM)	IS: 11256 (P-1)	42.9	mg/Nm ³	75.0
3	Oxide of Nitrogen (as NOx)	IS: 11255 (P-7)	335.1	ppmv	710.0
3	Carbon Monoxide (as CO)	USEPA (P-10)	63.6	mg/Nm ³	150.0
4	NMHC	IS: 6182 (P-21)	19.6	mg/Nm ³	100.0

Remark- PM, NOx, NMHC & CO at 15% O₂ Correction.

Notes :

- The results given above are related to the tested sample, for various parameters, as observed at the time of Sampling. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the invoiced amount only.

** End of Report **

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA KISHAN
 TECHNICAL MANAGER
 (Authorized Signatory)



Office & Laboratory : 3/211, Panch Sats Na 11, 1st Floor, Gurgaon Industrial Area, Gurgaon - 122003 (Haryana) INDIA
 Contact : 01294-442146/442147, 9870044207 Email: eko@ekopro.com, ekopro@gmail.com, ekopro@ekopro.com

TEST REPORT

Stack Emission Analysis

Test Report No. : EKO/123/070621

Issue Date : 12/06/2021

Issued To

: ACSI INSIGNIA SEZ PVT. LTD.
 Village - Gwal Pahari,
 Gurgaon Faridabad Road
 Gurugram Haryana- 122003

Sample Description : Stack Emission
 Sample Drawn on : 07/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj Kumar)
 Sample Received on : 07/06/2021
 Time of Sampling (minutes) : 30.0
 Sampling Location : BLDG-03
 Sampling Plan & Procedure : SOP-SF/09
 Analysis Duration : 07/06/2021 To 11/06/2021
 Source of Emission : St. Att. To DG Set No.15 (Engine No. 25394260)
 Capacity : 2000 KVA
 Operating Load : Normal
 Normal Operation Schedule : As per requirement
 Type of Stack : Metal/Circular
 Diameter of Stack (meter) : 0.4
 Height of Stack from Ground Level (meter) : 31.0
 Height of Stack from Roof Level (meter) : 18.0
 Height of Sampling Location (meter) : 12.5 From Ground Level
 Type of Fuel Used : HSD
 Fuel Consumed per hour : -
 Ambient Temperature (°C) : 37.0
 Stack Temperature (°C) : 255.0
 Average Velocity of Flue Emission (m/sec) : 14.8
 Average Flow Rate (lpm) : 19.6
 Control Measures (if any) : Nil
 Remark (if any) : NA

RESULTS

S.No.	Parameters	Test Methods	Results	Units	Limits as per EPA-1986, (SL-98 Schedule-I)
1	Particulate Matter (as PM)	IS: 11255 (P-1)	86.9	mg/Nm ³	75.0
3	Oxide of Nitrogen (as NOx)	IS: 11255 (P-7)	255.7	ppmv	710.0
3	Carbon Monoxide (as CO)	USEPA (P-10)	48.6	mg/Nm ³	150.0
4	NMHC	IS: 5182 (P-21)	20.1	mg/Nm ³	100.0

Remark: PM, NOx, NMHC & CO at 15% O₂ Correction.

Notes :

- The results given above are related to the tested sample, for various parameters, as observed at the time of Sampling. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer.
- Responsibility of the Laboratory is limited to the invoice amount only.

** End of Report **

For EKO PRO ENGINEERS PVT. LTD.

ANUJ KUMAR
 TECHNICAL MANAGER
 (Authorized Signatory)



EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory

Gurgaon, Haryana

Office & Laboratory : 2nd, 3rd, 4th, 5th & 6th Floor, UPSDC Industrial Area, Gurgaon - 122003 (Distt. Haryana)
 Contact No. 0122603002, 0122603003, 0122603004 | E-mail: eko@ekoengineers.com, eko@ekoenv.com

TEST REPORT

Noise Monitoring

Test Report No. : EKO/NA/020521

Issue Date : 03/08/2021

Issued To :

ASF INSIGNIA SEZ PVT. LTD.

Village- Gwal Bahari,
 Gurgaon Faridabad Road,
 Gurbigram Haryana-122003

Sample Description : Ambient Noise
 Sample Drawn on : 02/08/2021
 Sample Drawn by : EPEPL (Mr. Anuj Kumar)
 Sample Received on : 02/08/2021
 Sampling Location : Cafeteria Area
 Sampling Plan & Procedure : SOP-N/01
 Weather Condition : Normal
 Analysis Duration : 02/08/2021 To 03/08/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per "The Noise Pollution (Regulation & Control) Rules, 2000"
1	Leq	EKO/CHEM/SOP/S/N-01	63.6	dBS (A)	75.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA CHAUHAN
 TECHNICAL MANAGER
 (Authorized Signatory)



Office & Laboratory : 2741, Panch Sati, G.T. Road, Wazirpur, Industrial Area, Ghaziabad - 201 008 (Distt-NCT of Delhi)
 Contact No: 0182309427, 0182309428, 01221-4167 E-mail: eko@eko-pro.com, ekoengineers@gmail.com, eko@eko-pro.com

TEST REPORT

Ambient Air Quality Monitoring

Test Report No. : EKO/122/070621

Issue Date : 12/06/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
 Village - Gwai Pahari,
 Gurgaon Faridabad Road
 Gurugram Haryana- 122003

Sample Description : Ambient Air
 Sample Drawn on : 05/06/2021 To 06/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj kumar)
 Sample Received on : 07/06/2021
 Sampling Location : Near Konark Area
 Sampling Time : 24.0 Hrs.
 Sampling Plan & Procedure : SOI³-AAQ/15
 Analysis Duration : 07/06/2021 To 11/06/2021
 Ambient Temperature (°C) : 37.0
 Average Flow Rate of SPM (m³/min.) : 1.1
 Average Flow Rate of Gases (lpm) : 1.0
 Weather Conditions : Clear
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB Notification, 18th Nov 2009
1	Particulate Matter (PM10)	IS: 5182 (P-23)	130.0	µg/m ³	100.0
2	Particulate Matter (PM2.5)	EKO/CHEM/SOP/AAQ-01	53.1	µg/m ³	60.0
3	Sulphur Dioxide (as SO ₂)	IS: 5182 (P-2)	10.5	µg/m ³	60.0
4	Nitrogen Dioxide (as NO ₂)	IS: 5182 (P-6)	15.2	µg/m ³	80.0
5	Carbon Monoxide (as CO)	IS: 5182 (P-10)	0.74	mg/m ³	4.0

Notes :




- The results given above are related to the tested sample, for various parameters, as observed at the time of Sampling. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.


** End of Report **




For EKO PRO ENGINEERS PVT. LTD.




SPURNIMA CHALIAN
 TECHNICAL MANAGER
 (Authorized Signatory)




PHOTOGRAPH OF RAIN WATER HARVESTING PITS AT ASF INSIGNIA SEZ PVT. LTD

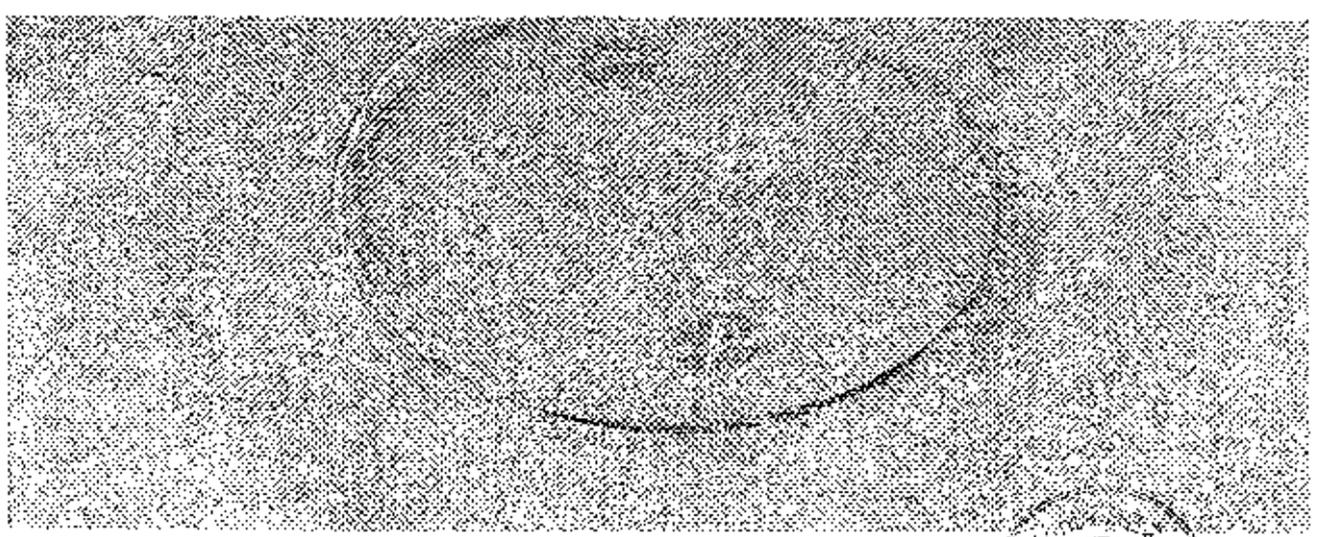
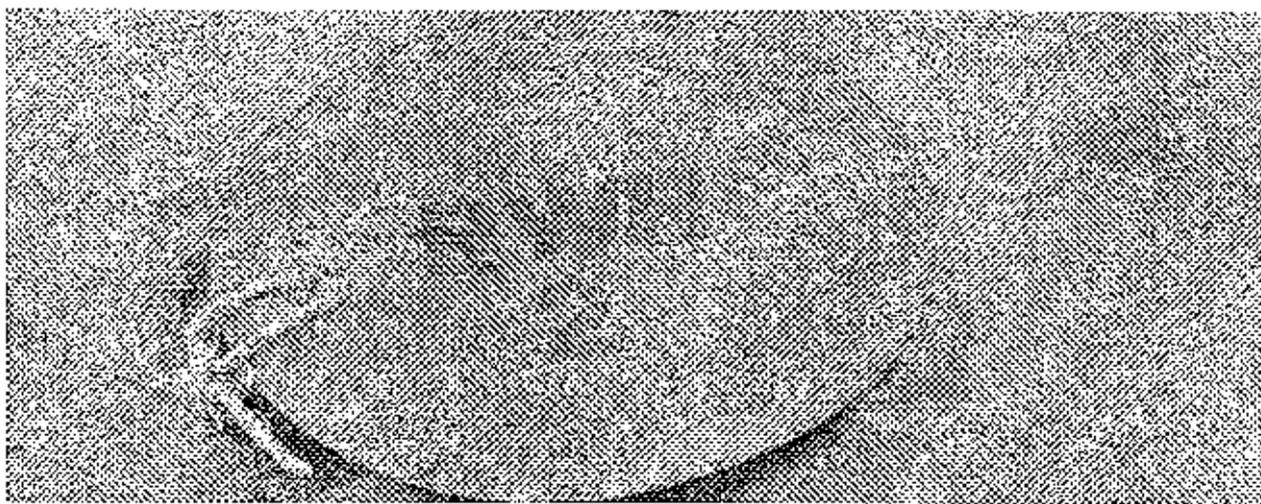
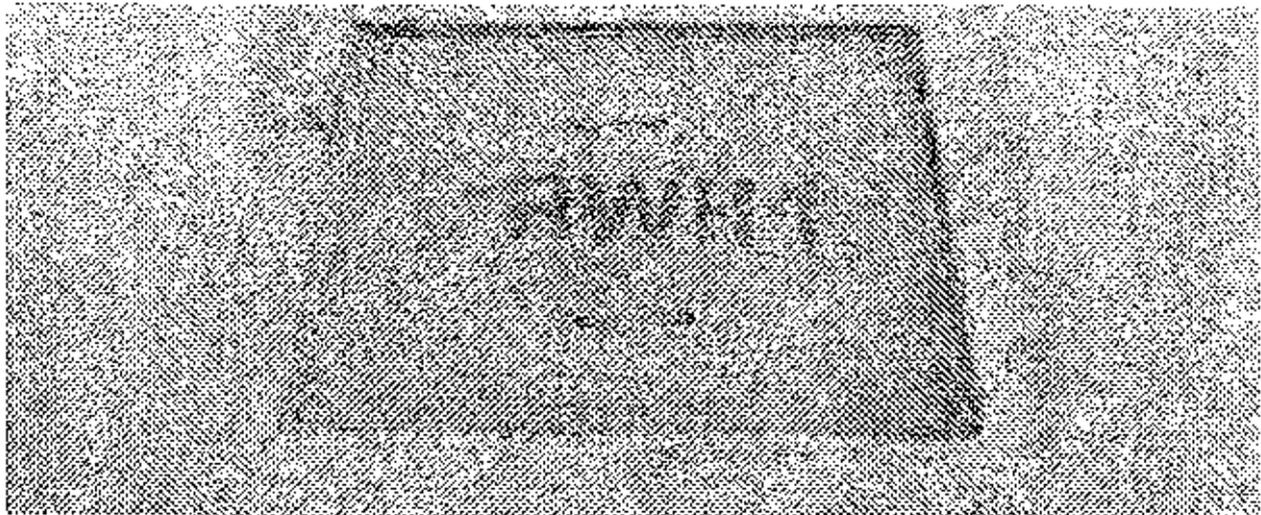




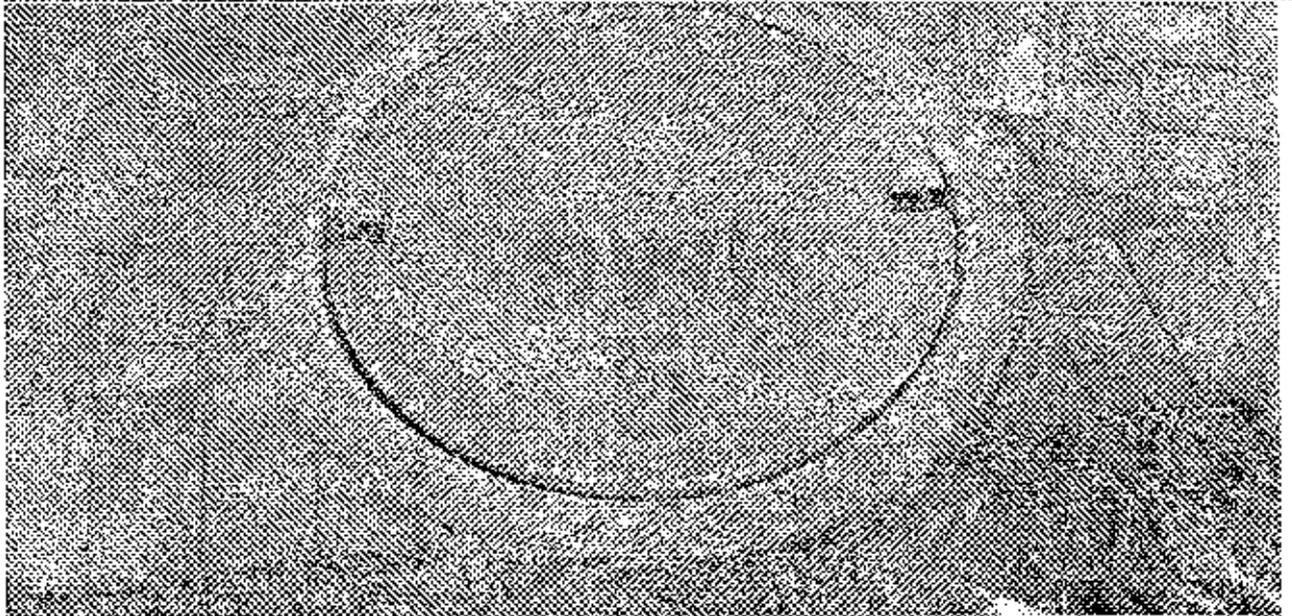


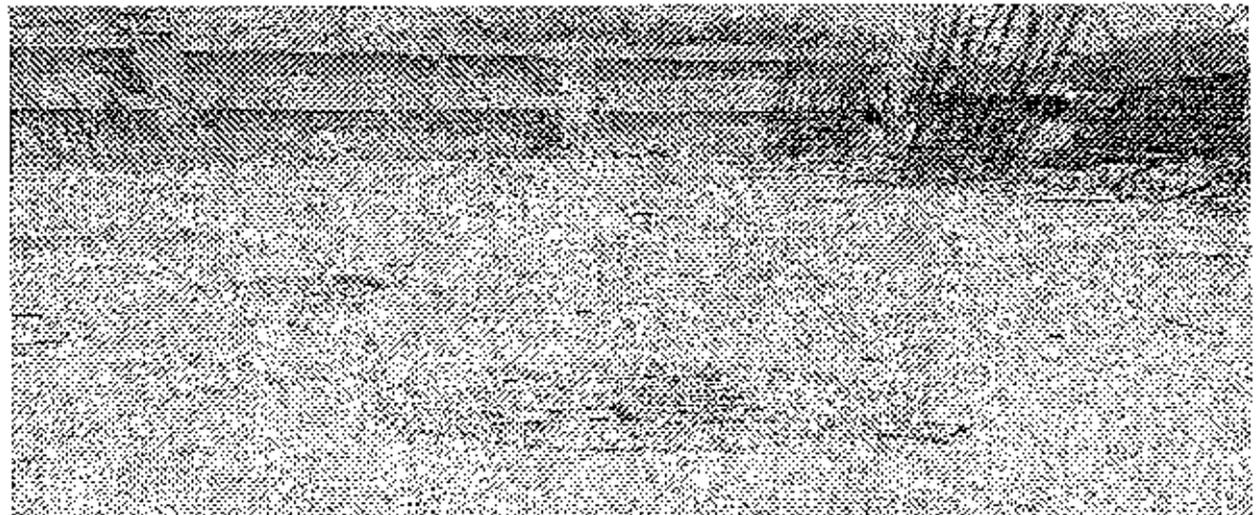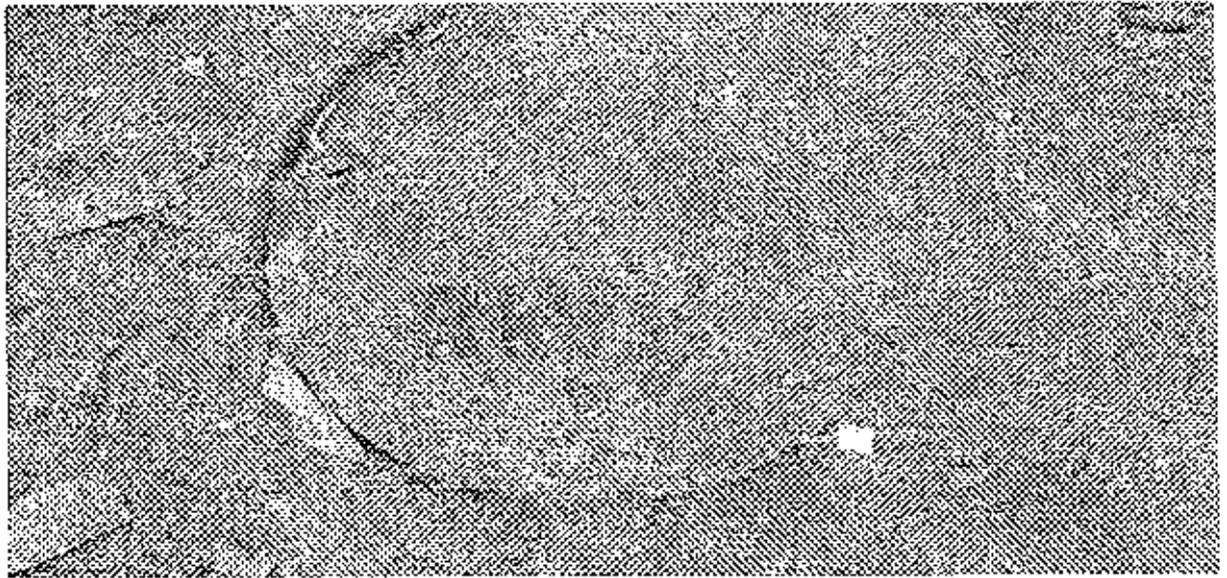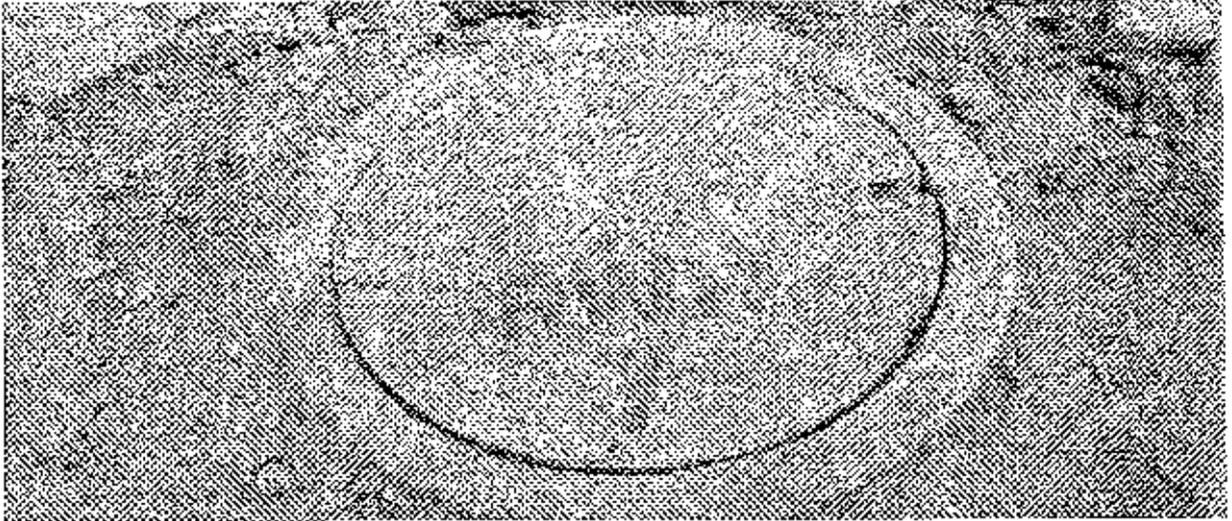


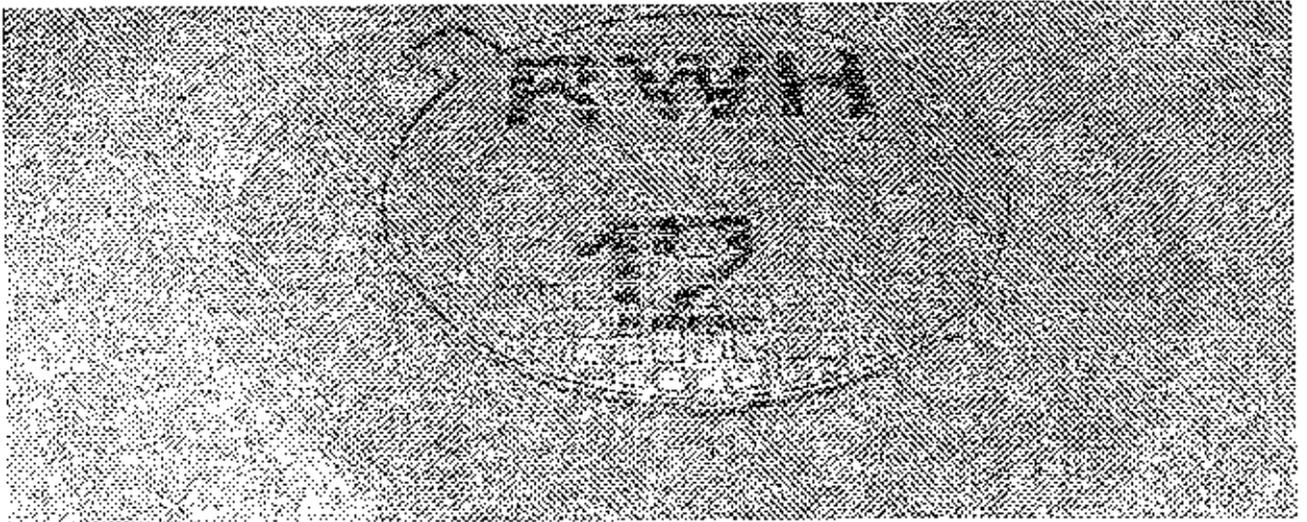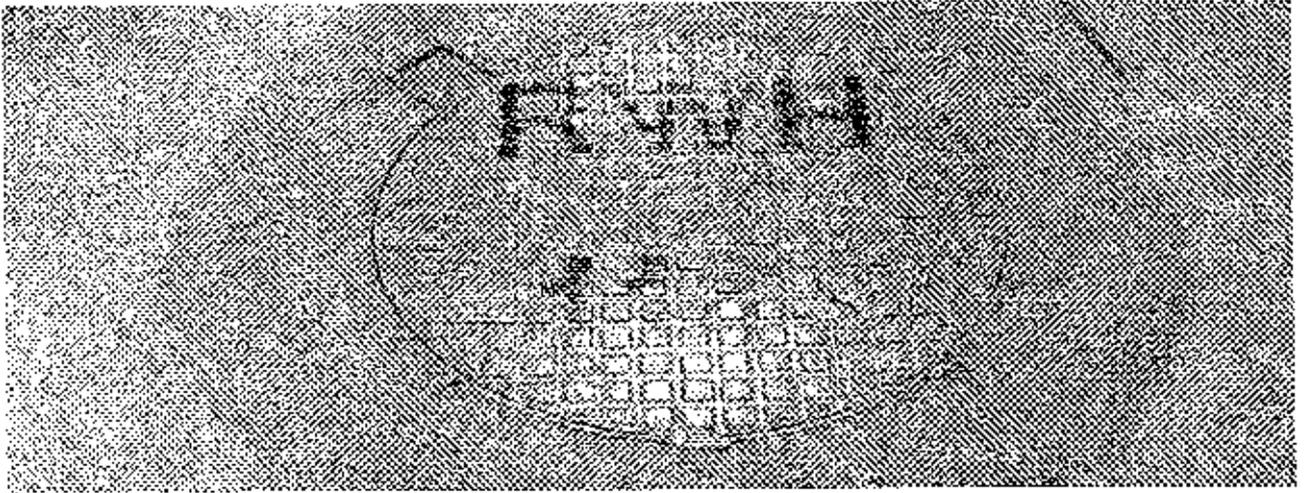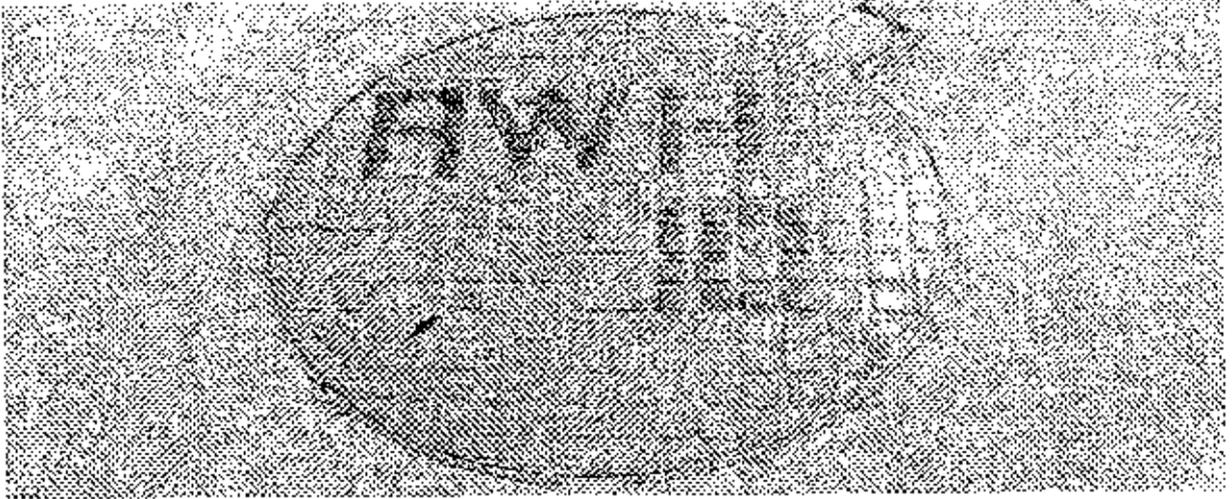

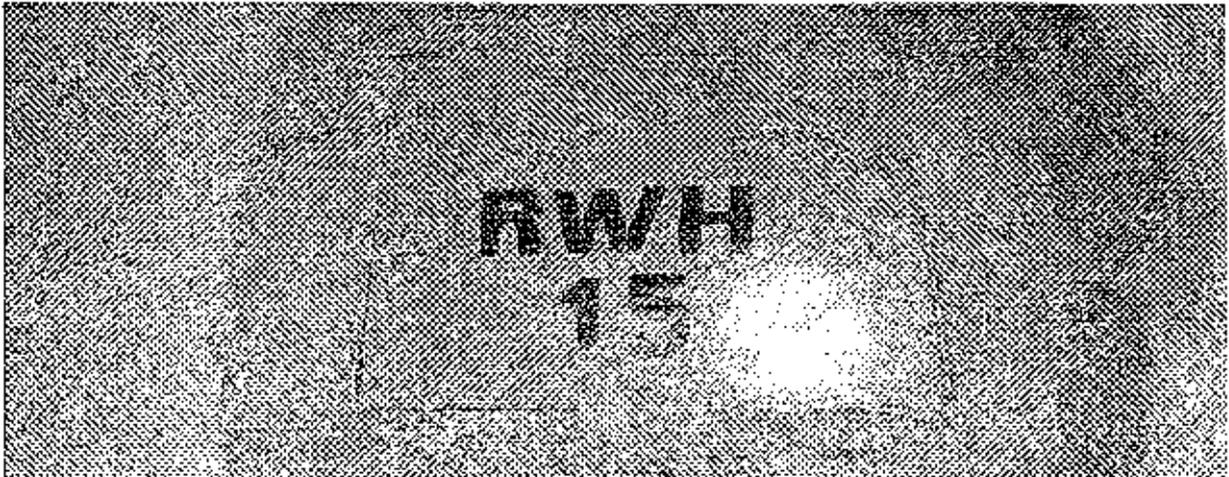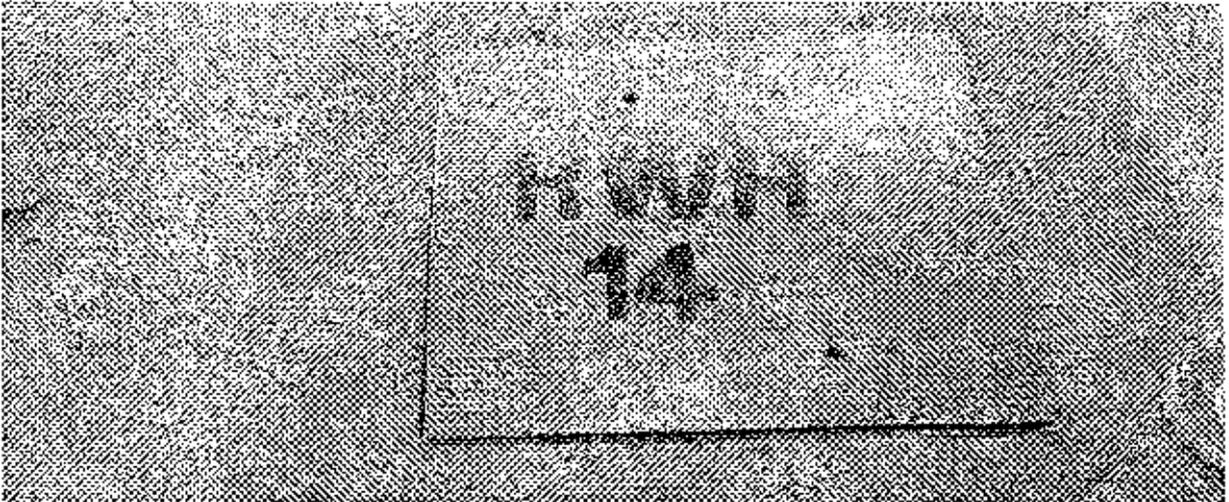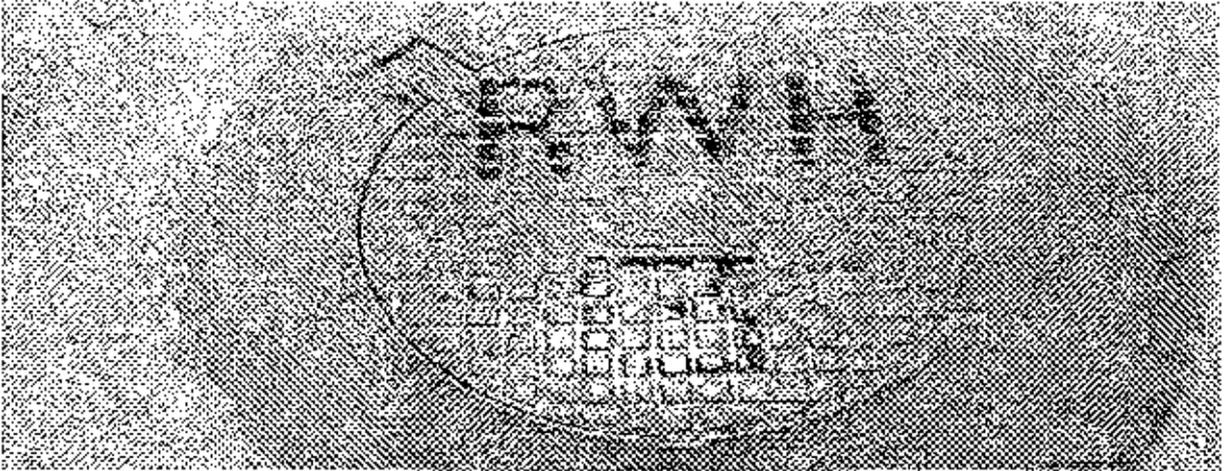


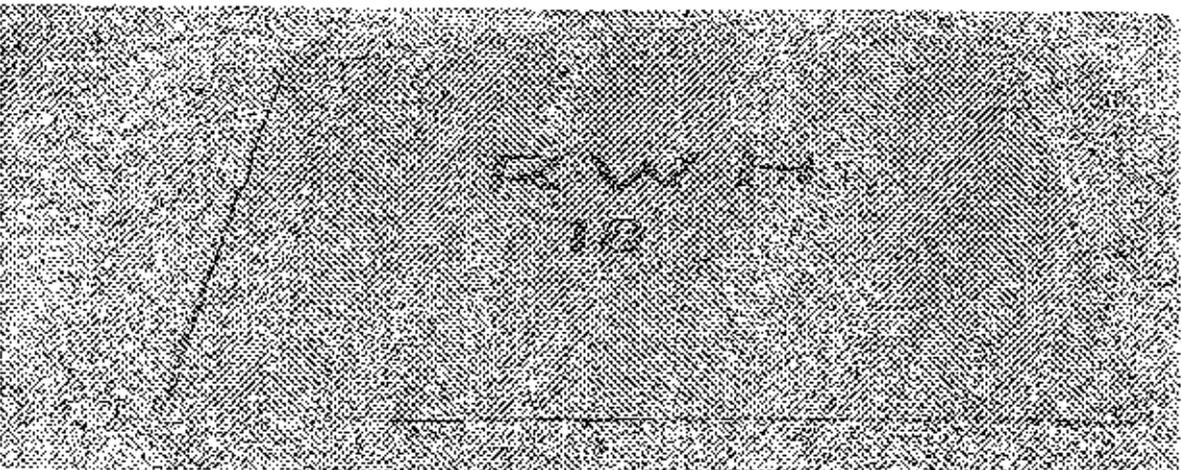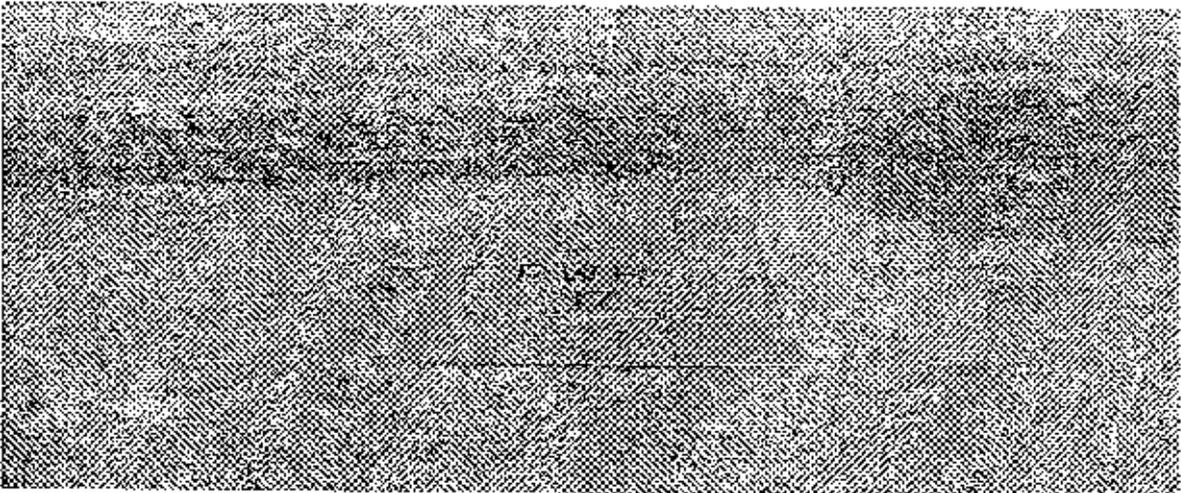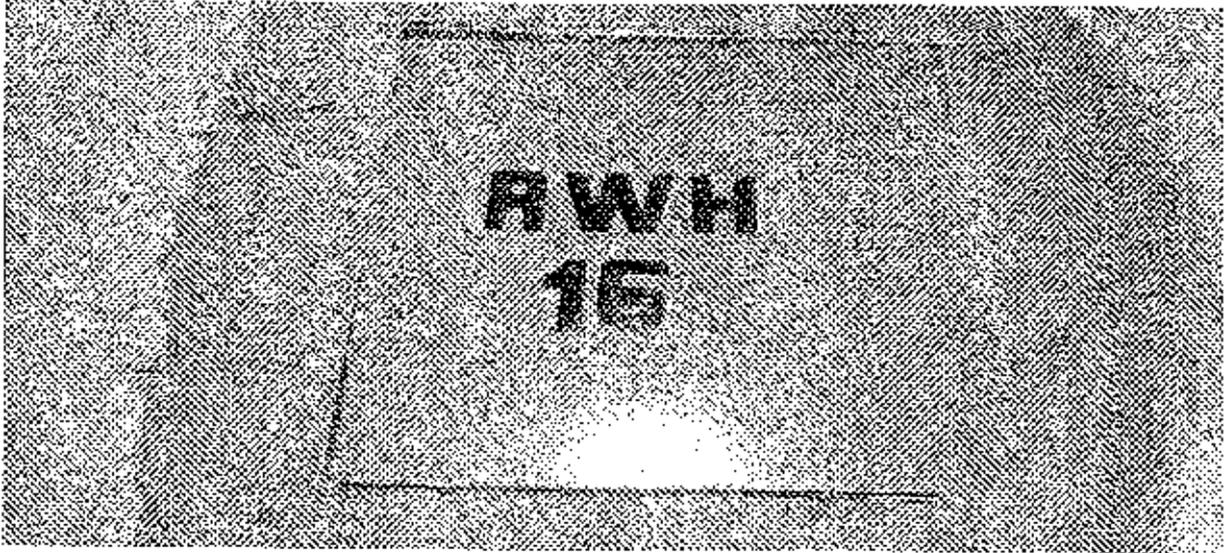

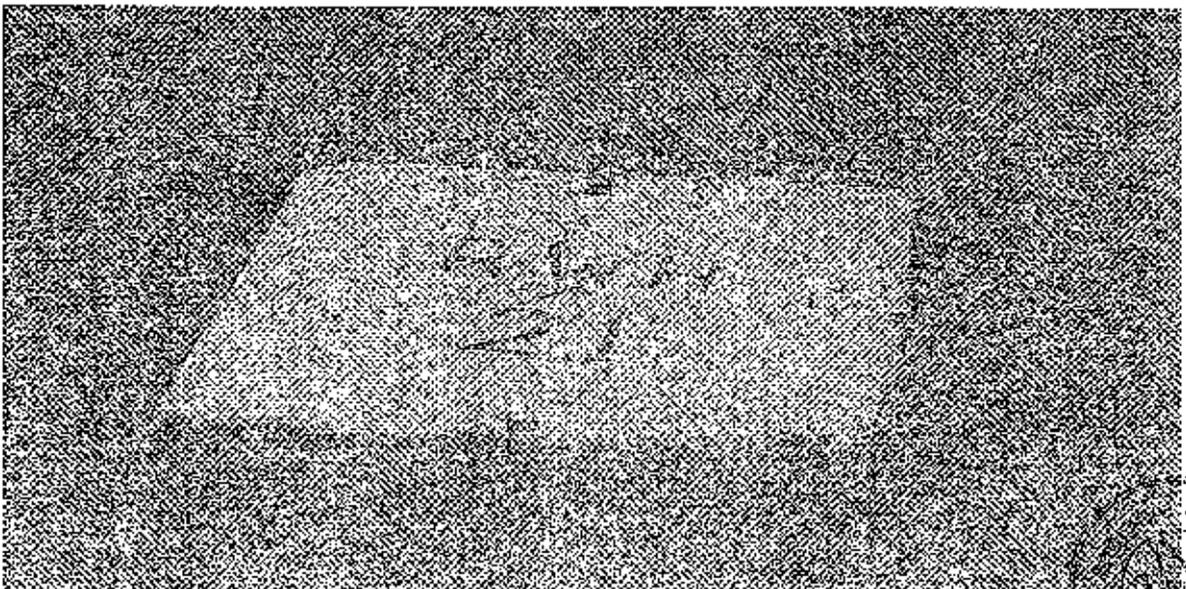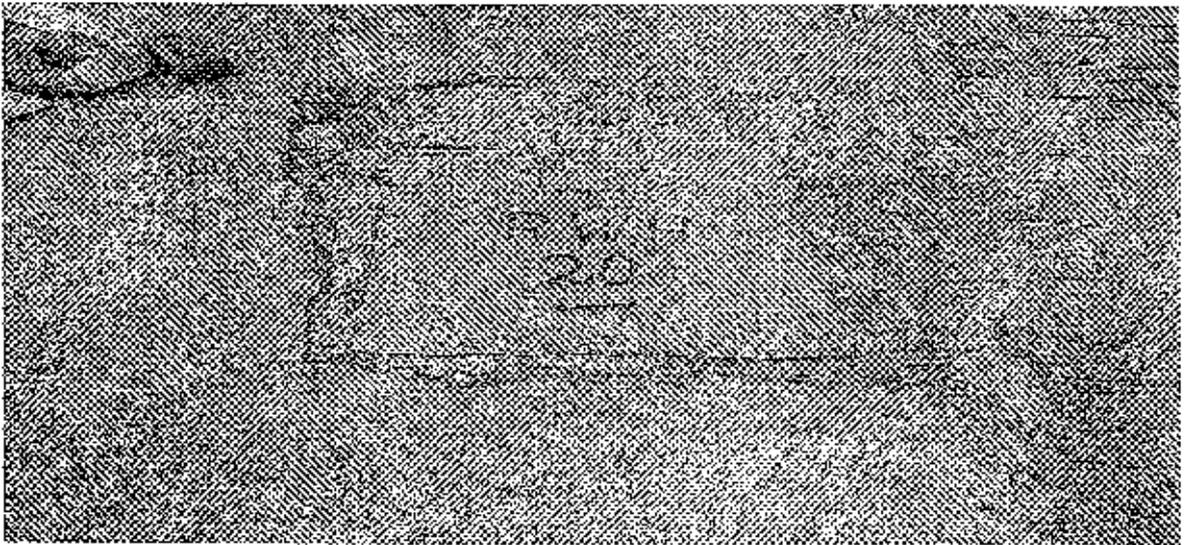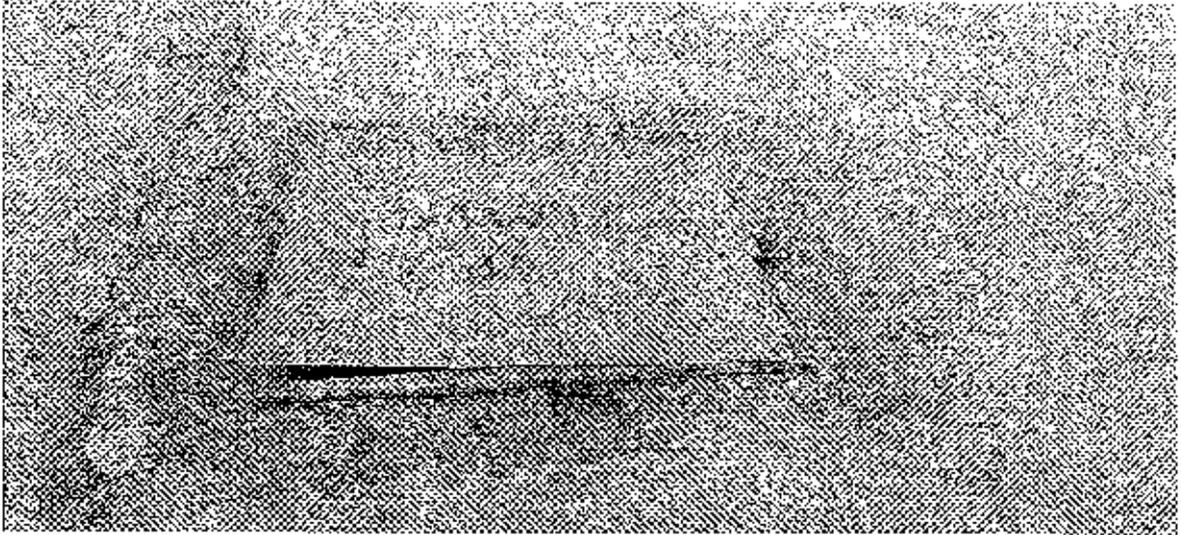

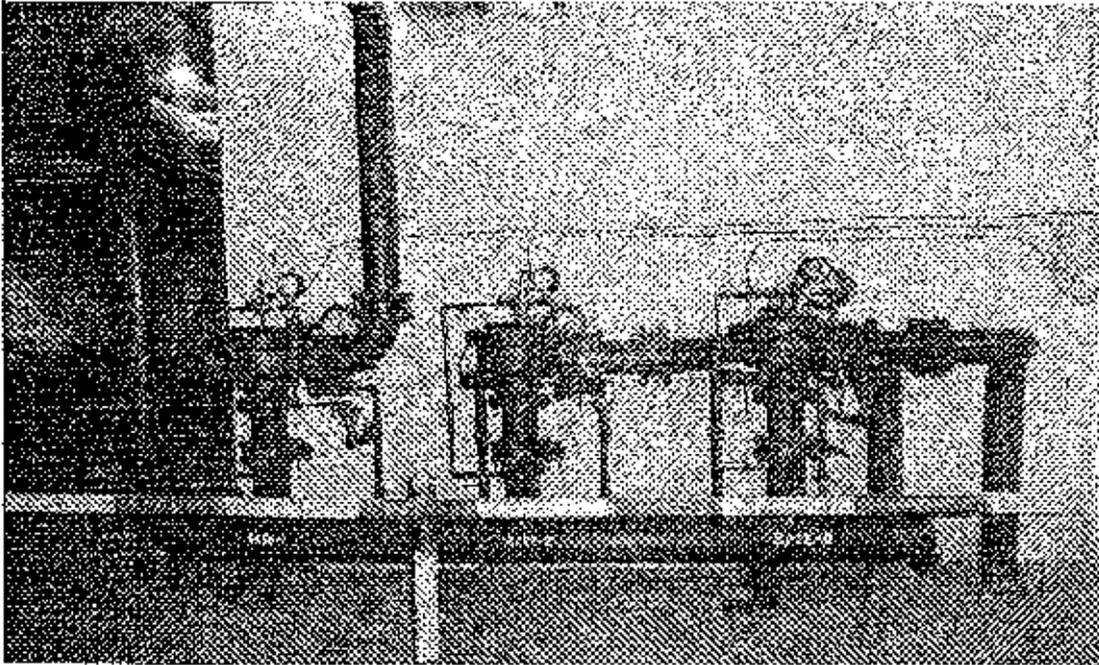


DELUGE SYSTEM FOR AUTOMATED WATER CURTAIN

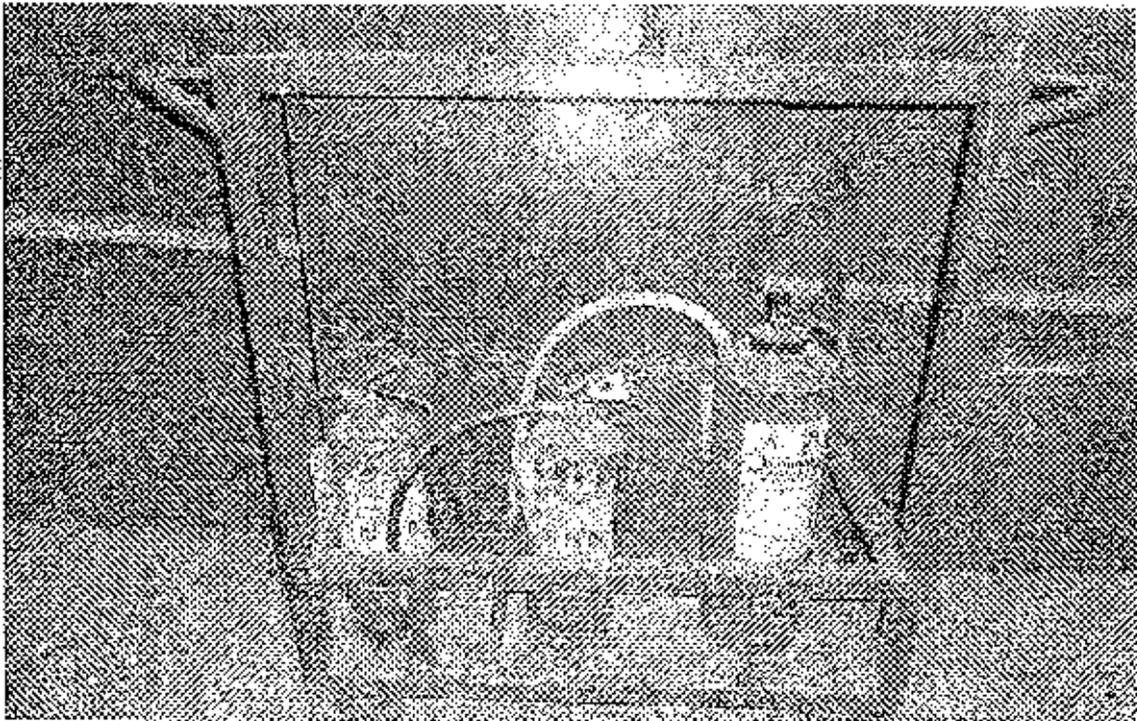

PORTABLE EXTINGUISHERS ON TROLLEY



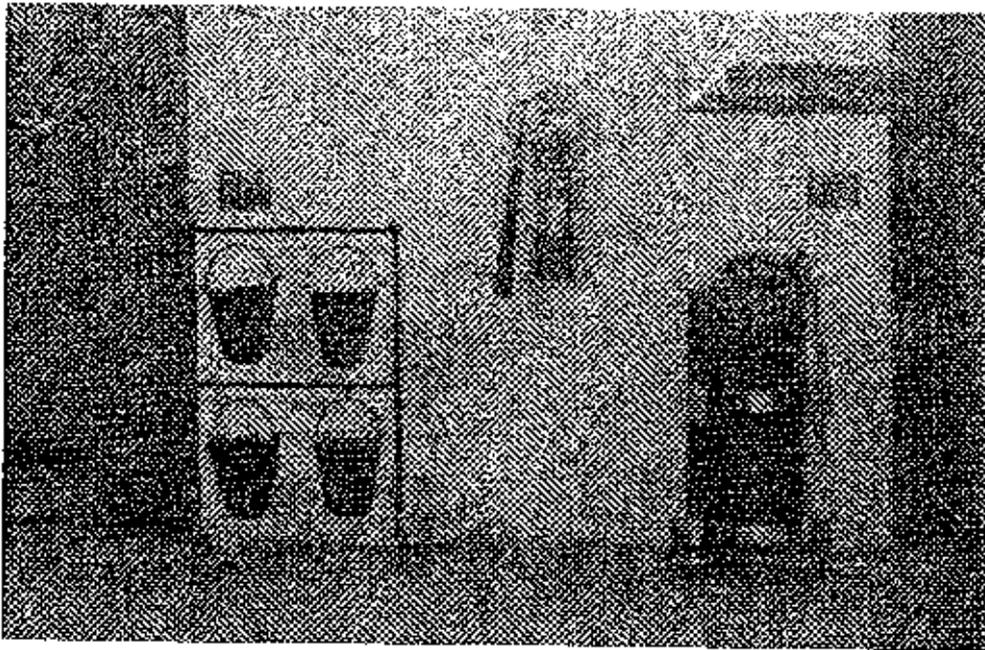


SAND BUCKET WITH FIRE EXTINGUISHER




FIRE TENDER AND AMBULANCE



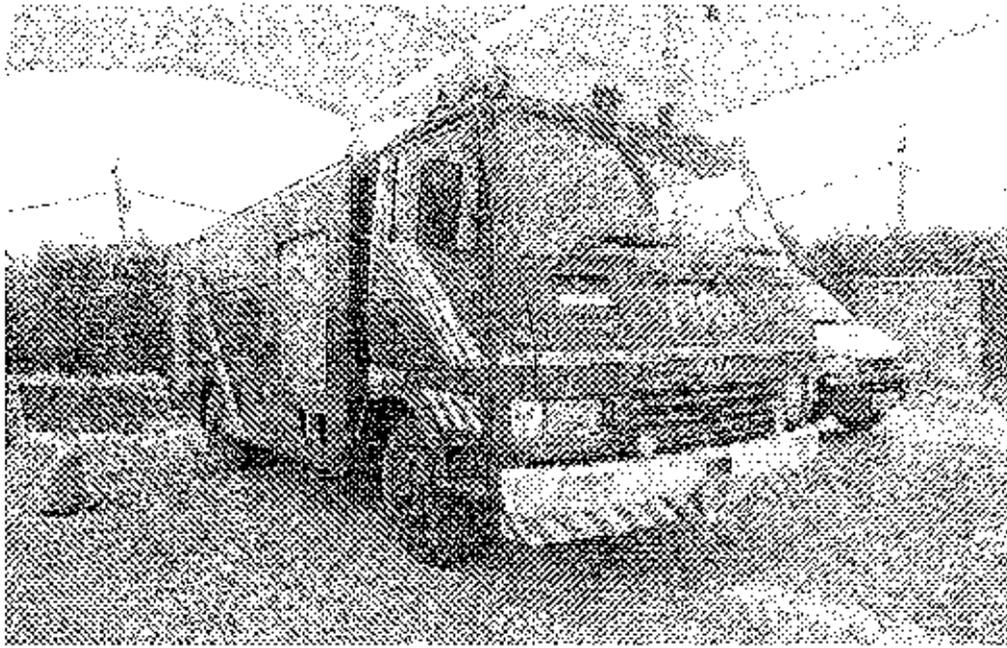


FIRE TENDER

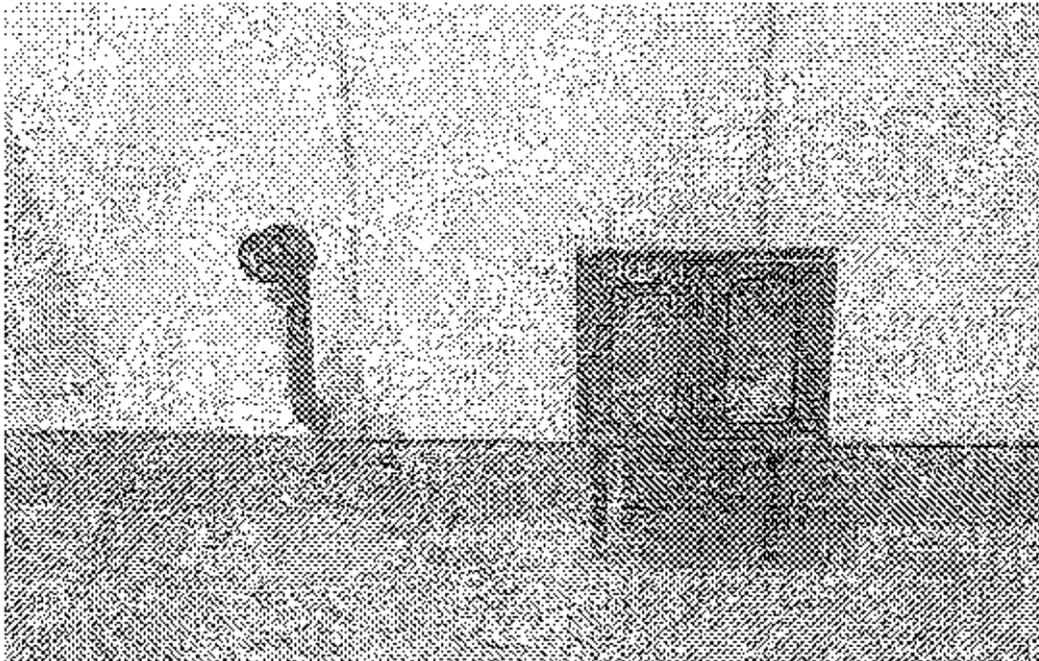

EXTERNAL FIRE HYDRANT



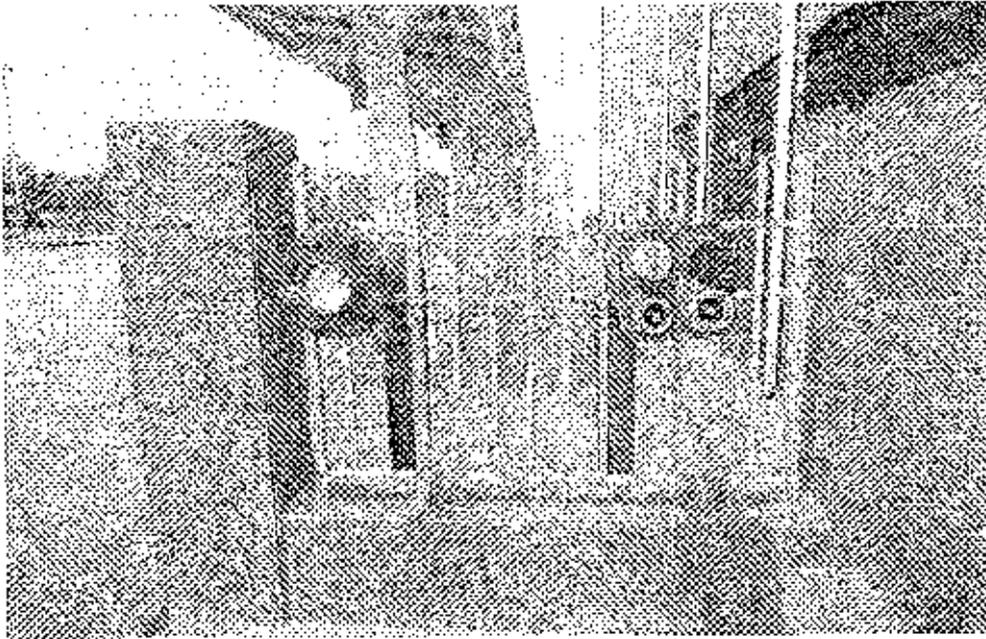


DRAW IN - DRAW OUT CONNECTION




FHC



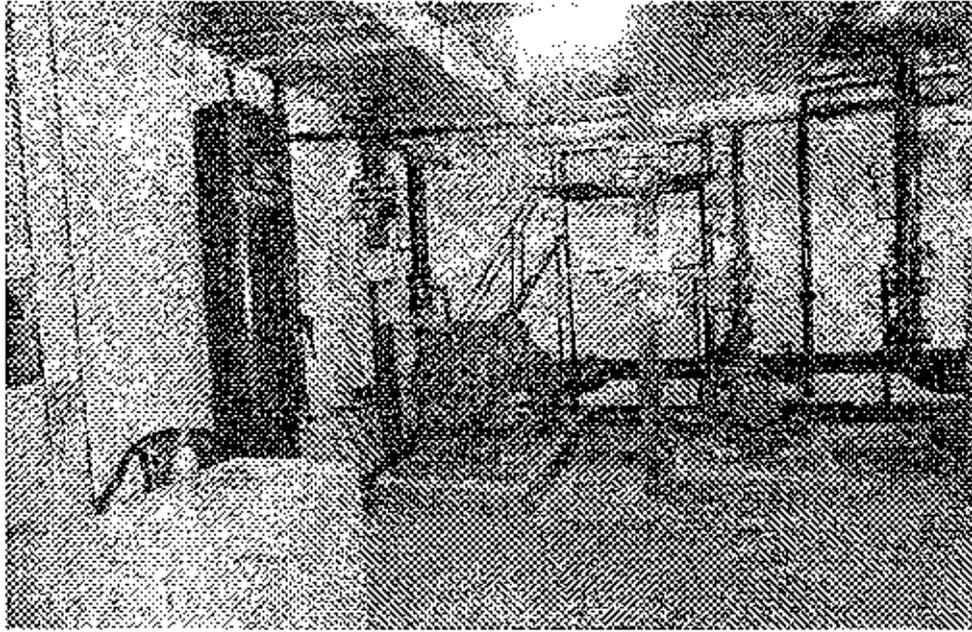


FIRE PUMP ROOM

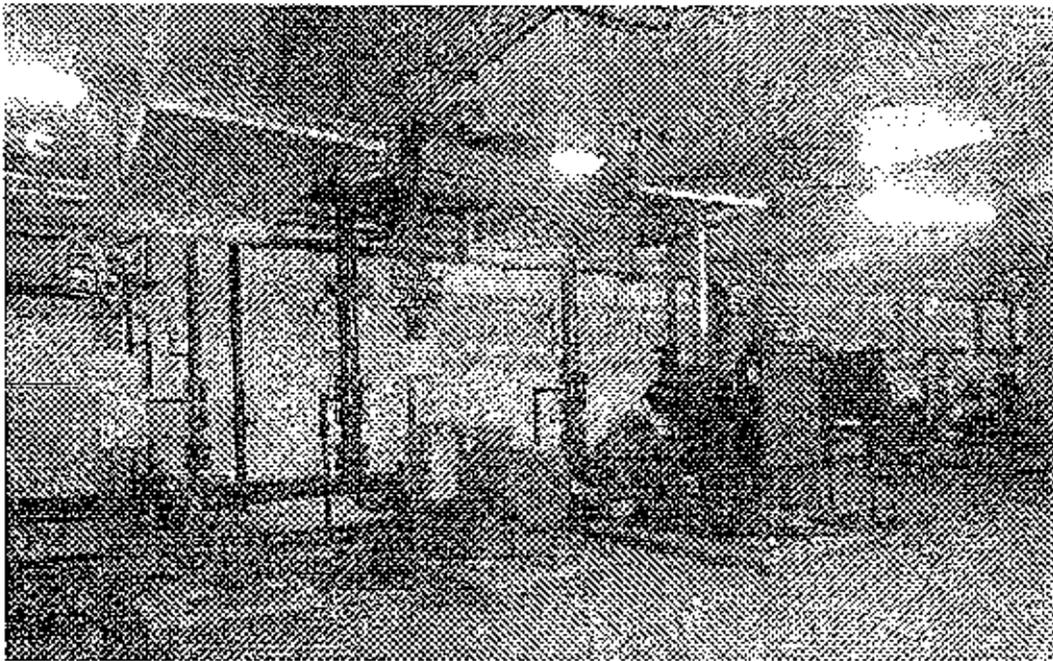


FIRE PUMP ROOM WITH DG BACK-UP



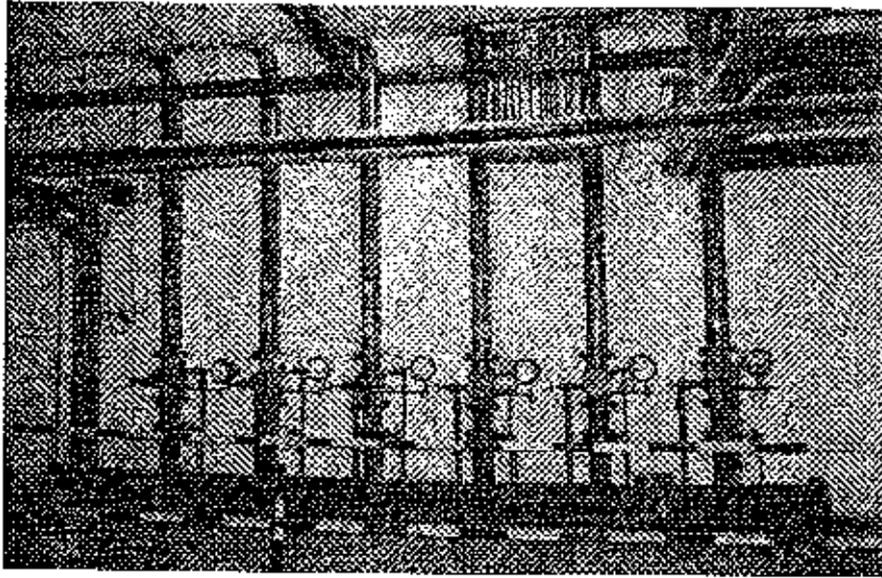

ACV FOR AUTOMATED SPRINKLER



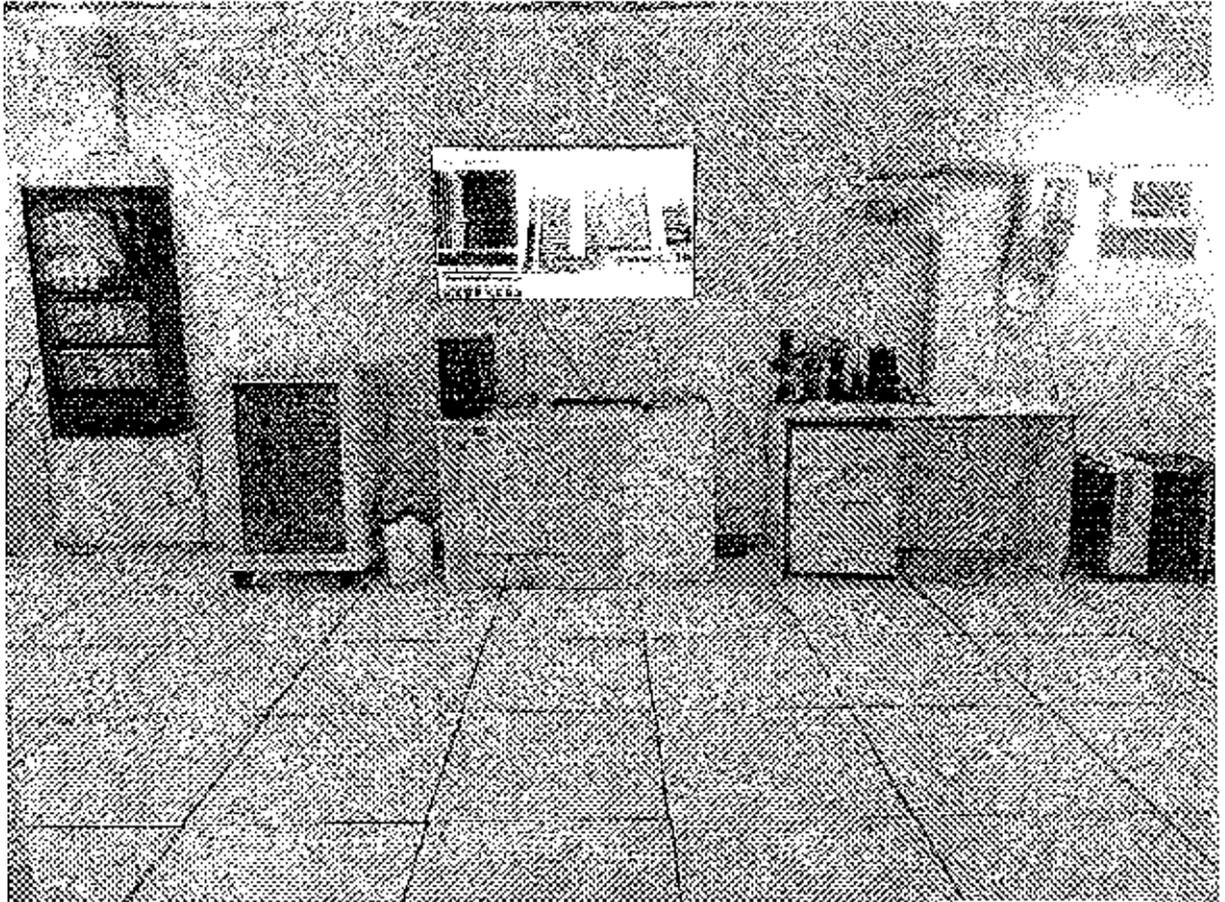

FIRE CONTROL ROOM





HARYANA STATE POLLUTION CONTROL
BOARD

Gurgaon North Vikas Sadan, 1st Floor, Near DC
Court, Gurgaon Ph.0124-2332775 Email:-
hspcbrogrn@gmail.com
E-mail: hspcb@hry.nic.in

No. HSPCB/Consent/ : 320303321GUNOCTO15794928

Dated:04/10/2021

To.

M/s :ASF INSIGNIA SEZ PVT. LTD. Building B2, Kings Canyon Sez Pvt. Ltd
Village Gwal Pahari, Gurgaon - Faridabad Road, Tehsil Sohna, District. Gurgaon

Subject: Grant of consent to operate to M/s ASF INSIGNIA SEZ PVT. LTD. Building B2,
Kings Canyon Sez Pvt. Ltd.

Please refer to your application no. 15794928 received on dated 2021-09-08 in
regional office Gurgaon North. With reference to your above application for consent to
operate, M/s ASF INSIGNIA SEZ PVT. LTD. Building B2, Kings Canyon Sez Pvt. Ltd is here
by granted consent as per following specification/Terms and conditions.

Consent Under	BOTH
Period of consent	01/10/2021 - 30/09/2022
Industry Type	Industrial estates/ parks / complexes/ areas/ export processing zones/ SEZs/ Biotech parks/ leather complex
Category	RED
Investment(In Lakh)	55912.0
Total Land Area(Sq. meter)	15131.0
Total Builtup Area(Sq. meter)	94669.0
Quantity of effluent	
1. Trade	0.0 KL/Day
2. Domestic	271.0 KL/Day
Number of outlets	1.0
Mode of discharge	
1. Domestic	Recycling/reuse
2. Trade	
Domestic Effluent Parameters	
1. BOD	30 mg/l
2. COD	250 mg/l
3. TSS	100 mg/l
4. O and G	10 mg/l
Trade Effluent Parameters	
1. NA	
Number of stacks	5
Height of stack	

1 . S T A C K ATTACHED TO DG SET NO 6	6 Meter above roof level
2 . S T A C K ATTACHED TO DG SET NO 7	6 Meter above roof level
3 . S T A C K ATTACHED TO DG SET NO 8	6 Meter above roof level
4 . S T A C K ATTACHED TO DG SET NO 9	6 Meter above roof level
5 . S T A C K ATTACHED TO DG SET NO 10	6 Meter above roof level
Emission parameters	
1. NA	
Product Details	
1. NA	Metric Tonnes/day
Capacity of boiler	
1. NA	Ton/hr.
Type of Furnace	
1. NA	
Type of Fuel	
1. Diesel	2.93 KI/day
Raw Material Details	
NA	Metric Tonnes/Day

*Regional Officer, Gurgaon North
Haryana State Pollution Control Board.*

Terms and conditions

1. The applicants shall maintain good house keeping both within factory and in the premises. All hose pipelines valves, storage tanks etc. shall be leak proof. In plant allowable pollutants levels, if specified by State Board should be met strictly.
2. The applicant/company shall comply with and carry out directive/orders issued by the Board in this consent order at all subsequent times without negligence of his /its part. The applicant/company shall be liable for such legal action against him as per provision of the law/act in case of violation of any order/directives. Issued at any time and or non compliance of the terms and conditions of his consent order.
3. The applicant shall make an application for grant of consent at least 90 days before the date of expiry of this consent.
4. Necessary fee as prescribed for obtaining renewal consent shall be paid by the applicant alongwith the consent application.
5. If due to any technological improvement or otherwise this Board is of opinion that all or any of the conditions referred to above required variation (including the change of any control equipment either in whole or in part) this Board shall after giving the applicant an opportunity of being heard vary all or such condition and there upon the applicant shall be bound to comply

with the conditions so varied.

6. The industry shall provide adequate arrangement for fighting the accidental leakages, discharge of any pollutants gas/liquids from the vessels, mechanical equipment etc. which are likely to cause environment pollution.
7. The industry shall comply noise pollution (Regulation and control) Rules, 2000.
8. The industry shall comply all the direction/Rules/Instructions as may be issued by the MOEF/CPCB/HSPCB from time to time.
9. The industry shall ensure that various characteristics of the effluents remain within the tolerance limits as specified in EPA Standard and as amended from time to time and at no time the concentration of any characteristics should exceed these limits for discharge.
10. The industry would immediately submit the revised application to the Board in the event of any change in the raw material in process, mode of treatment/discharge of effluent. In case of change of process at any stage during the consent period, the industry shall submit fresh consent application alongwith the consent to operate fee, if found due, which may be on any account and that shall be paid by the industry and the industry would immediately submit the consent application to the Board in the event of any change during the year in the raw material, quantity, quality of the effluent, mode of discharge, treatment facilities etc.
11. The officer/official of the Board shall reserve the right to access for the inspection of the industry in connection with the various process and the treatment facilities. The consent to operate is subject to review by the Board at any time.
12. Permissible limits for any pollutants mentioned in the consent to operate order should not exceed the concentration permitted in the effluent by the Board.
13. The industry shall pay the balance fee, in case it is found due from the industry at any time later on.
14. If the industry fails to adhere to any of the conditions of this consent to operate order, the consent to operate so granted shall automatically lapse.
15. If the industry is closed temporarily at its own, they shall inform the Board and obtain permission before restart of the unit.
16. The industry shall comply all the Directions/ Rules/Instructions issued from time to time by the Board.

Specific Conditions :

1. Unit will run and maintain it's STP/ETP/APCM regularly and properly, will provide separate energy meter on their STP/ETP/APCM and maintain the Log Book for energy consumption of STP/ETP/APCM and chemicals used daily for the STP/ETP.
2. That the unit shall keep all the parameters within the prescribed limits and shall comply with all the Norms and Rules as prescribed in the Act.
3. That the unit will adopt cleaner technology thereby reducing pollution load.
4. That the unit will provide inter locking arrangement of D/G set with STP/ETP/APCM and shall have separate D.G. set to ensure regular and effective running of pollution control devices.
5. That the unit will not discharge any untreated effluent inside and outside its premises.
6. Unit will provide separate flow meter at Inlet/ Outlet of STP/ETP for which separate log book will be maintained if required.
7. That the unit will not add any air polluting process/ machinery and also not to add any process which increases the water pollution load.
8. That the unit will comply with all the provisions of Hazardous Waste Rules and submit return under HWM Rules on yearly basis.
9. That the CTO so granted shall become invalid in case of violation of any of the above / any law of the land.
10. Unit will apply for

~~consent to operate for further period 90 days before expiry of this consent otherwise penalty~~ will be imposed as per policy. 11. Unit will submit compliance report of general & specific conditions mentioned in CTO alongwith fresh analysis report within 03 months. 12. Unit will install Emission control measures on DG set of capacity more than 500 KVA, having minimum specified PM capturing efficiency of atleast 70% approved by CPCB recognized labs or shift to gas based generator in compliance of HSPCB office order no. 4230-44 dated 25.06.2020. 13. Unit will deposit any balance CTE/CTO fee, if found at any stage and time.

KULDEEP SINGH Digitally Signed by KULDEEP SINGH
Date: 2021.10.04 09:53:41 +05:30
Regional Officer, Gurgaon North
Haryana State Pollution Control Board.





Haryana State Pollution Control Board
Gurgaon North Vikas Sadan, 1st Floor, Near DC Court, Gurgaon Ph.0124-
2332775 Email:- hspcborgn@gmail.com



No. :HWM/GUNO/2021/7322205

DT: 04/10/2021

To

M/s ASF INSIGNIA SEZ PVT. LTD. Building B2, Kings Canyon Sez Pvt. Ltd
Village Gwal Pahari, Gurgaon - Faridabad Road, Tehsil Sohna, District. Gurgaon
Gurgaon north

Sub: Grant of Authorization under Hazardous and Other Wastes(Management & Transboundary Movement) Rules, 2016

1. Reference of application:7322205 dated: 04/10/2021
2. Anil Sharma of ASF INSIGNIA SEZ PVT. LTD. Building B2, Kings Canyon Sez Pvt. Ltd is hereby granted an authorization for generation on the premises situated at Village Gwal Pahari, Gurgaon - Faridabad Road, Tehsil Sohna, District. Gurgaon

HARYANA STATE
Details of Authorization

S.No.	Name of process and Category of Hazardous Waste as per the Schedules I, II and III of these rules	Authorised mode of disposal or recycling or utilisation or co-processing, etc.	Quantity
1	Used oil and waste oil	approved used oil recycler.	6.16 KL/Annun

1. The authorization shall be valid for a period of 01/10/2021 to 30/09/2022
2. The authorization is subject to the following general and specific conditions :-
 - (i) 1. The unit will submit the analysis reports of effluent/air emissions/ noise, from all sources as applicable, before 30th June every year and will keep all parameters within standards prescribed under Environment (Protection) Rules, 1986. 2. The unit will submit the Annual Report under HWM Rules by 30th June and Environment Statement by 30th September every year. 3. Unit will apply for renewal of consent/Authorization at least 90 days before expiry date of the consent/Authorization. 4. The hazardous waste generated by the unit will be disposed off through authorized TSDF/recyclers / Refiners of hazardous waste. 5. Unit will comply all the applicable Law/Acts/CPCB directions under the HWM, Rules 2016 time to time, Unit will submit Annual Return under HWM, Rules timely. 6. Unit will maintain the record of storage and sold out the waste/spent oil of DG sets and same will submit in board on yearly basis. 7. That the authorization under HWM rules so granted shall become invalid in case of violation of any of the above / any law of the land.


**Regional Officer Gurgaon North
For Haryana State Pollution Control Board**

Conditions of Authorization:

1. The authorised person shall comply with the provisions of the Environment (Protection) Act, 1986, and the rules made there under.
2. The authorization or its renewal shall be produced for inspection at the request of an officer authorised by the State Pollution Control Board.
3. The person authorised shall not rent, lend, sell, transfer or otherwise transport the hazardous and other wastes except what is permitted through this authorization.
4. Any unauthorised change in personnel, equipment or working conditions as mentioned in the application by the person authorised shall constitute a breach of this authorization.
5. The person authorised shall implement Emergency Response Procedure (ERP) for which this authorization is being granted considering all site specific possible scenarios such as spillages, leakages, fire etc. and their possible impacts and also carry out mock drill in this regard at regular interval of time.
6. The person authorised shall comply with the provisions outlined in the Central Pollution Control Board guidelines on "Implementing Liabilities for Environmental Damages due to Handling and Disposal of Hazardous Waste and Penalty".
7. An application for the renewal of an authorization shall be made as laid down under these Rules.
8. Any other conditions for compliance as per the guidelines issued by the Ministry of Environment, Forest and Climate Changes or Central Pollution Control Board from time to time.
9. Annual return shall be filed by June 30th for the period ending 31st March of the year.
10. It is the duty of the authorised person to take prior permission of the State Pollution Control Board to close down the facility.
11. The imported hazardous and other wastes shall be fully insured for transit as well for any accidental occurrence and its clean-up operation.
12. The record of consignment and fate of the imported hazardous and other wastes shall be maintained.
13. The hazardous and other waste which gets generated during recycling or reuse or recovery or pre-processing or utilisation of imported hazardous or other wastes shall be treated and disposed of as per specific condition of authorisation.
14. The importer or exporter shall bear the cost of import and mitigation of damages if any.

KULDEEP SINGH Digitally signed by KULDEEP SINGH
Date: 2021.10.04 09:57:10 +05'30'

**Regional Officer Gurgaon North
For Haryana State Pollution Control Board**



HARYANA STATE POLLUTION CONTROL BOARD

Gurgaon North Vikas Sada, 1st Floor,
Near DC Court, Gurgaon Ph.0124-2332775
E-mail: hspcb.pkt@sify.com



No. HSPCB/Consent/ : 320303317GUPN/CTG/4398636

Dated:09/08/2017

To.

M/s ASF INSIGNIA SEZ PVT. LTD. Building B3
Village Gwal Pahari, Gurgaon - Faridabad Road, Tehsil Sohna, District. Gurgaon

Subject: Grant of consent to operate to M/s ASF INSIGNIA SEZ PVT. LTD. Building B3.

Please refer to your application no. 4398636 received on dated 2017-08-01 in regional office Gurgaon North. With reference to your above application for consent to operate, M/s ASF INSIGNIA SEZ PVT. LTD. Building B3 is here by granted consent as per following specification/Terms and conditions.

Consent Under	BOTH
Period of consent	01/10/2017 - 30/09/2022
Industry Type	Industrial estates/ parks / complexes/ areas/ export processing zones/ SEZs/ Biotech parks/ leather complex
Category	RED
Investment (in Lakh)	55912.5
Total Land Area (Sq. meter)	37854.29
Total Builtup Area (Sq. meter)	352379.9
Quantity of effluent	
1. Trade	0.0 KL/Day
2. Domestic	100.0 KL/Day
Number of outlets	1.0
Mode of discharge	
1. Domestic	reuse/recycle
2. Trade	0
Domestic Effluent Parameters	
1. BOD	30 mg/l
2. COD	250 mg/l
3. TSS	100 mg/l
Trade Effluent Parameters	
1. NA	0 mg/l
Number of stacks	1
Height of stack	
1. Stack to OG set	30 METER
5x2000 KVA	
Emission parameters	

L. NA	0 mg/m ³
Product Details	
L. NA	0 Metric Tonnes/day
Capacity of boiler	
L. NA	0 Tons/hr
Type of Furnace	
L. NA	0 0
Type of Fuel	
L. Diesel	1.6 KL/day
Raw Material Details	
NA	0 Metric Tonnes/Day

*Regional Officer, Gurgaon North
Haryana State Pollution Control Board.*

Terms and conditions

1. The applicants shall maintain good house keeping both within factory and in the premises. All hose pipelines valves, storage tanks etc. shall be leak proof. In plant allowable pollutants levels, if specified by State Board should be met strictly.
2. The applicant/company shall comply with and carry out directive/orders issued by the Board in this consent order at all subsequent times without negligence of his /its part. The applicant/company shall be liable for such legal action against him as per provision of the law/act in case of violation of any order/directives. Issued at any time and or non compliance of the terms and conditions of his consent order.
3. The applicant shall make an application for grant of consent at least 90 days before the date of expiry of this consent.
4. Necessary fee as prescribed for obtaining renewal consent shall be paid by the applicant alongwith the consent application.
5. If due to any technological improvement or otherwise this Board is of opinion that all or any of the conditions referred to above required variation (including the change of any control equipment either in whole or in part) this Board shall after giving the applicant an opportunity of being heard vary all or such condition and there upon the applicant shall be bound to comply with the conditions so varied.
6. The industry shall provide adequate arrangement for fighting the accidental leakages, discharge of any pollutants gas/liquids from the vessels, mechanical equipment etc. which are likely to cause environment pollution.
7. The industry shall comply noise pollution (Regulation and control) Rules, 2000.
8. The industry shall comply all the direction/Rules/instructions as may be issued by the MOEF/CPCB/HSPCB from time to time.
9. The industry shall ensure that various characteristics of the effluents remain within the tolerance limits as specified in EPA Standard and as amended from time to time and at no time the concentration of any characteristics should exceed these limits for discharge.
10. The industry would immediately submit the revised application to the Board in the event of any change in the raw material in process, mode of treatment/discharge of effluent. In case of change of process at any stage during the consent period, the industry shall submit fresh

consent application alongwith the consent to operate fee, if found due, which may be on any account and that shall be paid by the industry and the industry would immediately submit the consent application to the Board in the event of any change during the year in the raw material, quantity, quality of the effluent, mode of discharge, treatment facilities etc.

11. The officer/official of the Board shall reserve the right to access for the inspection of the industry in connection with the various process and the treatment facilities. The consent to operate is subject to review by the Board at any time.

12. Permissible limits for any pollutants mentioned in the consent to operate order should not exceed the concentration permitted in the effluent by the Board.

13. The industry shall pay the balance fee, in case it is found due from the industry at any time later on.

14. If the industry fails to adhere to any of the conditions of this consent to operate order, the consent to operate so granted shall automatically lapse.

15. If the industry is closed temporarily at its own, they shall inform the Board and obtain permission before restart of the unit.

16. The industry shall comply all the Directions/ Rules/Instructions issued from time to time by the Board.

Specific Conditions :

1. The unit will submit the analysis reports of trade effluent/air emissions/ noise, from all sources as applicable, before 30th June every year and will keep all parameters with in standards prescribed under Environment (Protection) Rules, 1986. 2. The unit will submit the Annual Report under HWM Rules by 30th June and Environment Statement by 30th September every year. 3. Unit will submit fresh balance sheet/ CA certificate regarding capital investment cost of the unit on land, building, plant and machinery without depreciation and will also deposit balance consent fee if any found due as per latest balance sheet/ CA certificate, by 30th September every year. 4. Unit will apply for renewal of consent/Authorization at least 90 days before expiry date of the consent/Authorization. 5. The hazardous waste generated by the unit in the form of used/spent oil will be sold only to authorized recyclers / Refiners of hazardous waste.

*Regional Officer, Gurgaon North
Haryana State Pollution Control Board.*



Haryana State Pollution Control Board
Gurgaon North Vikas Sadan, 1st Floor, Near DC Court, Gurgaon Ph.0124-
2332775 Email:- hspcbgrn@gmail.com



No. :HWM/GUNO/2020/4707609

DT: 21/01/2020

To

M/s ASF INSIGNIA SEZ PVT. LTD. Building B3
Village Gwal Pahari, Gurgaon - Faridabad Road, Tehsil Sohna, District. Gurgaon
Gurgaon north

Sub: Grant of Authorization under Hazardous and Other Wastes(Management & Transboundry Movement) Rules, 2016

1. Reference of application:4707609 dated: 21/01/2020
2. ASF INSIGNIA SEZ PVT. LTD. of ASF INSIGNIA SEZ PVT. LTD. Building B3 is hereby granted an authorization for generation on the premises situated at Village Gwal Pahari, Gurgaon - Faridabad Road, Tehsil Sohna, District. Gurgaon.

HARYANA STATE
Details of Authorization

S.No.	Name of process and Category of Hazardous Waste as per the Schedules I, II and III of these rules	Authorised mode of disposal or recycling or utilisation or co-processing, etc.	Quantity
1	Industrial operations using mineral/synthetic oil as lubricant in hydraulic systems or other applications. Used/spent oil	Recovery and Reuse-Authorized recyclers.	9.4 KI/Annu m

1. The authorization shall be valid for a period of 20/12/2019 to 30/09/2022
2. The authorization is subject to the following general and specific conditions :-

- (i) 1. The unit will submit the analysis reports of effluent/air emissions/ noise, from all sources as applicable, before 30th June every year and will keep all parameters within standards prescribed under Environment (Protection) Rules, 1986. 2. The unit will submit the Annual Report under HWM Rules by 30th June and Environment Statement by 30th September every year. 3. Unit will apply for renewal of consent/Authorization at least 90 days before expiry date of the consent/Authorization. 4. The hazardous waste generated by the unit will be disposed off through authorized TSD/ recyclers / Refiners of hazardous waste. 5. Unit will comply all the applicable Law/Acts/CPCB directions under the HOWM, Rules 2016 time to time, Unit will submit Annual Return under HWM, Rules timely

Regional Officer Gurgaon North
For Haryana State Pollution Control Board

Conditions of Authorization:

1. The authorised person shall comply with the provisions of the Environment (Protection) Act, 1986, and the rules made there under.
2. The authorization or its renewal shall be produced for inspection at the request of an officer authorised by the State Pollution Control Board.
3. The person authorised shall not rent, lend, sell, transfer or otherwise transport the hazardous and other wastes except what is permitted through this authorization.
4. Any unauthorised change in personnel equipment or working conditions as mentioned in the application by the person authorised shall constitute a breach of this authorization.
5. The person authorised shall implement Emergency Response Procedure (ERP) for which this authorization is being granted considering all site specific possible scenarios such as spillages, leakages, fire etc. and their possible impacts and also carry out mock drill in this regard at regular interval of time.
6. The person authorised shall comply with the provisions outlined in the Central Pollution Control Board guidelines on "Implementing Liabilities for Environmental Damages due to Handling and Disposal of Hazardous Waste and Penalty".
7. An application for the renewal of an authorization shall be made as laid down under these Rules.
8. Any other conditions for compliance as per the guidelines issued by the Ministry of Environment, Forest and Climate Changes or Central Pollution Control Board from time to time.
9. Annual return shall be filed by June 30th for the period ending 31 st March of the year.
10. It is the duty of the authorised person to take prior permission of the State Pollution Control Board to close down the facility.
11. The imported hazardous and other wastes shall be fully insured for transit as well for any accidental occurrence and its clean-up operation.
12. The record of consumption and fate of the imported hazardous and other wastes shall be maintained.
13. The hazardous and other waste which gets generated during recycling or reuse or recovery or pre-processing or utilisation of imported hazardous or other wastes shall be treated and disposed of as per specific condition of authorisation.
14. The importer or exporter shall bear the cost of import and mitigation of damages if any.

Kuldeep Singh
Regionally signed by Kuldeep Singh
Date: 2020.01.21 09:46:50 +05'30'
Regional Officer Gurgaon North
for Haryana State Pollution Control Board



HARYANA STATE POLLUTION CONTROL BOARD

Gurgaon North Vikas Sadan, 1st Floor, Near DC Court, Gurgaon Ph.0124-2332775 Email:-

hspcbrogrn@gmail.com

E-mail: hspcb.pkl@sify.com

No. HSPCB/Consent/ : 313116320GUNOCTO6503967

Dated:09/03/2020

To.

M/s ASF Insignia SEZ Pvt. Ltd. IDR Residential

Village Gwal Pahari, Gurgaon-Faridabad Road Tehsil Wazirabad Gurugram

Subject: Grant of consent to operate to M/s ASF Insignia SEZ Pvt. Ltd. IDR Residential.

Please refer to your application no. 6503967 received on dated 2020-02-11 in regional office Gurgaon North. With reference to your above application for consent to operate, M/s ASF Insignia SEZ Pvt. Ltd. IDR Residential is hereby granted consent as per following specification/Terms and conditions.

Consent Under	BOTH
Period of consent	01/04/2020 to 31/03/2022
Industry Type	Building and construction project having quantity of waste water generation 10 KLD to 100 KLD
Category	ORANGE
Investment(In Lakh)	15825.0
Total Land Area(Sq. meter)	8558.696
Total Builtup Area(Sq. meter)	25411.62
Quantity of effluent	
1. Trade	0.0 KL/Day
2. Domestic	42.0 KL/Day
Number of outlets	1.0
Mode of discharge	
1. Domestic	Reuse/Recycle
2. Trade	0
Domestic Effluent Parameters	
1. BOD	30 mg/l
2. COD	250 mg/l
3. TSS	100 mg/l
Trade Effluent Parameters	
1. NA	
Number of stacks	1
Height of stack	
1. NA	
Emission parameters	

1. NA	
Product Details	
1. NA	Metric Tonnes/day
Capacity of boiler	
1. NA	Ton/hr
Type of Furnace	
1. NA	
Type of Fuel	
1. Electricity	KJ/day
Raw Material Details	
NA	Metric Tonnes/Day

*Regional Officer, Gurgaon North
Haryana State Pollution Control Board.*

Terms and conditions

1. The applicants shall maintain good house keeping both within factory and in the premises. All hose pipelines valves, storage tanks etc. shall be leak proof. In plant allowable pollutants levels, if specified by State Board should be met strictly.
2. The applicant/company shall comply with and carry out directive/orders issued by the Board in this consent order at all subsequent times without negligence of his /its part. The applicant/company shall be liable for such legal action against him as per provision of the law/act in case of violation of any order/directives. Issued at any time and or non compliance of the terms and conditions of his consent order.
3. The applicant shall make an application for grant of consent at least 90 days before the date of expiry of this consent.
4. Necessary fee as prescribed for obtaining renewal consent shall be paid by the applicant alongwith the consent application.
5. If due to any technological improvement or otherwise this Board is of opinion that all or any of the conditions referred to above required variation (including the change of any control equipment either in whole or in part) this Board shall after giving the applicant an opportunity of being heard vary all or such condition and there upon the applicant shall be bound to comply with the conditions so varied.
6. The industry shall provide adequate arrangement for fighting the accidental leakages, discharge of any pollutants gas/liquids from the vessels, mechanical equipment etc. which are likely to cause environment pollution.
7. The industry shall comply noise pollution (Regulation and control) Rules, 2000.
8. The industry shall comply all the direction/Rules/Instructions as may be issued by the MOEF/CPCB/HSPCB from time to time.
9. The industry shall ensure that various characteristics of the effluents remain within the tolerance limits as specified in EPA Standard and as amended from time to time and at no time the concentration of any characteristics should exceed these limits for discharge.
10. The industry would immediately submit the revised application to the Board in the event of any change in the raw material in process, mode of treatment/discharge of effluent. In case of change of process at any stage during the consent period, the industry shall submit fresh

consent application along with the consent to operate fee, if found due, which may be on any account and that shall be paid by the industry and the industry would immediately submit the consent application to the Board in the event of any change during the year in the raw material, quantity, quality of the effluent, mode of discharge, treatment facilities etc.

11. The officer/official of the Board shall reserve the right to access for the inspection of the industry in connection with the various process and the treatment facilities. The consent to operate is subject to review by the Board at any time.

12. Permissible limits for any pollutants mentioned in the consent to operate order should not exceed the concentration permitted in the effluent by the Board.

13. The industry shall pay the balance fee, in case it is found due from the industry at any time later on.

14. If the industry fails to adhere to any of the conditions of this consent to operate order, the consent to operate so granted shall automatically lapse.

15. If the industry is closed temporarily at its own, they shall inform the Board and obtain permission before restart of the unit.

16. The industry shall comply all the Directions/ Rules/Instructions issued from time to time by the Board.

Specific Conditions :

1. Unit will run and maintain its STP/ETP/APCM regularly and properly, will provide separate energy meter on their STP/ETP/APCM and maintain the Log Book for energy consumption of STP/ETP/APCM and chemicals used daily for the STP/ETP. 2. That the unit shall keep all the parameters within the prescribed limits and shall comply with all the Norms and Rules as prescribed in the Act. 3. That the unit will adopt cleaner technology thereby reducing pollution load. 4. That the unit will provide inter locking arrangement of DG set with STP/ETP/APCM and shall have separate D.G. set to ensure regular and effective running of pollution control devices. 5. That the unit will not discharge any untreated effluent inside and outside its premises. 6. Unit will provide separate flow meter at Inlet/ Outlet of STP/ETP for which separate log book will be maintained if required. 7. That the unit will not add any air polluting process/ machinery and also not to add any process which increases the water pollution load. 8. That the unit will comply with all the provisions of Hazardous Waste Rules and submit return under HWM Rules on yearly basis. 9. That the CTO so granted shall become invalid in case of violation of any of the above / any law of the land. 10. Unit will apply for consent to operate for further period 90 days before expiry of this consent otherwise penalty will be imposed as per policy. 11. Unit will submit compliance report of general & specific conditions mentioned in CTO along with fresh analysis report within 03 months. 12. The unit will apply for authorization under HWM rules, 2016.

KULDEEP SINGH
SINGH
Date: 26.05.2019 11:49:43 AM

*Regional Officer, Gurgaon North
Haryana State Pollution Control Board.*



EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory
(An ISO 9001:2015 Certified Company)

Office & Laboratory : 27A, Gurgaon Side of U. 7 Road, UPSID/Industrial Area, Gurgaon - Dist. Haryana (Haryana) India.
Office No: 011-26121127, 26121128, 26121129 | Fax: 011-26121130, 26121131, 26121132 | Website: www.ekoindia.com

TEST REPORT Effluent Sample Analysis

Test Report No. : EKO/131/160421

Issue Date : 21/04/2021

Issued To :

ASE INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahari,
Gurgaon Faridabad Road
Gurgaon Haryana- 122009

Sample Description : STP Inlet
Sample Drawn on : 16/04/2021
Sample Drawn by : EPEPL (Mr. Amit Kumar)
Sample Received on : 16/04/2021
Sampling Location : From STP Plant #2 (350 KLD)
Sampling Plan & Procedure : SOP-W/68
Sample Quantity : 1.0 Litre
Environmental Condition : Normal
Analysis Duration : 16/04/2021 To 21/04/2021
Remark (if any) : NA

RESULTS


S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.71	-
2	Total Suspended Solids	IS: 3025 (P-17)	120.0	mg/L
3	Oil & Grease	IS: 3025 (P-39)	11.0	mg/L
4	COD (as O ₂)	IS: 3025 (P-58)	320.4	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	37.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.





Office & Laboratory : 92/41, South Side of G-1 Road, UPSIDC Industrial Area, Ghazipur-20, Old (GZP-NCP) BINA
 Contact No.: 9810942570, 9810940678, 9829944457 Email: envil@ekopro.in, ekoproengineers@gmail.com, website: www.ekopro.in

TEST REPORT**Effluent Sample Analysis**

Test Report No. : EKO/133/160421

Issue Date : 21/04/2021

Issued To

: ASF INSIGNIA BEZ. PVT. LTD.
 Village - Gwal Pahar,
 Gurgaon Faridabad Road
 Gurugram Haryana- 122003

Sample Description : STP Inlet
 Sample Drawn on : 16/04/2021
 Sample Drawn by : EPEPL (Mr. Amit Kumar)
 Sample Received on : 16/04/2021
 Sampling Location : From STP Plant B3 (530 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 16/04/2021 To 21/04/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.38	-
2	Total Suspended Solids	IS: 3025 (P-17)	122.0	mg/L
3	Oil & Grease	IS: 3025 (P-39)	12.0	mg/L
4	CO ₂ (as O ₂)	IS: 3025 (P-58)	322.6	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	94.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

SPURNIMA CHAUDHARI
 TECHNICAL MANAGER
 (Effluent and Laboratory)

**EKO PRO ENGINEERS PVT. LTD.**Environmental Consultants and Analytical Laboratory
As ISO 9001:2015 Certified Company

Office & Laboratory : DDA, South Side of K-1, Road, HUDA Industrial Area, Ghaziabad - 201 105 (Distt./City) India
 Contact No: 9810943670, 9810943671, 9808941487 | E-mail: eko@ekoprof.com, ekoprof@ekoprof.com, ekoprof@ekoprof.com

TEST REPORT**Effluent Sample Analysis**

Test Report No. : EKO/154/160421

Issue Date : 21/04/2021

Issued To :

ASF INSIGNIA SEZ PVT. LTD.
 Village - Gwal Pahari,
 Gurgaon Faridabad Road
 Gurugram Haryana- 122003

Sample Description : STP Outlet
 Sample Drawn on : 16/04/2021
 Sample Drawn by : EPEPL (Mr. Amit Kumar)
 Sample Received on : 16/04/2021
 Sampling Location : From STP Plant B3 (530 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 16/04/2021 To 21/04/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule-VI Part-A)
1	pH	IS: 3025 (P-11)	7.76	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	11.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3025 (P-50)	30.5	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	9.4	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- This test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA CHAUHAN
 TECHNICAL MANAGER
 (Authorised Signatory)



TEST REPORT

Effluent Sample Analysis

Test Report No. : EKOR15N/160421

Issue Date : 21/04/2021

Issued To :

ASF INDIGNIA SEZ PVT. LTD.
Village - Gwal Pahari,
Gurgaon Faridabad Road
Gurgaon Haryana- 122005

Sample Description : STP Inlet
Sample Drawn on : 16/04/2021
Sample Drawn by : EPEPL (Mr. Amit Kumar)
Sample Received on : 16/04/2021
Sampling Location : From STP Plant (IDR Building)
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 1.0 Litre
Environmental Condition : Normal
Analysis Duration : 16/04/2021 To 21/04/2021
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.19	-
2	Total Suspended Solids	IS: 3025 (P-17)	424.0	mg/l
3	Oil & Grease	IS: 3025 (P-39)	15.0	mg/l
4	COD (as O ₂)	IS: 3025 (P-53)	589.4	mg/l
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	217.0	mg/l

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

BERNIMA CHAUDHARI
REGIONAL MANAGER
(Analytical Laboratory)



Office & Laboratory : 2/49, Phase III of G. T. Road, IIT/SEC Industrial Area, Gurgaon - 201 009 (Delhi-02) India.
 Contact No: 011-26100607, 011-26100670, 011-26144571 Email: eko@ekoenvi.com, eko@proenvi.com, eko@ecoenvi.com

TEST REPORT**Effluent Sample Analysis**

Test Report No. : EKO/158/160421

Issue Date : 21/04/2021

Issued To

: ACF INSIGNIA SEZ PVT LTD.
 Village - Gwal Pahar,
 Gurgaon Faridabad Road
 Gurgaon Haryana- 122003

Sample Description : STP Outlet
 Sample Drawn on : 16/04/2021
 Sample Drawn by : EPEPL (Mr. Arnit Kumar)
 Sample Received on : 16/04/2021
 Sampling Location : From STP Plant (IDR Building)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 16/04/2021 To 21/04/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule-VI Part-A)
1	pH	IS: 3026 (P-11)	7.49	-	5.5-9.0
2	Total Suspended Solids	IS: 3026 (P-17)	26.0	mg/L	100.0
3	Oil & Grease	IS: 3026 (P-39)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3026 (P-5a)	60.6	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3026 (P-4c)	14.0	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA CHAUHAN
 TECHNICAL MANAGER
 (Authorized Signatory)



Office & Laboratory : 32nd South Side of G. T. Road, IHSKCO Industrial Area, Sector-29, Gurgaon (Haryana), India
Contact No. : 9101501177, 9101501178, 9101501179 | Email : eko@ekopro.in, ekopro@ekopro.in, ekopro@ekopro.com | Website : www.ekopro.in

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/H34/120621

Issue Date : 17/05/2021

Issued To :

ASF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahar,
Gurgaon Faridabad Road
Gurgaon Haryana- 122003

Sample Description : STP Outlet
Sample Drawn on : 12/05/2021
Sample Drawn by : EPEPL (Mr. Armit Kumar)
Sample Received on : 12/05/2021
Sampling Location : From STP Plant B2 (310 KLD)
Sampling Plan & Procedure : SOP-W/00
Sample Quantity : 1.0 Litre
Environmental Condition : Normal
Analysis Duration : 12/05/2021 To 17/05/2021
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule-VI Part-A)
1	pH	IS: 3025 (P-11)	7.61	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	7.0	mg/l	100.0
3	Oil & Grease	IS: 3025 (P-30)	<0.1	mg/l	10.0
4	COD (as O ₂)	IS: 3025 (P-58)	35.8	mg/L	250.0
5	BOD (@27°C for 5 days)	IS: 3025 (P-44)	10.0	mg/l	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA SHANUJAN
TECHNICAL MANAGER
(ANALYTICAL LABORATORY)


 Office & Laboratory: 13941, South Side of G.T. Road, (Opposite Industrial Area, Sector-14) - 201 004 (Distt. Meerut, Uttar Pradesh) India. Contact No. +91-9899243379, 9899243378, 9126-344877. E-mail: info@ekopro.in, ekopro@ekopro.in, ekopro@ekopro.in, website: www.ekopro.in

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/135/120521

Issue Date : 17/05/2021

Issued To

 ASF INSIGNIA SEZ PVT. LTD.
 Village - Gwal Pahari,
 Gurgaon Faridabad Road
 Gurugram Haryana- 122003

Sample Description	: STP Inlet
Sample Drawn on	: 12/05/2021
Sample Drawn by	: EPEPL (Mr. Arjit kumar)
Sample Received on	: 12/05/2021
Sampling Location	: From STP Plant B3 (530 KLD)
Sampling Plan & Procedure	: SOP-W/66
Sample Quantity	: 1.0 Litro
Environmental Condition	: Normal
Analysis Duration	: 12/05/2021 To 17/05/2021
Remark (if any)	: NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.55	-
2	Total Suspended Solids	IS: 3025 (P-17)	122.0	mg/L
3	Oil & Grease	IS: 3025 (P-39)	12.0	mg/L
4	COD (as O ₂)	IS: 3025 (P-58)	322.6	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	95.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

 SPURNIMA CHAUHAN
 TECHNICAL MANAGER
 (ANALYTICAL LABORATORY)



Office & Laboratory : 2214, South Side of G.T. Road, (P.O. Industrial Area, Ghazipur - 201 009 (Noida, U.P.) India.
 Contact No. 9810849800, 9810849801, 9810849802 Email: ekoproengineers@gmail.com, website: www.ekopro.com

TEST REPORT**Effluent Sample Analysis**

Test Report No. : EKO/136/120821

Issue Date : 17/05/2021

Issued To :

ASF INSIGNIA SEZ PVT. LTD.
 Village - Gwal Pahari,
 Gurgaon Faridabad Road
 Gurugram Haryana- 122003

Sample Description : STP Outlet
 Sample Drawn on : 12/05/2021
 Sample Drawn by : EPEPL (Mr. Amit kumar)
 Sample Received on : 12/05/2021
 Sampling Location : From STP Plant B3 (500 KLD)
 Sampling Plan & Procedure : SOP-W/68
 Sample Quantity : 1.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 12/05/2021 To 17/05/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule- VI Part-A)
1	pH	IS: 3025 (P-11)	7.75	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	12.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-36)	<4.0	mg/L	10.0
4	COO (as O ₂)	IS: 3025 (P-68)	38.9	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	10.0	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA CHAUHAN
 * TECHNICAL MANAGER
 (Authorized Signatory)



Office & Laboratory : 204/1, South Side of G-7 Road, D-30/27 Industrial Area, Ghaziabad - 201 005 (Ghaziabad) INDIA
Contact No. 9896150979, 9810210876, 9920341487 Email : eko@ekoproindia.com, ekoproeng@gmail.com, website : www.ekoproindia.com

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/138/126621

Issue Date : 17/05/2021

Issued To :

ASIF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahari,
Gurgaon Faridabad Road
Gurgaon Haryana- 122003

Sample Description : STP Outlet
Sample Drawn on : 12/05/2021
Sample Drawn by : EPEPL (Mr. Amit kumar)
Sample Received on : 12/05/2021
Sampling Location : From STP Efflu (IDR Building)
Sampling Plan & Procedure : SOP-W/03
Sample Quantity : 1.0 Litre
Environmental Condition : Normal
Analysis Duration : 12/05/2021 To 17/05/2021
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule-VI Part-A)
1	pH	IS: 3025 (P-11)	7.42	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	26.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-30)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3025 (P-58)	72.3	mg/L	250.0
5	BOD (@27°C for 5 days)	IS: 3025 (P-44)	17.0	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

 RAJNIKANT CHAUDHARY
 TECHNICAL MANAGER
 EKO PRO ENGINEERS PVT. LTD.
 (Authorized Signatory)



EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory
(an ISO 9001:2015 Certified Company)

Plot No. 5, Subsector - 10, Sector - 10, Phase - I, Faridkot Industrial Area, Ghaziabad - 201 305 (Distt. Ghaziabad, U.P.)
 Contact No: 9810245676, 9810245677, 9810245678, 9810245679, Email: anuj@ekopro.com, ekopro@gmail.com, ekopro@yahoo.com, website: www.ekopro.com

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/13/06/0621

Issue Date : 12/06/2021

Issued To :

ASF INSIGNIA SEZ PVT. LTD.
 Village - Gwal Bahari,
 Gurgaon Faridabad Road
 Gurgaon Haryana- 122003

Sample Description : STP Inlet
 Sample Drawn on : 05/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj Kumar)
 Sample Received on : 07/06/2021
 Sampling Location : From STP Plant B2 (310 KLD)
 Sampling Plan & Procedure : SOP-W/6B
 Sample Quantity : 1.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 07/06/2021 To 11/06/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.69	-
2	Total Suspended Solids	IS: 3025 (P-17)	116.0	mg/L
3	Oil & Grease	IS: 3025 (P-39)	13.0	mg/L
4	COD (as O ₂)	IS: 3025 (P-58)	339.8	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	94.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

PIUSHMA CHAUHAN
 TECHNICAL MANAGER
 (Authorised Signatory)



EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory
(As per ISO 9001:2015 Certified Company)

Office & Laboratory: 122nd, 1st Floor, Noida, Distt. Gautam Buddha Nagar, Ghaziabad - 201 004 (Delhi-NCR), INDIA
Contact No: 011-26162656, 9810248578, 9868463677 E-mail: ekopro@ekopro.com, info@ekopro.com, ekopro@ekopro.com

TEST REPORT

Effluent Sample Analysis

Test Report No.: EKO/132/070621

Issue Date: 12/06/2021

Issued To: : ASF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahari,
Gurgaon Faridabad Road
Gurgaon Haryana- 122003

Sample Description : STP Outlet
Sample Drawn on : 05/06/2021
Sample Drawn by : ISPEPL (Mr. Anuj Kumar)
Sample Received on : 07/06/2021
Sampling Location : From STP Plant H2 (310 KLD)
Sampling Place & Procedure : SOP-W/00
Sample Quantity : 1.0 Liter
Environmental Condition : Normal
Analysis Duration : 07/06/2021 To 11/06/2021
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule-VI Part-A)
1	pH	IS: 3025 (P-11)	7.76	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	8.4	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3025 (P-56)	27.8	mg/L	260.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	7.2	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

PRINITHA BHUSHAN
TECHNICAL MANAGER
(Authorized Signatory)



Office & Laboratory : D-14, Sector-14, Gurgaon, Haryana
Gurgaon, Haryana - 122002. Contact : 9910248897, 9910248898, 9910248899, 9910248900, 9910248901, 9910248902

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/133/070821

Issue Date : 12/06/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahraji,
Gurgaon Faridabad Road
Gurugram Haryana- 122003

Sample Description : STP Inlet
Sample Drawn on : 05/06/2021
Sample Drawn by : EEPEPL (Mr. Anuj Kumar)
Sample Received on : 07/06/2021
Sampling Location : From STP Plant BS (630 KLD)
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 1.0 Litre
Environmental Condition : Normal
Analysis Duration : 07/06/2021 To 14/06/2021
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.45	-
2	Total Suspended Solids	IS: 3025 (P-17)	120.0	mg/L
3	Oil & Grease	IS: 3025 (P-30)	12.0	mg/L
4	COD (as O ₂)	IS: 3025 (P-68)	319.4	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	60.5	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

PERNIMA ANAHLAN
TECHNICAL MANAGER
(Authorised Signatory)



EKO PRO ENGINEERS PVT. LTD.

Environment: Consultants and Analytical Laboratory
(An ISO 9001:2015 Certified Company)

Office & Laboratory: 29/1, Gurgaon Side Street, 1st Floor, EPRPL Building Area, Ghosla Road - 122 003 (Gurgaon, Haryana, India)
Branch: 101, Sector 29, Gurgaon, Haryana - 122 003 (Gurgaon, Haryana, India) | Email: info@ekopro.com, ekopro@ekopro.com | Website: www.ekopro.com

TEST REPORT

Effluent Sample Analysis

Test Report No.: EKO/134/070821

Issue Date: 12/06/2021

Issued To:

: ASF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahari,
Gurgaon, Faridabad Road
Gurugram Haryana- 122003

Sample Description : STP Outlet
Sample Drawn on : 06/06/2021
Sample Drawn by : EPRPL (Mr. Anuj Kumar)
Sample Received on : 07/06/2021
Sampling Location : From STP Plant B3 (530 KLD)
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 1.0 Litre
Environmental Condition : Normal
Analysis Duration : 07/06/2021 To 11/06/2021
Remark (If any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1988 Schedule-VI Part-A)
1	pH	IS: 3025 (P-11)	7.84	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	9.0	mg/l	100.0
3	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/l	10.0
4	COD (as O ₂)	IS: 3025 (P-58)	29.4	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	8.2	mg/L	30.0

Notes:

- The results given above are related to the tested sample, as received & mentioned parameters. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA BRADHAN
TECHNICAL MANAGER
(Authorised Signatory)



Head Office: Laboratory - 1781, Sector No. 14, Gurgaon, Haryana - 122003. Contact No. - 0122-961424, 961425, 961426. Email: encl@ekopro.in, ekoproengg@ekopro.in, www.ekopro.in

TEST REPORT

Effluent Sample Analysis

Test Report No. : ERC/192/050621

Issue Date : 09/06/2021

Issued To :

ASF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahari,
Gurgaon Faridabad Road
Gurgaon Haryana- 122003

Sample Description : STP Inlet
Sample Drawn on : 05/06/2021
Sample Drawn by : EPEPL (Mr. Anuj Kumar)
Sample Received on : 05/06/2021
Sampling Location : From STP Plant (IDR Building)
Sampling Plan & Procedure : SOP-V/06
Sample Quantity : 1.0 Litre
Environmental Condition : Normal
Analysis Duration : 05/06/2021 To 09/06/2021
Remark (if any) : NA

RESULTS


S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.16	-
2	Total Suspended Solids	IS: 3025 (P-17)	420.0	mg/L
3	Oil & Grease	IS: 3025 (P-39)	13.0	mg/L
4	COD (as O ₂)	IS: 3025 (P-58)	680.2	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	208.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless unless specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.


PURNIMA CHAHAL
 TECHNICAL MANAGER
 (Authorised Signatory)



Office & Laboratory : 224, Sector-14, Part-1, Phase-1, Gurgaon, Haryana - 122003. Phone No. - 011-3331024/26/27, Fax No. - 3331028
E-mail : info@eko-pro.com, sales@eko-pro.com, testing@eko-pro.com, hr@eko-pro.com, ecompliance@eko-pro.com, eko@eko-pro.com

TEST REPORT**Effluent Sample Analysis**

Test Report No. : EKO/193/060521

Issue Date : 09/06/2021

Issued To :

ASF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahar,
Gurgaon Faridabad Road
Gurgaon Haryana- 122003

Sample Description : STP Outlet
Sample Drawn on : 05/06/2021
Sample Drawn by : EPEPL (Mr. Anuj Kumar)
Sample Received on : 06/06/2021
Sampling Location : From STP Plant (DR Building)
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 1.0 Litre
Environmental Condition : Normal
Analysis Duration : 05/06/2021 To 09/06/2021
Remark (if any) : NA

RESULTS


S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule-VI Part-A)
1	pH	IS: 3025 (P-11)	7.45	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	24.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-30)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3025 (P-53)	69.9	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	16.0	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.


PURNIMA CHHAYAN
TECHNICAL MANAGER
(Authorized Signatory)



Office & Laboratory : 107/1, South Gate of G. I. Road, (P/400 Industrial Area, Kharadi) - 411 004 (Mumbai) (Maharashtra)
Contact No: 920202427, 920202428, 920202440 Email: eco.pro@ecopro.com, ekoproengineers@gmail.com, website: www.ecopro.in

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/132/020721

Issue Date : 06/07/2021

Issued To :

ASF INSIGNIA SEZ PVT. LTD.

Village- Gwal Pahari.

Gurgaon Faridabad Road,

Gurgaon Haryana-122003

Sample Description : STP Inlet
 Sample Drawn on : 02/07/2021
 Sample Drawn by : EPEPL (Mr. Amit kumar)
 Sample Received on : 02/07/2021
 Sampling Location : From STP Plant B2 (310 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/07/2021 To 06/07/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.69	-
2	Total Suspended Solids	IS: 3025 (P-17)	117.0	mg/L
3	Oil & Grease	IS: 3025 (P-39)	15.0	mg/L
4	COD (as O ₂)	IS: 3025 (P-58)	325.4	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	90.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA KHANNA
TECHNICAL MANAGER
Authorised Signatory



Office & Laboratory : 6051, Sector 28A of G. Z. Road, Noida, Industrial Area, Ghaziabad - 201 309 (Distt-GZ) India.
 Contact no: Mobile: 9810943884, 9826344669 - Email: eko@ekoengineers.com, ekoenviro@gmail.com, eko@ekoenviro.com

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/134/020721

Issue Date : 06/07/2021

Issued To

: ASF INSIGMA SEZ PVT. LTD.

Village- Gwal Pahsa,
 Gurugram Faridabad Road,
 Gurugram Haryana-122003

Sample Description : STP Outlet
 Sample Drawn on : 02/07/2021
 Sample Drawn by : EPEPL (Mr. Amit kumar)
 Sample Received on : 02/07/2021
 Sampling Location : From STP Plant B2 (310 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/07/2021 To 06/07/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per GPCB (EPR-1986 Schedule VI Part-A)
1	pH	IS: 3025 (P-11)	7.68	-	5.5-9.0
3	Total Suspended Solids	IS: 3025 (P-17)	8.0	mg/L	100.0
4	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/L	<0.0
5	COD (as O ₂)	IS: 3025 (P-58)	42.4	mg/L	250.0
6	BOD (@27°C for 3 days)	IS: 3025 (P-44)	12.0	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA CHAUHAN
 TECHNICAL MANAGER
 (Analytical Laboratory)



Office & Laboratory : Plot No. 302/3025, Connaught Place, New Delhi-110029 (India)
 Contact : 011-26101261, 9810044877 | E-mail : info@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/133/020721

Issue Date : 06/07/2021

Issued To :

ASF INSIGNIA SEZ PVT. LTD.
 Village- Gwal Paheri,
 Gurgaon Faridabad Road,
 Gurugram Haryana-122003

Sample Description : STP Inlet
 Sample Drawn on : 02/07/2021
 Sample Drawn by : EPEPL (Mr. Amit kumar)
 Sample Received on : 02/07/2021
 Sampling Location : From STP Plant 83 (630 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/07/2021 To 06/07/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.58	-
2	Total Suspended Solids	IS: 3025 (P-17)	120.0	mg/L
3	Oil & Grease	IS: 3026 (P-39)	13.0	mg/L
4	COD (as O ₂)	IS: 3026 (P-53)	328.4	mg/L
5	BOD (@27°C for 3 days)	IS: 3026 (P-44)	92.6	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicly/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA CHATURVEDI
 TECHNICAL MANAGER
 (Authorized Signatory)



EKO PRO ENGINEERS PVT. LTD.
 Environmental Consultants and Analytical Laboratory
 (An ISO 9001:2015 Certified Company)

Office & Laboratory : 2041, South Side of B Road, MIDC, Khandivda, Mumbai - 400 051 (MUMBAI) INDIA
 Contact No. 02612427, 02612428, 02612429 Fax: 02612430, 02612431, 02612432 E-mail: info@ekoengineers.com, ekoengineers@yahoo.com, web: www.ekoengineers.com

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/136/020721

Issue Date : 06/07/2021

Tested To

: ASF INSIGNIA SEZ PVT. LTD.
 Village- Gwal Paharil,
 Gurgaon Faridabad Road,
 Gurugram Haryana-122003

Sample Description : STP Outlet
 Sample Drawn on : 02/07/2021
 Sample Drawn by : EPEPL (Mr. Anil Kumar)
 Sample Received on : 03/07/2021
 Sampling Location : From STP Plant B3 (630 KLD)
 Sampling Plan & Procedure : SOP-W68
 Sample Quantity : 2.0 Litrs
 Environmental Condition : Normal
 Analysis Duration : 02/07/2021 To 06/07/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (SPR-1986 Schedule VI Part-A)
1	pH	IS: 3025 (P-11)	7.71	-	5.5-10.0
3	Total Suspended Solids	IS: 3025 (P-17)	14.0	mg/L	100.0
4	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/L	10.0
5	COD (as O ₂)	IS: 3025 (P-55)	49.4	mg/L	250.0
6	BOD (@27°C for 5 days)	IS: 3025 (P-44)	12.0	mg/L	50.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA CHAUHAN
 TECHNICAL MANAGER
 (Authorized Signatory)



Office & Laboratory : 13/41, Sector 29 of G. D. S. Road, Industrial Area, Okhla, New Delhi (India) PIN-110025
 Contact nos: 011-26102661, 011-26102662, 011-26102663 Email: enquiry@eko-pro.com, laboratory@eko-pro.com, website: www.eko-pro.com

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/130/020721

Issue Date : 06/07/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
 Village- Gwal Pahari,
 Gurgaon Faridabad Road,
 Gurgaon Haryana-122003

Sample Description : STP Inlet
 Sample Drawn on : 02/07/2021
 Sample Drawn by : EPEPL (Mr. Amit kumar)
 Sample Received on : 02/07/2021
 Sampling Location : From STP Plant (IDR Bedding)
 Sampling Plan & Procedure : SOP-W/S6
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/07/2021 to 06/07/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.12	-
2	Total Suspended Solids	IS: 3025 (P-17)	405.0	mg/L
3	Oil & Grease	IS: 3026 (P-39)	14.0	mg/L
4	COD (as O ₂)	IS: 3025 (P-58)	570.2	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-64)	204.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

PURNMA CHAUHAN
 TECHNICAL MANAGER
 (Authorized Signatory)



Office & Laboratory : Sect. 3, Main Gate No. 1 Road, UPBDC Bypass Area, Haridwar - 241 002 (Distt. NCTD) INDIA
 Contact No: 99200570, 981076078, 8828341877 | Email: eko@eko-pro.com, ekoengineers@gmail.com, eko@eko-pro.in

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/131/020721

Issue Date : 06/07/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
 Village- Gwal Paheri,
 Gurgaon Faridabad Road,
 Gurugram Haryana-122003

Sample Description : STP Outlet
 Sample Drawn on : 02/07/2021
 Sample Drawn by : EPEPL (Mr. Amit kumar)
 Sample Received on : 02/07/2021
 Sampling Location : From STP Plant (DR Building)
 Sampling Plan & Procedure : SOP-W/08
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/07/2021 To 03/07/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule- VI Part-A)
1	pH	IS: 3025 (P-11)	7.48	-	6.5-8.0
3	Total Suspended Solids	IS: 3025 (P-17)	26.0	mg/l	100.0
4	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/L	10.0
5	COD (as O ₂)	IS: 3025 (P-58)	62.4	mg/L	250.0
6	BOD (@27°C for 5 days)	IS: 3025 (P-44)	16.0	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
 The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA CHATTERJAN
 TECHNICAL MANAGER
 (Authorized Signatory)



Office & Laboratory : 27/11, Sector 29B of Gurgaon, Haryana (122002) India. Phone : (0129277) 8800
 Contact No. : (0129) 425271, 425272, 425273, 425274. Fax : (0129) 425275. E-mail : info@ekopro.com, ekopro@ekopro.com

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/A77/020021

Issue Date : 05/08/2021

Issued To

: ASIF INSIGNIA GEZ PVT. LTD.

Village- Gwal Pahari,
 Gurgaon Faridkot Road,
 Gurugram Haryana-122003

Sample Description : STP Inlet
 Sample Drawn on : 02/08/2021
 Sample Drawn by : EPEPL (Mr. Anuj Kumar)
 Sample Received on : 02/08/2021
 Sampling Location : From STP Plant B2 (S+0 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/08/2021 To 05/08/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.62	-
2	Total Suspended Solids	IS: 3025 (P-17)	124.0	mg/L
3	Oil & Grease	IS: 3025 (P-30)	12.0	mg/l.
4	COD (as O ₂)	IS: 3025 (P-68)	309.2	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	92.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA GAUBHAN
 TECHNICAL MANAGER
 (Authorised Signatory)



Office & Laboratory : A-94, Sector 14B of G. T. Road, UPPCO, Indira Park, Gurgaon - 122001 (Haryana) India.
 Contact No. 01294-221500/221501/221502. E-mail: management@eko-peo.com/eko-peo@eko-peo.com

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/178/020821	Issue Date : 05/08/2021
Issued To : ASF INSIGNIA SEZ PVT. LTD.	
	Village- Gwal Paharj, Gurgaon Faridabad Road, Gurgaon Haryana-122003
Sample Description : STP Outlet	
Sample Drawn on : 02/08/2021	
Sample Drawn by : EPEPL (Mr. Anuj Kumar)	
Sample Received on : 02/08/2021	
Sampling Location : From STP Plant B2 (310 KLD)	
Sampling Plan & Procedure : SOP-W/66	
Sample Quantity : 2.0 Litre	
Environmental Condition : Normal	
Analysis Duration : 02/08/2021 To 05/08/2021	
Remark (if any) : NA	

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule-VI Part-A)
1	pH	IS: 3025 (P-11)	7.56	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (F-17)	8.0	mg/l	100.0
3	Oil & Grease	IS: 3025 (F-39)	4.0	mg/l	10.0
4	COD (as O ₂)	IS: 3025 (F-58)	34.6	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (F-44)	9.0	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PEO ENGINEERS PVT. LTD.

PURNIMA CHAUHAN
 TECHNICAL MANAGER
 (Authorized Signatory)



Office : 1/194/1st Floor, South Block of P. T. House, 147000 Indraprastha Area, Ghazipur, Distt. WZ, New Delhi-110002
 Contact No. : 91-11-4301307, 911111375, 762934452 | E-mail: eko@ekoengineers.com, eko@ekoengineers.co.in, eko@ekoengineers.net | Website : www.ekoengineers.com

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/178/020521

Issue Date : 05/08/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.

Village- Gwal Puhari,

Gurgaon Faridabad Road,

Gurgaon Haryana-122003

Sample Description : STP Inlet
 Sample Drawn on : 02/08/2021
 Sample Drawn by : EPEPL (Mr. Anuj Kumar)
 Sample Received on : 02/08/2021
 Sampling Location : From STP Plant B3 (530 KLD)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/08/2021 To 05/08/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.51	
2	Total Suspended Solids	IS: 3025 (P-17)	120.0	mg/l.
3	Oil & Grease	IS: 3025 (P-39)	11.0	mg/l.
4	COD (as O ₂)	IS: 3025 (P-58)	320.5	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	91.0	mg/l.

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA CHHABHAN
TECHNICAL MANAGER

(Authorized Signatory)



Office & Laboratory : 27A, South Side of H. I. Road, UPSIDE of Metro Station, Gurgaon - 122003 (Sector-10 Gurgaon)
 Contact No. : 0124-2718217, 0124-2718218, 0124-2718219 E-mail: ekopro@ekopro.com, ekopro@gmail.com

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/180/020821

Issue Date : 05/08/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.

 Village- Gwal Pahar,
 Gurgaon Faridabad Road,
 Gurugram Haryana-122003

Sample Description : STP Outlet
 Sample Drawn on : 02/08/2021
 Sample Drawn by : EPEPL (Mr. Anuj kumar)
 Sample Received on : 02/08/2021
 Sampling Location : From STP Plant B3 (530 KLD)
 Sampling Plan & Procedure : SOP-W/86
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/08/2021 To 05/08/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule-VI Part-A)
1	pH	IS: 3025 (P-11)	7.74		5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	10.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-30)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3025 (P-58)	35.6	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	9.2	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.


 JURNIMA CHHATAN
 TECHNICAL MANAGER
 (Authorised Signatory)



EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory
(An ISO 9001:2015 Certified Company)

Office & Laboratory : 3rd Fl., Subh-Seti, Plot No. 14/6222, Gurgaon Road, Gurgaon, Haryana-122009, India.
 Contact : 01294282021, 01294282022, 01294241407. Email : info@eko-pro.com, eko-pro@eko-pro.com, eko-pro@eko-pro.com

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/175/020821

Issue Date : 05/08/2021

Issued To :

: ASF INSIGNIA SEZ PVT. LTD.
 Village- Gwal Pahari,
 Gurgaon Faridabad Road,
 Gurugram Haryana-122009

Sample Description : STP Inlet (50 KLD STP)
 Sample Drawn on : 02/08/2021
 Sample Drawn by : EPEPL (Mr. Antij kumar)
 Sample Received on : 02/08/2021
 Sampling Location : From STP Plant (BOR Building)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/08/2021 To 05/08/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.16	
2	Total Suspended Solids	IS: 3025 (P-17)	360.0	mg/L
3	Oil & Grease	IS: 3025 (P-39)	16.0	mg/L
4	COD (as O ₂)	IS: 3025 (P-58)	582.9	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-41)	295.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
 The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA BHADHAN
 TECHNICAL MANAGER
 THE LABORATORY
 (Authorized Signatory)


 Office & Laboratory : 337/1, Sector 149, Phase 1, Gurgaon, Haryana (India) - 122002 (Distt:-Gurgaon) Haryana
 Contact No : 0129724177, 0129723076, 0129724178 | E-mail : ekoproengg@gmail.com, ekoproengg@yahoo.co.in

TEST REPORT
Effluent Sample Analysis

Test Report No. : EKO/178/020/21

Issue Date : 05/08/2021

Issued To :

 ASE INSIGNIA SEZ PVT. LTD.
 Village- Gwal Pahari,
 Gurgaon Faridabad Road,
 Gurgaon Haryana-122003

 Sample Description : STP Outlet (50 KLD STP)
 Sample Drawn on : 02/08/2021
 Sample Drawn by : EPEPL (Mr. Anuj kumar)
 Sample Received on : 02/08/2021
 Sampling Location : From STP Plant (BDR Building)
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 02/08/2021 To 05/08/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule-VI Part-A)
1	pH	IS: 3025 (P-11)	7.38	-	5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	25.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3025 (P-58)	70.5	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	15.0	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

 PURNIMA CHAUHAN
 TECHNICAL MANAGER
 (Authorised Signatory)



Office & Laboratory: 27A1, Tughlakpur, A-13, 1st Floor, UPSIDC Industrial Area, Jharkhand - 831 001 (Dist. Bokaro) JHAR.
 Corporate Office: 27A1, Tughlakpur, A-13, 1st Floor, UPSIDC Industrial Area, Jharkhand - 831 001 (Dist. Bokaro) JHAR.

TEST REPORT
Sewage Sample Analysis

Test Report No. : **EKO/01/040821** Issue Date : **05/09/2021**
 Issued to : **ASF INSIGNIA SEZ (PES),**
Village- Gwal Pahan,
Gurgaon Faridabad Road,
Sub Teh. Wazirabad, Gurgaon-122003

Sample Description : **STP Inlet**
 Sample Drawn on : **04/08/2021**
 Sample Drawn by : **EPEPL (M: Amit Kumar)**
 Sample Received on : **04/08/2021**
 Sampling Location : **From STP Plant B2 (310 KLE)**
 Sampling Plan & Procedure : **SOP-W/06**
 Sample Quantity : **2.0 Litre**
 Environmental Condition : **Normal**
 Analysis Duration : **04/09/2021 To 08/09/2021**
 Remark (if any) : **NA**

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.64	-
2	Total Suspended Solids	IS: 3025 (P-17)	112.0	mg/L
3	Oil & Grease	IS: 3025 (P-39)	13.0	mg/L
4	CO ₂ (as O ₂)	IS: 3025 (P-56)	330.6	mg/L
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	87.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For **EKO PRO ENGINEERS PVT. LTD.**
PURNIMA CHAUDHARI,
TECHNICAL MANAGER
 (Authorized Signatory)



EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory
(an ISO 9001:2015 Certified Company)

Office & Laboratory : 127, 2nd Floor of 'A' Wing, 15th Street, Connaught Place, New Delhi - 110028, India.
E-mail: eko@ekopro.com, info@ekopro.com, eko@ekopro.com | Tel: +91-11-26104457 | Fax: +91-11-26104458

TEST REPORT

Sewage Sample Analysis

Test Report No. : EKC/152/040821

Issue Date : 09/09/2021

Issued To :

MSF INDIGNIA SEZ OTES,
Village- Gawa Pahad,
Gurgaon Faridabad Road,
Sub Teh. Wazirabad, Gurgaon-122003

Sample Description : STP Outlet
Sample Drawn on : 04/09/2021
Sample Drawn by : EPEPL (Mr. Amit kumar)
Sample Received on : 04/09/2021
Sampling Location : From STP Plant B2 (310 KLD)
Sampling Plan & Procedure : SOP-W/03
Sample Quantity : 2.0 Litre
Environmental Condition : Normal
Analysis Duration : 04/09/2021 To 09/09/2021
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule-VI Part-A)
1	pH	IS: 3025 (P-11)	7.02		5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	9.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-36)	<4.0	mg/L	10.0
4	COG (as O ₂)	IS: 3025 (P-58)	39.6	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	10.0	mg/L	30.0

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA GUPTA
TECHNICAL MANAGER
(Authorized Signatory)



EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory,
 101/102/103/104/105/106/107/108/109/110/111/112/113/114/115/116/117/118/119/120/121/122/123/124/125/126/127/128/129/130/131/132/133/134/135/136/137/138/139/140/141/142/143/144/145/146/147/148/149/150/151/152/153/154/155/156/157/158/159/160/161/162/163/164/165/166/167/168/169/170/171/172/173/174/175/176/177/178/179/180/181/182/183/184/185/186/187/188/189/190/191/192/193/194/195/196/197/198/199/200/201/202/203/204/205/206/207/208/209/210/211/212/213/214/215/216/217/218/219/220/221/222/223/224/225/226/227/228/229/230/231/232/233/234/235/236/237/238/239/240/241/242/243/244/245/246/247/248/249/250/251/252/253/254/255/256/257/258/259/260/261/262/263/264/265/266/267/268/269/270/271/272/273/274/275/276/277/278/279/280/281/282/283/284/285/286/287/288/289/290/291/292/293/294/295/296/297/298/299/300/301/302/303/304/305/306/307/308/309/310/311/312/313/314/315/316/317/318/319/320/321/322/323/324/325/326/327/328/329/330/331/332/333/334/335/336/337/338/339/340/341/342/343/344/345/346/347/348/349/350/351/352/353/354/355/356/357/358/359/360/361/362/363/364/365/366/367/368/369/370/371/372/373/374/375/376/377/378/379/380/381/382/383/384/385/386/387/388/389/390/391/392/393/394/395/396/397/398/399/400/401/402/403/404/405/406/407/408/409/410/411/412/413/414/415/416/417/418/419/420/421/422/423/424/425/426/427/428/429/430/431/432/433/434/435/436/437/438/439/440/441/442/443/444/445/446/447/448/449/450/451/452/453/454/455/456/457/458/459/460/461/462/463/464/465/466/467/468/469/470/471/472/473/474/475/476/477/478/479/480/481/482/483/484/485/486/487/488/489/490/491/492/493/494/495/496/497/498/499/500/501/502/503/504/505/506/507/508/509/510/511/512/513/514/515/516/517/518/519/520/521/522/523/524/525/526/527/528/529/530/531/532/533/534/535/536/537/538/539/540/541/542/543/544/545/546/547/548/549/550/551/552/553/554/555/556/557/558/559/560/561/562/563/564/565/566/567/568/569/570/571/572/573/574/575/576/577/578/579/580/581/582/583/584/585/586/587/588/589/590/591/592/593/594/595/596/597/598/599/600/601/602/603/604/605/606/607/608/609/610/611/612/613/614/615/616/617/618/619/620/621/622/623/624/625/626/627/628/629/630/631/632/633/634/635/636/637/638/639/640/641/642/643/644/645/646/647/648/649/650/651/652/653/654/655/656/657/658/659/660/661/662/663/664/665/666/667/668/669/670/671/672/673/674/675/676/677/678/679/680/681/682/683/684/685/686/687/688/689/690/691/692/693/694/695/696/697/698/699/700/701/702/703/704/705/706/707/708/709/710/711/712/713/714/715/716/717/718/719/720/721/722/723/724/725/726/727/728/729/730/731/732/733/734/735/736/737/738/739/740/741/742/743/744/745/746/747/748/749/750/751/752/753/754/755/756/757/758/759/760/761/762/763/764/765/766/767/768/769/770/771/772/773/774/775/776/777/778/779/780/781/782/783/784/785/786/787/788/789/790/791/792/793/794/795/796/797/798/799/800/801/802/803/804/805/806/807/808/809/810/811/812/813/814/815/816/817/818/819/820/821/822/823/824/825/826/827/828/829/830/831/832/833/834/835/836/837/838/839/840/841/842/843/844/845/846/847/848/849/850/851/852/853/854/855/856/857/858/859/860/861/862/863/864/865/866/867/868/869/870/871/872/873/874/875/876/877/878/879/880/881/882/883/884/885/886/887/888/889/890/891/892/893/894/895/896/897/898/899/900/901/902/903/904/905/906/907/908/909/910/911/912/913/914/915/916/917/918/919/920/921/922/923/924/925/926/927/928/929/930/931/932/933/934/935/936/937/938/939/940/941/942/943/944/945/946/947/948/949/950/951/952/953/954/955/956/957/958/959/960/961/962/963/964/965/966/967/968/969/970/971/972/973/974/975/976/977/978/979/980/981/982/983/984/985/986/987/988/989/990/991/992/993/994/995/996/997/998/999/1000

Office : 101/102/103/104/105/106/107/108/109/110/111/112/113/114/115/116/117/118/119/120/121/122/123/124/125/126/127/128/129/130/131/132/133/134/135/136/137/138/139/140/141/142/143/144/145/146/147/148/149/150/151/152/153/154/155/156/157/158/159/160/161/162/163/164/165/166/167/168/169/170/171/172/173/174/175/176/177/178/179/180/181/182/183/184/185/186/187/188/189/190/191/192/193/194/195/196/197/198/199/200/201/202/203/204/205/206/207/208/209/210/211/212/213/214/215/216/217/218/219/220/221/222/223/224/225/226/227/228/229/230/231/232/233/234/235/236/237/238/239/240/241/242/243/244/245/246/247/248/249/250/251/252/253/254/255/256/257/258/259/260/261/262/263/264/265/266/267/268/269/270/271/272/273/274/275/276/277/278/279/280/281/282/283/284/285/286/287/288/289/290/291/292/293/294/295/296/297/298/299/300/301/302/303/304/305/306/307/308/309/310/311/312/313/314/315/316/317/318/319/320/321/322/323/324/325/326/327/328/329/330/331/332/333/334/335/336/337/338/339/340/341/342/343/344/345/346/347/348/349/350/351/352/353/354/355/356/357/358/359/360/361/362/363/364/365/366/367/368/369/370/371/372/373/374/375/376/377/378/379/380/381/382/383/384/385/386/387/388/389/390/391/392/393/394/395/396/397/398/399/400/401/402/403/404/405/406/407/408/409/410/411/412/413/414/415/416/417/418/419/420/421/422/423/424/425/426/427/428/429/430/431/432/433/434/435/436/437/438/439/440/441/442/443/444/445/446/447/448/449/450/451/452/453/454/455/456/457/458/459/460/461/462/463/464/465/466/467/468/469/470/471/472/473/474/475/476/477/478/479/480/481/482/483/484/485/486/487/488/489/490/491/492/493/494/495/496/497/498/499/500/501/502/503/504/505/506/507/508/509/510/511/512/513/514/515/516/517/518/519/520/521/522/523/524/525/526/527/528/529/530/531/532/533/534/535/536/537/538/539/540/541/542/543/544/545/546/547/548/549/550/551/552/553/554/555/556/557/558/559/560/561/562/563/564/565/566/567/568/569/570/571/572/573/574/575/576/577/578/579/580/581/582/583/584/585/586/587/588/589/590/591/592/593/594/595/596/597/598/599/600/601/602/603/604/605/606/607/608/609/610/611/612/613/614/615/616/617/618/619/620/621/622/623/624/625/626/627/628/629/630/631/632/633/634/635/636/637/638/639/640/641/642/643/644/645/646/647/648/649/650/651/652/653/654/655/656/657/658/659/660/661/662/663/664/665/666/667/668/669/670/671/672/673/674/675/676/677/678/679/680/681/682/683/684/685/686/687/688/689/690/691/692/693/694/695/696/697/698/699/700/701/702/703/704/705/706/707/708/709/710/711/712/713/714/715/716/717/718/719/720/721/722/723/724/725/726/727/728/729/730/731/732/733/734/735/736/737/738/739/740/741/742/743/744/745/746/747/748/749/750/751/752/753/754/755/756/757/758/759/760/761/762/763/764/765/766/767/768/769/770/771/772/773/774/775/776/777/778/779/780/781/782/783/784/785/786/787/788/789/790/791/792/793/794/795/796/797/798/799/800/801/802/803/804/805/806/807/808/809/810/811/812/813/814/815/816/817/818/819/820/821/822/823/824/825/826/827/828/829/830/831/832/833/834/835/836/837/838/839/840/841/842/843/844/845/846/847/848/849/850/851/852/853/854/855/856/857/858/859/860/861/862/863/864/865/866/867/868/869/870/871/872/873/874/875/876/877/878/879/880/881/882/883/884/885/886/887/888/889/890/891/892/893/894/895/896/897/898/899/900/901/902/903/904/905/906/907/908/909/910/911/912/913/914/915/916/917/918/919/920/921/922/923/924/925/926/927/928/929/930/931/932/933/934/935/936/937/938/939/940/941/942/943/944/945/946/947/948/949/950/951/952/953/954/955/956/957/958/959/960/961/962/963/964/965/966/967/968/969/970/971/972/973/974/975/976/977/978/979/980/981/982/983/984/985/986/987/988/989/990/991/992/993/994/995/996/997/998/999/1000

TEST REPORT

Sewage Sample Analysis

Test Report No.: EKO/PS/046889

Issue Date: 04/09/2021

Issued To:

ASIF BISHNIA, SEZ, I SEC,
 Village - Gwal Pahar,
 Gurgaon Faridabad Road,
 Sub Teh. Wazirabad, Gurgaon-122003

Sample Description : STP Inlet
 Sample Drawn on : 04/09/2021
 Sample Drawn by : EPEPL (Mr. Amit kumar)
 Sample Received on : 04/09/2021
 Sampling Location : From STP Plant B3 (SSO RLD)
 Sampling Plan & Procedure : SOP-WWS
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 04/09/2021 To 05/09/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Method	Results	Units
1	pH	IS: 3025 (P-11)	7.51	-
2	Total Suspended Solids	IS: 3025 (P-17)	124.0	mg/L
3	Oil & Grease	IS: 3025 (P-38)	14.0	mg/L
4	COD (as O ₂)	IS: 3025 (P-58)	220.4	mg/L
5	BOD (@27°C for 5 days)	IS: 3025 (P-44)	80.0	mg/L

Notes :

- The results given above are related to the tested sample, as received & mentioned parameters.
 The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For EKO PRO ENGINEERS PVT. LTD.

ROHINI KUMAR
 TECHNICAL MANAGER
 (Authenticated Signature)



Office & Laboratory: 10th Floor, 10th Cross, 1st Stage, 1st Mile, 1st Main Road, Industrial Area, Ground Floor, 1st Stage, 1st Mile, 1st Main Road, 1st Stage, 1st Mile, 1st Main Road, Bangalore-560025. Contact: 98453 22222, 98453 22222. Email: info@eko-pro.com, eko@eko-pro.com

TEST REPORT

Effluent Sample Analysis

Test Report No. : EKO/60/050921 Issue Date : 06/05/2021
 Issued To : A&P INSIGNIA SEZ ITES,
 Village- Gwal Bahari,
 Gurgaon Faridabad Road,
 Sub Teh Wazirabad, Gurgaon-122003

Sample Description : STP Outlet
 Sample Drawn on : 04/09/2021
 Sample Drawn by : EPEPL (Mr. Anil kumar)
 Sample Received on : 04/09/2021
 Sampling Location : From STP Plant (IDR Building)
 Sampling Plan & Procedure : SOP-W/06
 Sample Quantity : 2.0 Litre
 Environmental Condition : Normal
 Analysis Duration : 04/09/2021 To 06/09/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per CPCB (EPR-1986 Schedule-VI Part-A)
1	pH	IS: 3025 (P-11)	7.41		5.5-9.0
2	Total Suspended Solids	IS: 3025 (P-17)	28.0	mg/L	100.0
3	Oil & Grease	IS: 3025 (P-39)	<4.0	mg/L	10.0
4	COD (as O ₂)	IS: 3025 (P-58)	74.8	mg/L	250.0
5	BOD (@27°C for 3 days)	IS: 3025 (P-44)	17.0	mg/L	30.0

Notes :




- The results given above are related to the tested sample, as received & mentioned parameters. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****



For EKO PRO ENGINEERS PVT. LTD.

ANURAG KUMAR
 TECHNICAL MANAGER
 (Authorised Signatory)


Borewell No.1

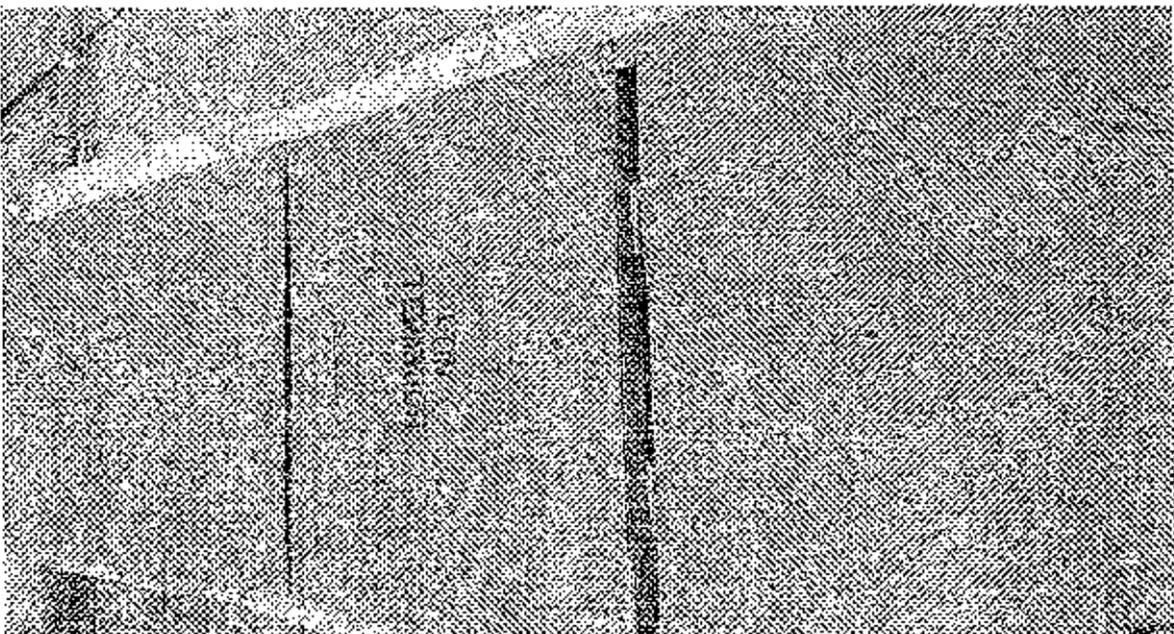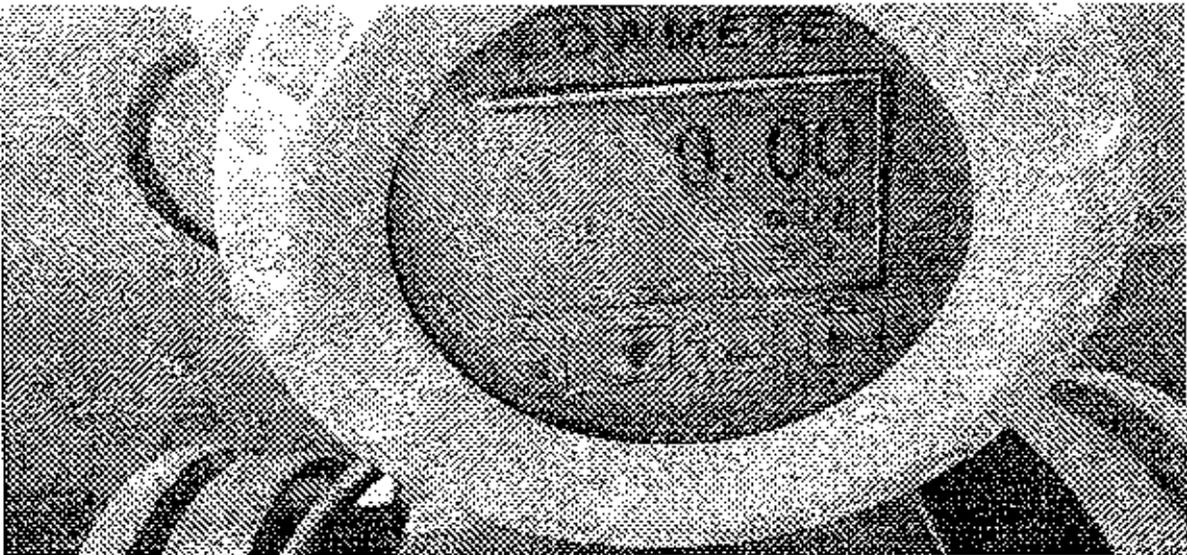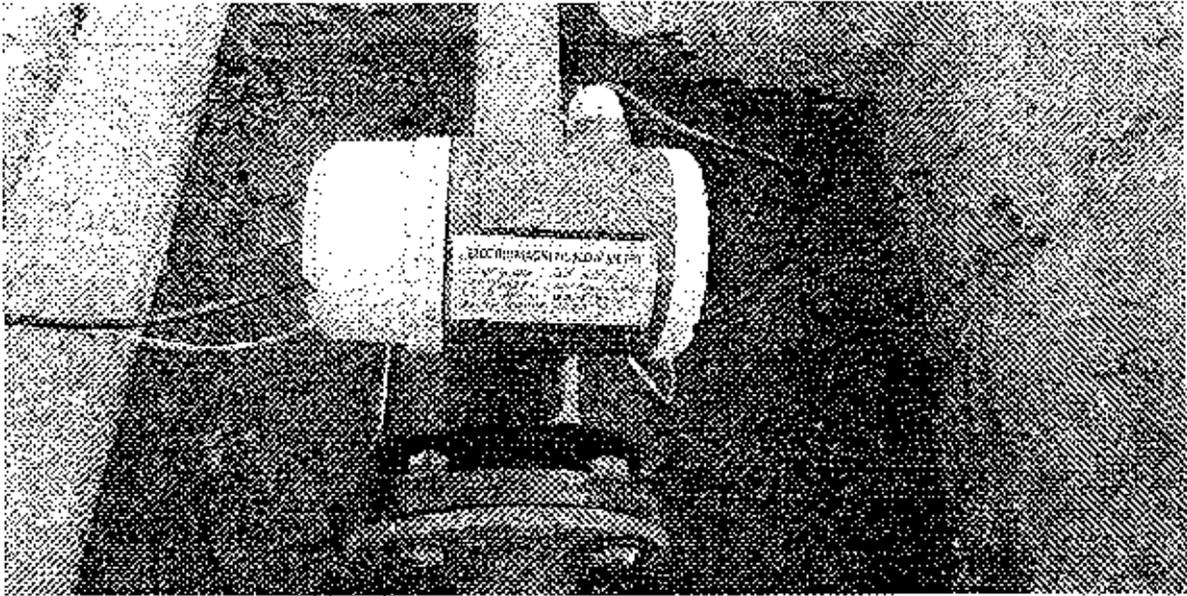

Borewell No.2

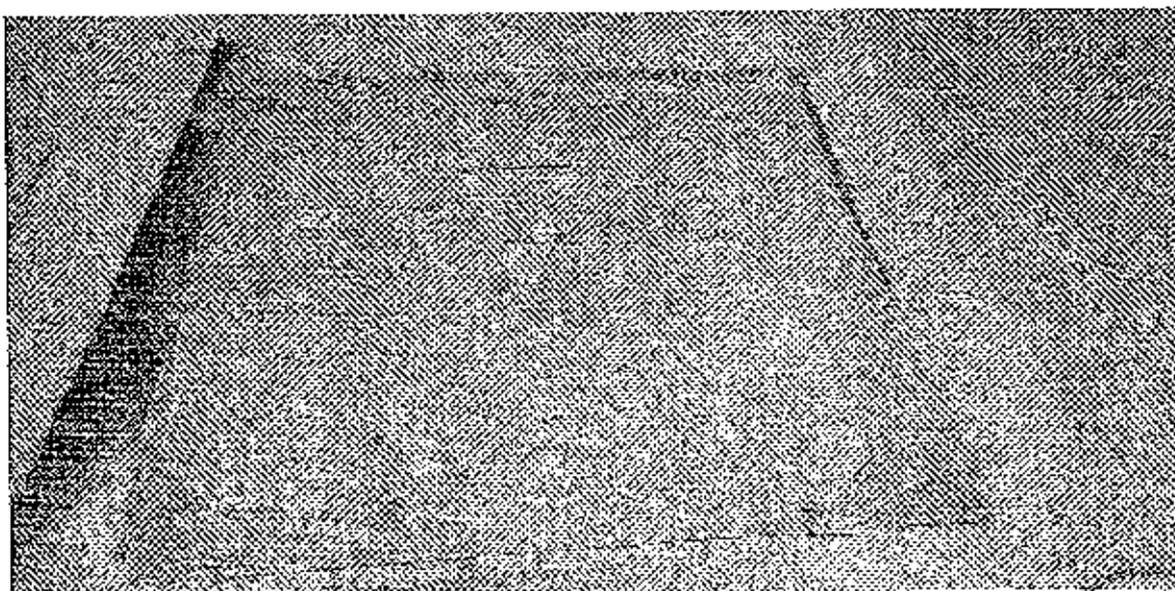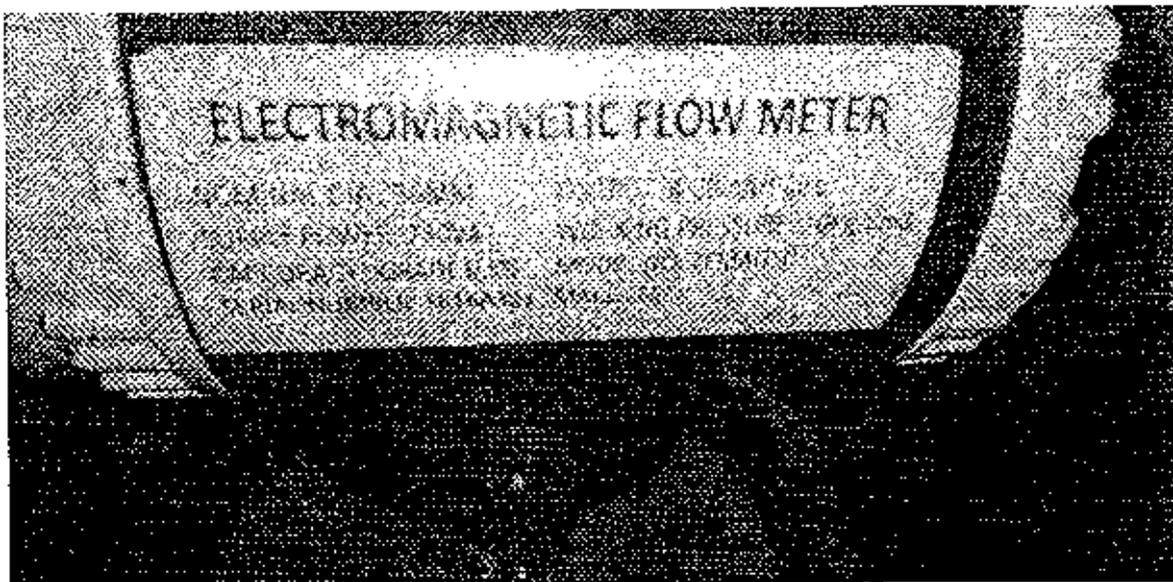

Borewell No. 4

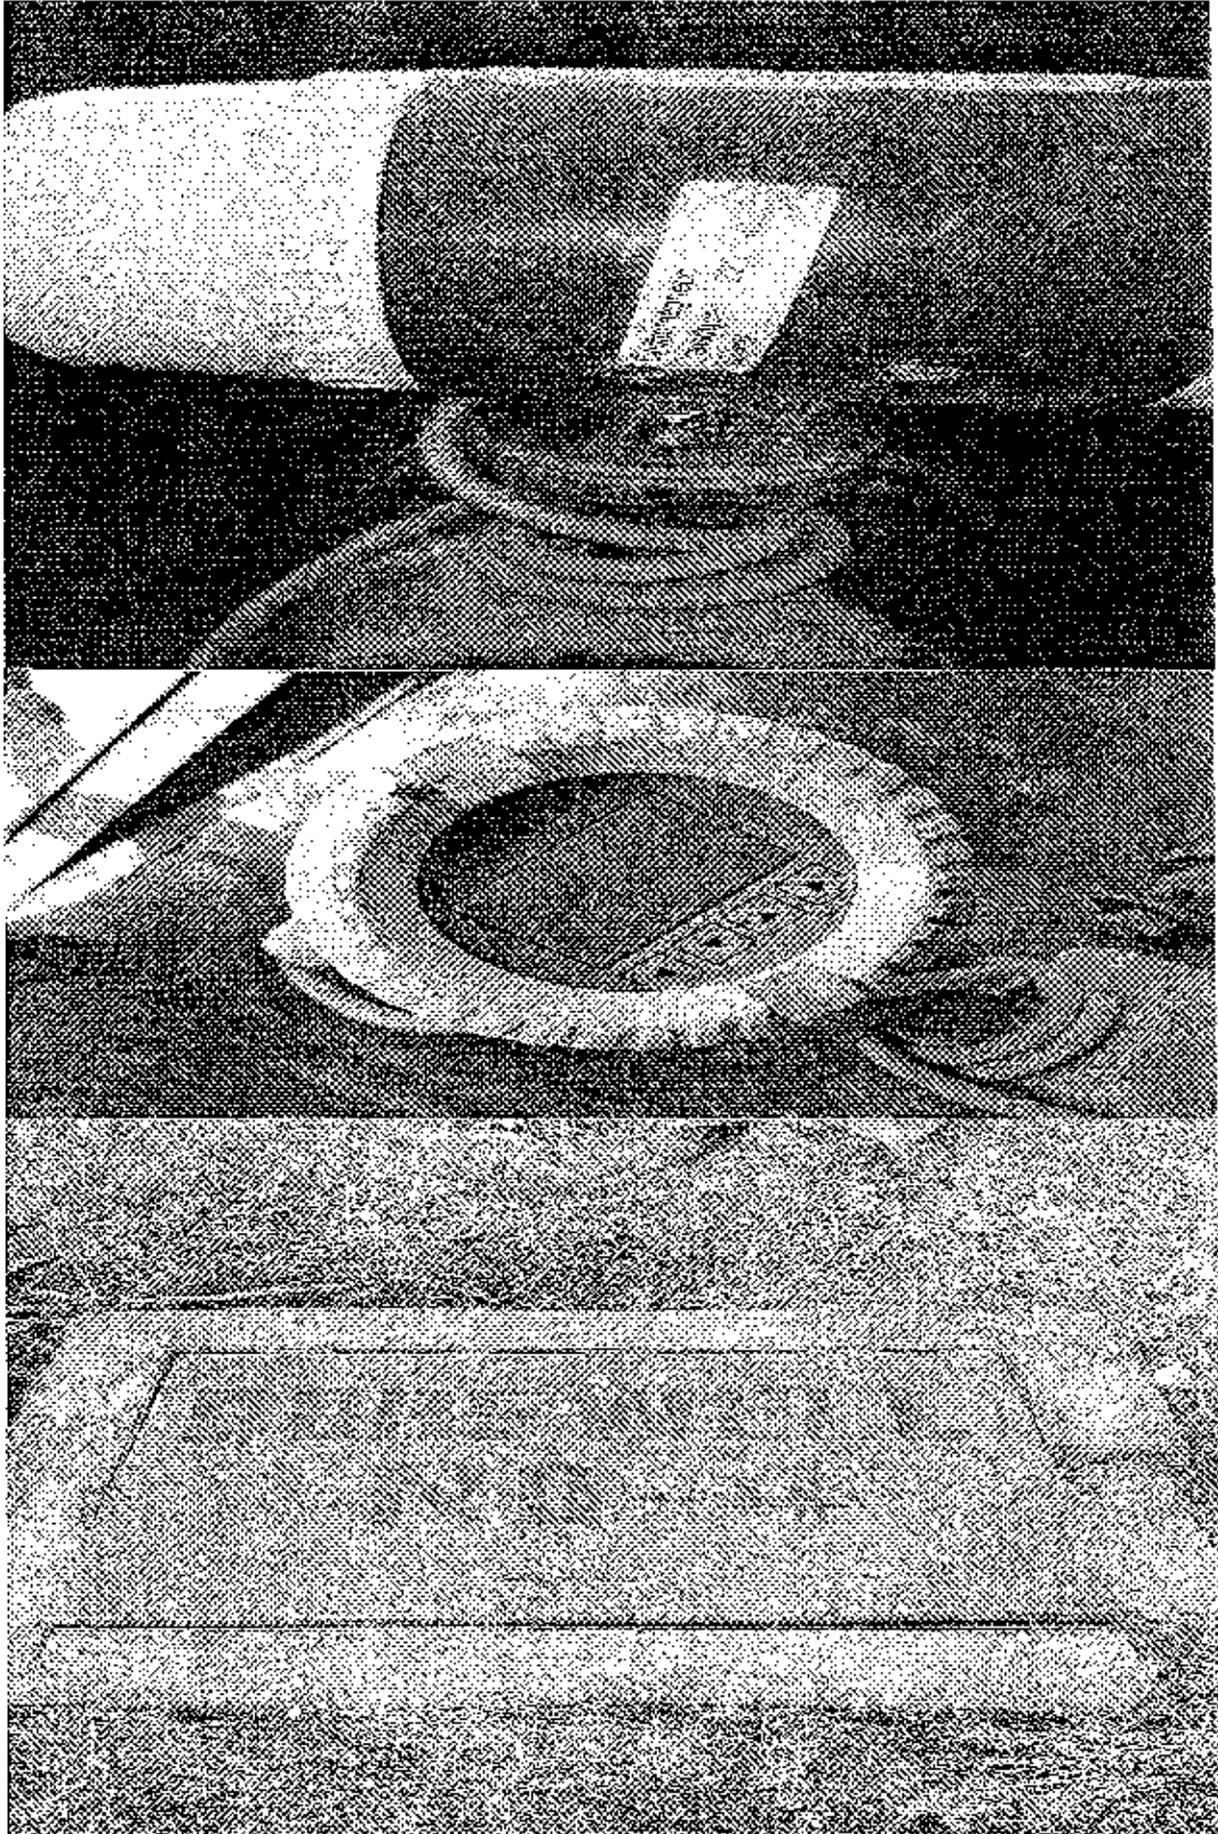



Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009 (Distt-NCT of N.D.).
 Contact No. 882684447, 9810249179, 882684447. E-mail: ekopro@ekopro.in, ekoproengineers@gmail.com, website: www.ekopro.in

TEST REPORT

Water Sample Analysis

Test Report No. : EKO/129/070621

Issue Date : 12/06/2021

Issued To : ASF INSIGNIA SEZ PVT. LTD.
 Village -Gwal Pahari
 Gurgaon Faridabad Road
 Gurgaon (Haryana) -122003

Sample Description : Ground Water
 Sample Drawn on : 05/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj kumar)
 Sample Received on : 07/06/2021
 Sampling Location : From Building No.-3
 Sampling Plan & Procedure : SOP-W/86
 Sample Quantity : 1.0 Litre
 Environmental Conditions : Normal
 Analysis Duration : 07/06/2021 To 11/06/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS: 10500-2012 (Amd.No.2 Sep-2018)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	--	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	--	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.32	--	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 P-21)	234.0	mg/L	200.0	300.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	65.2	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	380.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	174.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/l.	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 1622	Absent (<2)	MPN/100ml	Should be Absent	No relaxation
16	E.coli	IS: 1622	Absent	Per 100ml	Should be Absent	No relaxation

Remark:- Standard Applicable only for Drinking Water.





Office & Laboratory : 32/41, South Side of C. T. Road, UPSIDC Industrial Area, Faridabad - 201 009 (Distt-NCR) Haryana.
 Contact No: 98 10940370, 9810240373, 9826344457 E-mail: email@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in

TEST REPORT
Water Sample Analysis

Test Report No. : EKO/H30/070621

Issue Date : 12/06/2021

Issued To : ASF INSIGNIA SEZ PVT. LTD.
 Village - Gwal Pahari
 Gurgaon Faridabad Road
 Gurgaon (Haryana) -122003

Sample Description : Ground Water
 Sample Drawn on : 05/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj kumar)
 Sample Received on : 07/06/2021
 Sampling Location : From Building No.-2
 Sampling Plan & Procedure : SOP-W/65
 Sample Quantity : 1.0 Litre
 Environmental Conditions : Normal
 Analysis Duration : 07/06/2021 To 11/06/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS: 10500-2012	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	--	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	--	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.22	--	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 P-21)	284.0	mg/l.	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	120.0	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	490.0	mg/l.	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	210.0	mg/l.	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/l.	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/l.	0.06	No relaxation
15	Total Coliform	IS: 1022	Absent (<2)	MPN/100ml	Should be Absent	No relaxation
16	E.coli	IS: 1622	Absent	Per 100mL	Should be Absent	No relaxation

Remark:- Standard Application only for Drinking Water.





EKO PRO ENGINEERS PVT. LTD.
Environmental Consultants and Analytical Laboratory
(An ISO 9001:2015 Certified Company)

Office & Laboratory : 22A1, South Side of G-1 Road, UPSIDC Industrial Area, Ghaziabad - 201 002 (Distt-NCR) (U.P.)
Contact No.: 01126104227, 0110260670, 0826344437 E-mail : ecost@ekopro.in, ekoproengineers@gmail.com, ekopro@ecost.in

Test Report No. : EKO/130/070621

Issue Date : 12/06/2024

Notes:

1. The results given above are related to the tested sample, as received & mentioned parameters
The customer asked for the above tests only.
2. This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
3. The test report will not be used for any publicity/legal purpose.
4. The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report
5. Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.
SHIVANGI SINGH RAIZADA
SECTION INCHARGE MICROBIOLOGY
THE ENVIRONMENTAL CONSULTANTS
(Authorised Signatory)

For EKO PRO ENGINEERS PVT. LTD.
PURNIMA RAJAHAN
TECHNICAL MANAGER
THE ENVIRONMENTAL CONSULTANTS
(Authorised Signatory)



Office & Laboratory : 37/61, North Side of D. I. Road, IITGATE Industrial Area, Ghaziabad - 201 002 (Distt NCT) India.
 Contact No: 011-26102427; 9810240016; 9810244487 Email: enq@ekopro.in, ekoproengnrs@gmail.com, website: www.ekopro.in

TEST REPORT
Water Sample Analysis

Test Report No : EKO/101/200621 Issue Date : 02/07/2021
 Issued To : ASF INSIGNIA SEZ PVT. LTD,
 Village - Gwal Pahari
 Gurgaon Faridabad Road,
 Gurugram Haryana -122003

Sample Description : Ground Water
 Sample Drawn on : 30/06/2021
 Sample Drawn by : EPEPL (Mr. Harish Kumar)
 Sample Received on : 30/06/2021
 Sampling Location : From Borewell - HDR, (Residential Building)
 Sampling Plat. & Procedure : SOP-W/06
 Sample Quantity : 1.0 Litre
 Environmental Conditions : Normal
 Analysis Duration : 30/06/2021 To 03/07/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS:10500-2012 (Amtd.No.2 Sep-2018)	
					Acceptable	Permissible*
1	Colour	IS: 3025 (P-4)	<1.0	Mazen	5.0	15.0
2	Odeur	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.24	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	310.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	109.5	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-50)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	484.0	mg/L	500.0	2000.0
12	Phenolic Compounds (as C6H5OH)	IS : 3025 (P-43)	<0.001	mg/L	0.001	0.002
13	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.06	No relaxation
14	Total Alkalinity (as CaCO ₃)	IS : 3025 (P-23)	160.0	mg/L	200.0	600.0
15	Total Coliform	IS : 3022	Absent (<2)	MPN/100ml	Should be Absent	-
16	E.coli	IS : 3022	Absent	Per 100mL	Should be Absent	-

Remark: *It is recommended that the acceptable limit is to be implemented. Values in excess of those mentioned under 'acceptable' render the water not suitable, but still may be tolerated in the absence of an alternative source but up to the limits indicated under 'permissible limit in the absence of alternate source'

Notes:

- The results given above are related to the tested sample, as received & mentioned parameters. The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

SIKHWANGI SINGH RAIZAYIA
 (Authorised Signatory)
 SAVE THE ENVIRONMENT

For EKO PRO ENGINEERS PVT. LTD.

VEDNAMA CHATURAN
 (Authorised Signatory)
 SAVE THE ENVIRONMENT



Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009 (Distt-NCR) INDIA.
Contact No. : 9515403427, 9810240675, 9826349487 E-mail : ekopro@ekopro.in, ekoproengineers@gned.com, website : www.ekopro.in

TEST REPORT
Water Sample Analysis

Test Report No. : EKO/12B/070621

Issue Date : 12/06/2021

Issued To : ASF INSIGNIA SEZ PVE. LTD.
Village -Gwal Pahari
Gurgaon Faridabad Road
Gurgaon (Haryana) -122003

Sample Description : Ground Water
Sample Drawn on : 05/06/2021
Sample Drawn by : EPEPL (Mr. Anuj kumar)
Sample Received on : 07/06/2021
Sampling Location : Stand By Borewell
Sampling Plan & Procedure : SOP-W/66
Sample Quantity : 1.0 Litre
Environmental Conditions : Normal
Analysis Duration : 07/06/2021 To 11/06/2021
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS: 10500-2012 (Amd.No.2 Sep-2018)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.19	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	240.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-63)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	75.2	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	430.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	182.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 1622	Absent (<2)	MPN/100ml	Should be Absent	No relaxation
16	E.coli	IS: 1622	Absent	Per 100mL	Should be Absent	No relaxation

Remark:- Standard Applicable only for Drinking Water.





EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory
(An ISO 9001:2015 Certified Company)

Office & Laboratory : 22/41, South Side of G. T. Road, UPBDC Industrial Area, Ghaziabad - 201 002 (Distt-NCT); U.P.
Contact No.: 9910-05427, 9910240678, 9926344457 E-mail: ekopro@yahoo.co.in, ekoproengineers@gmail.com, ekopro www.ekopro.in

Test Report No. : EKO/12H/070621

Issue Date : 12/06/2021

Notes:

1. The results given above are related to the tested sample, as received & mentioned parameters
The customer asked for the above tests only.
2. This test report will not be generated again, either wholly or in part, without prior written permission of the Laboratory.
3. The test report will not be used for any publicity/legal purpose.
4. The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
5. Responsibility of the Laboratory is limited to the invoiced amount only.

****End of Report****

For EKO PRO ENGINEERS PVT. LTD.

SPIVANGHOSH BARRAZADA
SECTION INCHARGE MICROBIOLOGY
(Authorized Signatory)

For EKO PRO ENGINEERS PVT. LTD.

PURNIMA CHAUHAN
TECHNICAL MANAGER
(Authorized Signatory)



C/L

ANIL KUMAR - JPL

Date: 10.11.2021

To,
Chairman, T.C.C
Cum Additional Deputy Commissioner, Gurgaon

Subject: Submission of CGWA compliance for IT/ Information Technology Enable Services (SEZ) project at Village- Gwal Pahari, Gurgaon -- Faridabad road, Tehsil Wazirabad, District Gurgram, Haryana by M/s ASF Insignia SEZ Pvt. Ltd.


Reference No: Chairman, T.C.C cum Additional Deputy Commissioner, Gurgaon letter no. 1011 dated 23.11.2010

Dear Sir,

This is with reference to the above captioned subject; we are here with submitting quarterly compliance report for the period July 2021 to September 2021 and The Ground Water Level monitoring report dated 07.10.2021 at 8 (eight) different locations at IT/ITES Project ASF Insignia SEZ Pvt. Ltd.

Thanking you,

For ASF INSIGNIA SEZ PVT. LTD.



Authorised Signatory

Encl: As above

CC:

1. Member Secretary, CGWA, New Delhi.
2. Hydrologist Office, Ground Water Cell, Gurgaon, Haryana.

Copy forwarded to the Hon. Secy, Dept.

FORWARDED TO THE CHAIRMAN
T.C.C. Gurgaon for the compliance report
submitted on 10.11.2021
Signature: [Signature]
Name: [Name]
Designation: [Designation]



ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office : ASF Insignia SEZ (IT/ITES), Vasant Valley (Gwal Pahari), off Gurgaon-Faridabad Road, Gurugram-122008, Haryana

E: (+91 124 4777200) / (+91 124 4234110) corporate@asfinfrastruc.com w: www.asfinfrastruc.com

Regd. Office : 11, Bahar Lane, Bengali Market, New Delhi-110001 / (+91 11 23255511) / (+91 1123735280)

Corp. Office : ASF Centre, 302-353, Udyog Vihar, Phase-IV, Gurugram-122018 (India)

CIN U45201DL2006PTC140108

Creating Intelligent Spaces®

(AOC)
14/11/21

10/11/2021
(Hydrologist)

COMPLIANCE OF THE CONDITIONS AS PER THE NO OBJECTION CERTIFICATE OBTAINED FROM CHAIRMAN, T.C.C CUM ADDITIONAL DEPUTY COMMISSIONER, GURGAON VIDE LETTER NO: 1011 DATED 23.11.2010 (ANNEXURE-I). PERIOD July 2021 – September 2021.


CONDITIONS

S.NO.	CONDITIONS	COMPLIANCE
1	The ground water from the tube well shall be exclusively used for drinking purpose only and not for construction or any other purpose. The applicant will have to submit the undertaking on affidavit for the same.	Being Complied. The ground water from the tube well is being exclusively used for drinking purpose only. The affidavit stating the same has already been submitted.
2	The applicant shall take up Rain Water Harvesting system in project area.	Complied. Total 21. nos of Rain Water Harvesting Pits are operational at the site.
3	Treated waste water shall be utilized for gardening and flushing purposes by dual water supply system	Complied. Treated waste water is being utilized for gardening and flushing purposes by dual water supply system.
4	Photograph of the recharge structure is to be submitted immediately after completion to Chairman T.C.C. Gurgaon.	Complied. Photograph of the recharge structure has been submitted to the office of Chairman T.C.C. Cum Additional Deputy Commissioner Gurgaon.
5	After getting the drinking water supply from concerned Private/Govt. agency, applicant would not to be allowed abstraction of ground water through this tube well.	Noted.



6	The applicant will have to submit the depth, diameter, H.P. of primemover and exact location (Khasra no., Killa no.) as per revenue record of permitted tube well along with photograph within 15 days after getting permission letter. Otherwise the permission will be withdrawn. No further drilling or deeping of the tube well should be carried out.	Being Complied. Details already submitted
7	The ground water level in the tube wells is to be monitored at least quarterly (January, May, August & November) in a year on regular basis and ground water quality is to be monitored twice in a year during pre and post monsoon period and data to be submitted Hydrologist office, Ground Water Cell Gurgaon on regular basis.	Complied. We are regularly submitting the required data to your esteemed office. latest Ground Water Level report & Ground Water Test Report is attached as an <i>Annexure II & II-A</i> .
8	Violation of the above mentioned conditions, T.C.C. Gurgaon reserves its rights to withdraw/cancel the permission of the said tube well at any time without assigning any reason, if the contingency so demand	Noted.





RAJ ROSEWELL & PROJECTS

Specialists in Rain Water Harvesting, Tubewell Drilling, Borecasting,
Trenching Projects, Re-development of Old Borewells

Office : Ambience Market, First Floor, Opp. Indian Oil Corp., Sector - 13, Gurgaon Road, Faridkot - 122007
E-mail : rajrosowell@gmail.com ; Phone : +91-98111-41355

Ref. No.

Date 07.10.2021

M/s ASF Insignia SEZ Pvt. Ltd.
ASF Centre
Udyog Vihar, Phase - 4
Gurgaon- 122016

Sub : Checking of water level of the existing bore of site M/s ASF insignia
SEZ Pvt. Ltd. Village, Gwal Pahari, Tehsil -Wajirabad, Distt. Gurgaon
Haryana. (July-21 to Sept-21)

Dear Sir

As per our finding following are the water level of different bores for the period
July-21 to Sept-21 at the subject site:-

- | | | |
|------------------------|---|--|
| 1. Marked B.W No. I | - | Cooling Tower WL at 121 ft. |
| 2. Marked B.W No. II | - | Ground Floor, Tower-1, South WL at 122 ft. |
| 3. Marked B.W No. III | - | Basement-3, Tower-3, WL at 85 ft. |
| 4. Marked B.W No. IV | - | Housing Northwest WL at 124 ft. |
| 5. Marked B.W No. V | - | Housing East WL at 121 ft. |
| 6. Marked B.W No. VI | - | Behind residential building WL at 120 ft. |
| 7. Marked B.W No. VII | - | North of B3 Building 1 WL at 118 ft. |
| 8. Marked B.W No. VIII | - | North of B3 Building 2 WL at 122 ft. |

Thanking You,

Yours truly,



Raj Rosewells & Projects

Authorized signatory


 Office & Laboratory : 32/61, South Side of G. T. Road, UPSIDC Industrial Area, Ghaziabad - 201 008 (Main-NCR) INDIA
 Contact No. : 9810405327, 9810242670, 9826344487 E-mail : email@ekopro.in, ekoproengineers@gmail.com, ekops@ekopro.in

TEST REPORT

Water Sample Analysis

Test Report No. : EKO/130/070621

Issue Date : 12/06/2021

Issued To

 : ASF INSIGNIA SEZ PVT. LTD.
 Village - Qwal Pahari
 Gurgaon Faridabad Road
 Gurgaon (Haryana) -122003

 Sample Description : Ground Water
 Sample Drawn on : 05/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj Kumar)
 Sample Received on : 07/06/2021
 Sampling Location : From Building No.-2
 Sampling Plan & Procedure : SQP-W/86
 Sample Quantity : 1.0 Litre
 Environmental Conditions : Normal
 Analysis Duration : 07/06/2021 To 11/06/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS: 10500:2012	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.22	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	284.0	mg/L	200.0	500.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	120.8	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-00)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	490.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	210.0	mg/L	200.0	500.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500-CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 1622	Absent (<2)	MPN/100ml	Should be Absent	No relaxation
16	E.coli	IS: 1622	Absent	Per 100ml	Should be Absent	No relaxation

Remark:- Standard Applicable only for Drinking Water.





EKO PRO ENGINEERS PVT. LTD.

Environmental Consultants and Analytical Laboratory
(An ISO 9001:2015 Certified Company)

Office & Laboratory : 32/41, South Side of G.T. Road, UPSIDC Industrial Area, Ghaziabad - 201 009 (Distt. GZT) INDIA
Contact No. 08-18405427, 9810240678, 9826244487 E-mail: ekopro@ecolabpro.in, ekoproengineers@gmail.com, website: www.ekopro.in

TEST REPORT

Water Sample Analysis

Test Report No.: EKO/129/070621

Issue Date : 12/06/2021

Issued To

: ASF INSIGNIA SEZ PVT. LTD.
Village - Gwal Pahari
Gurgaon Faridabad Road
Gurgaon (Haryana) -122003

Sample Description : Ground Water
Sample Drawn on : 05/06/2021
Sample Drawn by : EPEPL (Mr. Anuj Kumar)
Sample Received on : 07/06/2021
Sampling Location : From Building No.-3
Sampling Plan & Procedure : SOP-W/06
Sample Quantity : 1.0 Litre
Environmental Conditions : Normal
Analysis Duration : 07/06/2021 To 11/06/2021
Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS: 10500-2012 (Amd. No.2 Sep-2013)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.82	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	784.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	657	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	360.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	174.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-43)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 1622	Absent (<2)	MPN/100ml	Should be Absent	No relaxation
16	E.coli	IS: 1622	Absent	Per 100ml	Should be Absent	No relaxation

Remark:- Standard Applicable only for Drinking Water.





Office & Laboratory : 32/41, South Side of G. T. Road, UPSIDCO Industrial Area, Ghazabad - 201 008 (Delhi-NCR) INDIA
 Contact No.: 9211405427, 9210240678, 9926344487; E-mail: email@ekopro.in, ekoproengineers@gmail.com; website: www.ekopro.in

TEST REPORT

Water Sample Analysis

Test Report No: EKO/10/300621

Issue Date: 03/07/2021

Issued To

: AGP INSIGNIA SEZ PVT. LTD.
 Village - Gwal Pahari
 Gurgaon Faridabad Road,
 Gurugram, Haryana - 122003.

Sample Description : Ground Water
 Sample Drawn on : 30/06/2021
 Sample Drawn by : EPEPL (Mr. Harish Kumar)
 Sample Received on : 30/06/2021
 Sampling Location : From Borewell - IDR, (Residential Building).
 Sampling Plan & Procedure : SOP-W/66
 Sample Quantity : 1.0 Litre
 Environmental Conditions : Normal
 Analysis Duration : 30/06/2021 To 03/07/2021
 Remark (If any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS:10500-2012 (Amd.No.2 Sep-2018)	
					Acceptable	Permissible*
1	Colour	IS: 3025 (P-4)	<1.0	Hexen	5.0	15.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.24	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	310.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-55)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	109.6	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-26)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-60)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	484.0	mg/L	500.0	2000.0
12	Phenolic Compounds (as OHSO ₂)	IS: 3025 (P-43)	≤0.001	mg/L	0.001	0.002
13	Cyanide (as CN)	APHA 4500-CN-H	Absent	mg/L	0.05	No relaxation
14	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	190.0	mg/L	200.0	600.0
16	Total Coliform	IS: 1622	Absent (≤2)	MPN/100 ml	Should be Absent	
19	E.coli	IS: 1622	Absent	Per 100ml	Should be Absent	


Remark: *It is recommended that the acceptable limit is to be implemented. Values in excess of those mentioned under 'acceptable' render the water not suitable, but still may be tolerated in the absence of an alternative source but up to the limits indicated under 'permissible' limit in the absence of alternate source.

Notes:


- The results given above are related to the tested sample, as received & mentioned parameters.
- The customer asked for the above tests only.
- This test report will not be generated again, either wholly or in part, without prior written permission of the laboratory.
- The test report will not be used for any publicity/legal purpose.
- The test samples will be disposed off after 15 days from the date of issue of test report, unless until specified by the customer. Sample received for biological tests will be destroyed after 7 days from the date of issue of test report.
- Responsibility of the Laboratory is limited to the invoiced amount only.

End of Report

For: EKO PRO ENGINEERS PVT. LTD.



For: EKO PRO ENGINEERS PVT. LTD.





Contact : +91 - 96116243870

EKO PRO ENGINEERS PVT. LTD.
 Environmental Consultants and Analytical Laboratory
 (An ISO 9001:2016 Certified Company)

Office & Laboratory : 32/41, South Side of E. T. Road, UPSIDC Industrial Area, Ghazabad - 201 009 (Delhi-NCR) INDIA
 Contact No : 9819403427, 9611624387/0, 9826344467 E-mail : email@ekopro.in, ekoproengineers@gmail.com, website : www.ekopro.in

TEST REPORT

Water Sample Analysis

Test Report No. : EKO/12B/070621 Issue Date : 12/06/2021


Issued To : ASF INSIGNIA SEZ PVT. LTD.
 Village - Gwal Bahari
 Gurgaon Faridabad Road
 Gurgaon, (Haryana) -122003

Sample Description : Ground Water
 Sample Drawn on : 05/06/2021
 Sample Drawn by : EPEPL (Mr. Anuj Kumar)
 Sample Received on : 07/06/2021
 Sampling Location : Stand By Borewell
 Sampling Plan & Procedure : SOP-W/06
 Sample Quantity : 1.0 Litre
 Environmental Conditions : Normal
 Analysis Duration : 07/06/2021 To 11/06/2021
 Remark (if any) : NA

RESULTS

S. No.	Parameters	Test Methods	Results	Units	Limits as per IS: 10500-2012 (Amd. No.2 Sep-2018)	
					Acceptable	Permissible
1	Colour	IS: 3025 (P-4)	<1.0	Hazen	5.0	35.0
2	Odour	IS: 3025 (P-5)	Agreeable	-	Agreeable	Agreeable
3	Taste	IS: 3025 (P-7)	Agreeable	-	Agreeable	Agreeable
4	Turbidity	IS: 3025 (P-10)	<1.0	NTU	1.0	5.0
5	pH	IS: 3025 (P-11)	7.19	-	6.5-8.5	No relaxation
6	Total Hardness (as CaCO ₃)	IS: 3025 (P-21)	240.0	mg/L	200.0	600.0
7	Iron (as Fe)	IS: 3025 (P-53)	<0.1	mg/L	1.0	No relaxation
8	Chloride (as Cl)	IS: 3025 (P-32)	75.2	mg/L	250.0	1000.0
9	Residual Free Chlorine	IS: 3025 (P-28)	<0.1	mg/L	0.2	1.0
10	Fluoride (as F)	IS: 3025 (P-00)	<1.0	mg/L	1.0	1.5
11	Total Dissolved Solids	IS: 3025 (P-16)	430.0	mg/L	500.0	2000.0
12	Total Alkalinity (as CaCO ₃)	IS: 3025 (P-23)	182.0	mg/L	200.0	600.0
13	Phenolic Compounds (as C ₆ H ₅ OH)	IS: 3025 (P-23)	<0.001	mg/L	0.001	0.002
14	Cyanide (as CN)	APHA 4500 CN-K	Absent	mg/L	0.05	No relaxation
15	Total Coliform	IS: 1622	Absent (<2)	MPN/100ml	Should be Absent	No relaxation
16	E.coli	IS: 1622	Absent	Per 100mL	Should be Absent	No relaxation

Remark:- Standard Applicable only for Drinking Water.



B-1

From

Chairman, T.C.C.
Cum Additional Deputy Commissioner, Gurgaon.

To

Canton Buildings Pvt Ltd, 362/363 ASF Circle Vidyotsakh
Gurgaon

No. 1011

dated

Sub:

N.O.C. for regularization of existing tubewells for drinking & domestic purpose.

Memo.

With reference to your application no _____ dated
2-8-2010 on the above cited subject the Technical Core Committee
has no objection for withdrawal of ground water from existing Eight
tubewell located at Village Gawal Pahali.

The N.O.C. is subject to the following terms & conditions :-

- 1 The ground water from the tubewell shall be exclusively used for drinking & domestic purpose only and not for construction or any other purposes. The applicant will have to submit the undertaking on affidavit for the same.
- 2 The applicant shall take up Rain Water Harvesting scheme in the project area.
- 3 Treated waste water shall be utilized for gardening and flushing purposes by providing dual water supply system.
- 4 Photograph of the recharge structure is to be submitted immediately after completion to the chairman T.C.C, Gurgaon.
- 5 After getting the drinking water supply from concerned Private/Govt. agency, the applicant would not be allowed abstraction of ground water through this tubewell.
- 6 The applicant will have to submit the depth, diameter, H.P. of primemover and exact location (Khasra no., Killa no.) as per revenue record of the permitted tubewell alongwith photograph within 15 days after getting permission letter, otherwise the permission will be withdrawn. No further drilling or deeping of the tubewell should be carried out.
- 7 The ground water level in the tubewells is to be monitored atleast quarterly (January, May, August & November) in a year on regular basis and ground water quality is to be monitored twice in a year during pre & post monsoon period and data to be submitted to Hydrologist office, Ground Water Cell Gurgaon on regular basis.
- 8 Violation of the above mentioned conditions, T.C.C. Gurgaon reserves its rights to withdraw/cancel the permission of the said tubewell at any time without assigning any reason, if the contingency so demand.

Chairman, T.C.C.

Cum Additional Deputy Commissioner, Gurgaon.

No. 1012 dated

A copy is forwarded to Member Secretary, C.G.W.A. New Delhi for favour of information & necessary action please.

Chairman, T.C.C.

Cum Additional Deputy Commissioner, Gurgaon.

B. S. YADAV HAS-II
Asst. Geologist
Ground Water Cell, Gurgaon

As per record available the copy
has been compared with the original
office copy and found correct

28/3/16

Date: 25.03.2010



To,

The Chairman-TCC
Cum Addl. Dy. Commissioner,
Vikas Sadan
Gurgaon

Sub.: Request for providing original copy/ certified copy of the NOC dated 23.11.2010 granted to Canton Buildwell Pvt. Ltd.(Now) ASF Insignia SEZ Pvt. Ltd.) for 8 tubewells for drinking and domestic purposes.

Ref.: Your NOC vide Memo No. 1011 dated 23.11.2010

Dear Sir,

This has reference to the above referred NOC dated 23.11.2010 issued to Canton Buildwell Pvt. Ltd. (now known as ASF Insignia SEZ Pvt. Ltd.). This is to bring to your kind notice that the original copy of the above mentioned NOC is somehow not traceable in our records, and perhaps it was never received by us, and we are having only a copy of the office copy of the Deptt. in our records.

It is therefore requested that we may kindly be provided with the original copy of the said NOC issued in our favour vide Memo No. 1011 dated 23.11.2010.

In the alternate, we may be provided with a duly authenticated /certified copy of the said NOC at the earliest.

Thanking you,

Yours faithfully,
For ASF INSIGNIA SEZ PVT.LTD.
(formerly known as Canton Buildwell Pvt. Ltd.)

AUTHORIZED SIGNATORY

Encl. Photocopy of NOC vide Memo No. 1011 dated 23.11.2010.

Hydrologist To supply
URGENT certified copy
Put up on
urgently
ADC



de

14 April 2021

To,

The Regional Officer,
Haryana State Pollution Control Board
Gurgaon

Sub.: Submission of Form- V, Environmental Statement for the financial year 01.04.2020 to 31.03.2021

Dear Sir,

We are enclosing herewith Form-V for the period from **01.04.2020 to 31.03.2021** i.e. Environmental Statement for the financial year 2020 to 2021 for our site at Village Gwal Pahari, Tehsil Wazirabad Distt. Gurgaon (Haryana).

Thanking you,
Yours faithfully,


For ASF INSIGNIA SEZ PVT.LTD.



Authorized Signatory

Encl: As Above

CC: The Chairman
Haryana State Pollution Control Board,
C-11, Sector-6, Panchkula

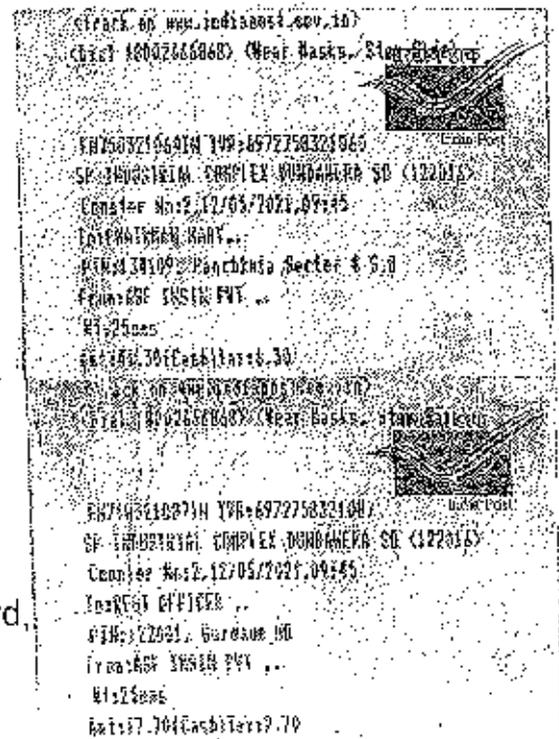

ASF INSIGNIA SEZ PRIVATE LIMITED

Site Office : ASF Insignia SEZ (IT/Res), Vatsal Valley (Gwal Pahari), off Gurugram-Faridabad Road, Gurugram-122003, Haryana
t: +91 124 4777200 f: +91 124 4234110 e: corporate@asfinfrastructure.com w: www.asfinfrastructure.com
Regd. Office : 11, Bebar Lane, Bangal Market, New Delhi-110001 t: +91 11 29355511 f: +91 1123739290
Corp. Office : ASF Centre, 352-363, Udyog Vihar, Phase-IV, Gurugram-122016 (India)

CIN : U45201DL2005PTC140408

Creating Intelligent Spaces®

FORM - V
(See Rule-14)

Environmental Statement for the financial year 01.04.2020 - 31.03.2021

Part-A

- (i) Name and address of owner/occupier of the Industry, operation or process : ASF Insignia SEZ Pvt. Ltd.
Village Gwal Pahari, Sub-Tehsil
Wazirabad Distt. Gurgaon, Haryana
- (ii) Industry category: Primary (STC code) : IT/ITES Special Economic Zone
Secondary- (SIC Code)
- (iii) Production capacity: Units : Not Applicable.
- (iv) Year of establishment : November, 2011
- (v) Date of last environmental statement submitted :

Part - B

Water and Raw material consumption

(i) Water consumption m³/day:

- Process : NIL
Cooling : 25 m³ /day (25 m³ /day treated sewage)
Domestic : 176 m³/day (176 m³ /day extracted from ground through approved tube well)
Horticulture : 100 m³ /day (100 m³ /day treated sewage)

HUDA WATER SOURCE NOT PROVIDED YET

S. No.	Name of Products	Process water consumption per unit of product output	
		During the previous financial year	During the current financial year
1.	Not Applicable	Not Applicable	Not Applicable

(ii) Raw Material consumption : Not Applicable

S. No.	*Name of Raw Material	Name of Products	Consumption of raw material per unit output	
			During the previous financial year	During the current financial year
1.				
2.				
3.				

* Industry may use if disclosing details of raw material would violate contractual obligations; otherwise all industries have to name the raw material used.



Part - C
Pollution discharged to environment /unit of output
 (Parameters as specified in the consent issued)

	Pollutants	Quantity of pollutants discharged (mass/day)	Concentration of pollutants in discharges (mass/volume)	Percentage variation from prescribed standards with reasons
(a) Water	Zero Discharge Unit. No pollutants discharged into the environment as the entire sewage is treated and the entire (100%) treated effluent from STP is used for cooling towers and horticulture. The monitoring report of STP effluent is enclosed as <i>Annexure - I</i> .	Not Applicable	Not Applicable	Not Applicable
(b) Air	Emissions from stacks of back-up DG sets (operated only during power failure) The Stack Emission monitoring report is attached as an <i>Annexure - II</i>	The results of monitoring of DG stack emissions from approved laboratory is enclosed as Annex 2		


Part - D
Hazardous Wastes

(As specified under Hazardous Wastes (Management, Handling and Trans-boundary Movement) Rules.

	Hazardous Wastes	Total Quantity (kg)	
		During the previous financial year	During the current financial year
(a) From process	Used Oil from DG sets	3080 L	6160 L
(b) From Process	E-Waste (Burnt lights, hardware etc)	1000 KG	NIL
(c) From pollution control facilities	Not Applicable	Not Applicable	Not Applicable

Part - E
Solid Wastes

	Solid Wastes	Total Quantity (kg)	
		During the previous financial year	During the current financial year
(a) From process (IITATES Special Economic Zone)	1) Wet Garbage	174562 KG	6322 KG
	2) Dry Garbage	154826 KG	47910 KG
	3) Scrap	NIL	NIL
(b) From pollution control facility	STP Sludge	227990 KG	17061.6 KG
(c) (1) Quantity recycled or re-utilizes within the unit	1) Dewatered STP Sludge is used as manure in	NIL	



(2) Sold	horticulture		
	1) Scrap		NL
(3) Disposed	1) Wet Garbage is disposed to Govt. of Haryana authorized vendor.	174562 KG	6322 KG
	2) Dry Garbage is disposed to Govt. of Haryana authorized vendor	154826 KG	47910 KG

Part - F

Please specify the characterizations (in terms of composition of quantum) of hazardous as well as solid wastes and indicate disposal practice adopted for both these categories of wastes.

Solid wastes	Solid Wastes are segregated into organic biodegradable wastes (Waste vegetables, food, etc) , non-biodegradable wastes (paper, plastic, glass, etc) and Domestic Hazardous waste (sanitary & other non recyclable & non combustible waste) and collected in separate bins. The said wastes are disposed to MCG/ State Govt. Approved vendor.
Hazardous wastes	The used oil from DG sets is sold to authorized waste recycler.

Part - G

Impact of the pollution abatement measures taken on conservation of natural resources and the cost of production.

Treated effluent from STP is recycled for use in toilet flushing, Air-conditioning and horticulture

Part - H


Additional measures/investment proposal for environmental protection including abatement of pollution, prevention of pollution.

All measures for environmental protection and abatement/ prevention of pollution have already been taken. Therefore, no additional measure is envisaged.




Part - I

Any other particulars for improving the quality of the environment:


1. The entire sewage is treated up to the tertiary level in the STP.
2. The entire (100%) treated effluent from STP is recycled for use in HVAC, toilet flushing & horticulture.
3. Required stack height for DG sets provided as per norms to reduce air pollution.
4. Acoustic treatment of DG room for reduction/control of noise as per norms.
5. Adequate tree plantation has been carried out for dust control, noise control, protection from pollutants in air, shading and aesthetics.
6. Rainwater harvesting pits have been provided for recharge of groundwater.
7. Solid wastes are segregated and recycled through authorized vendors.
8. Operation of anti smog gun for dust control, for its application, 24 KLD of STP Treated Water is being used
9. Installation of Online monitoring system for STPs




Photograph of sanitation facilities

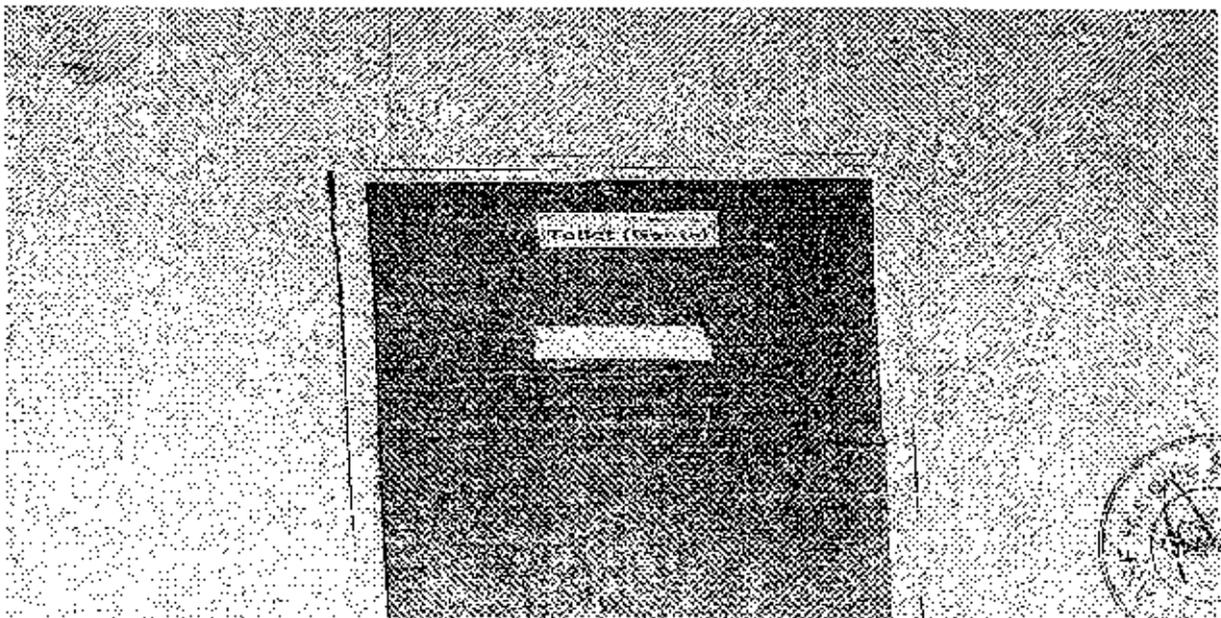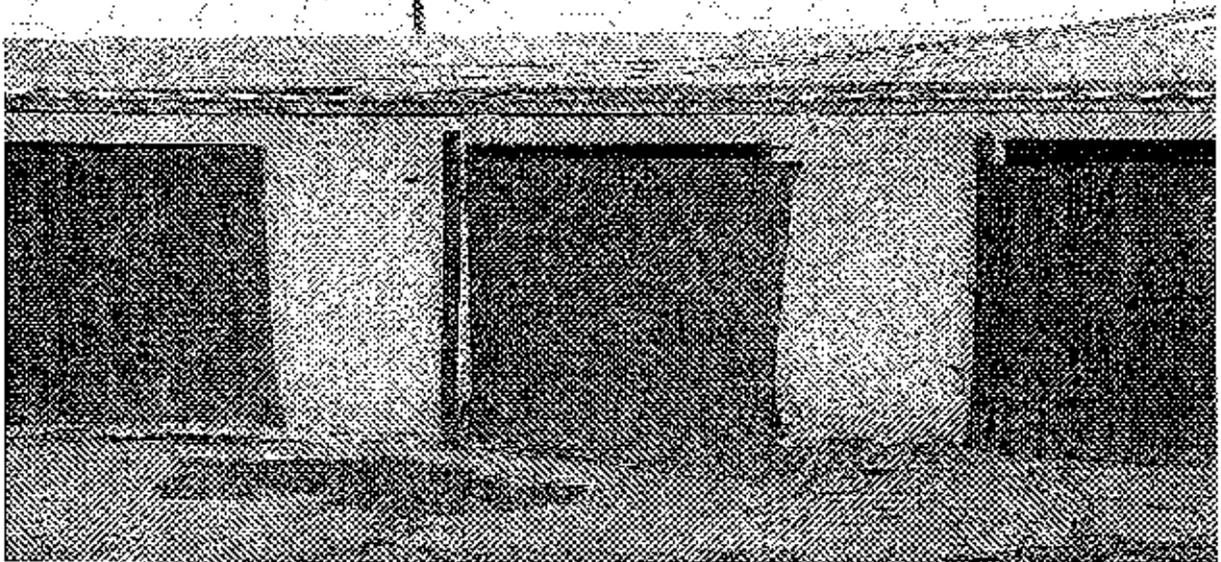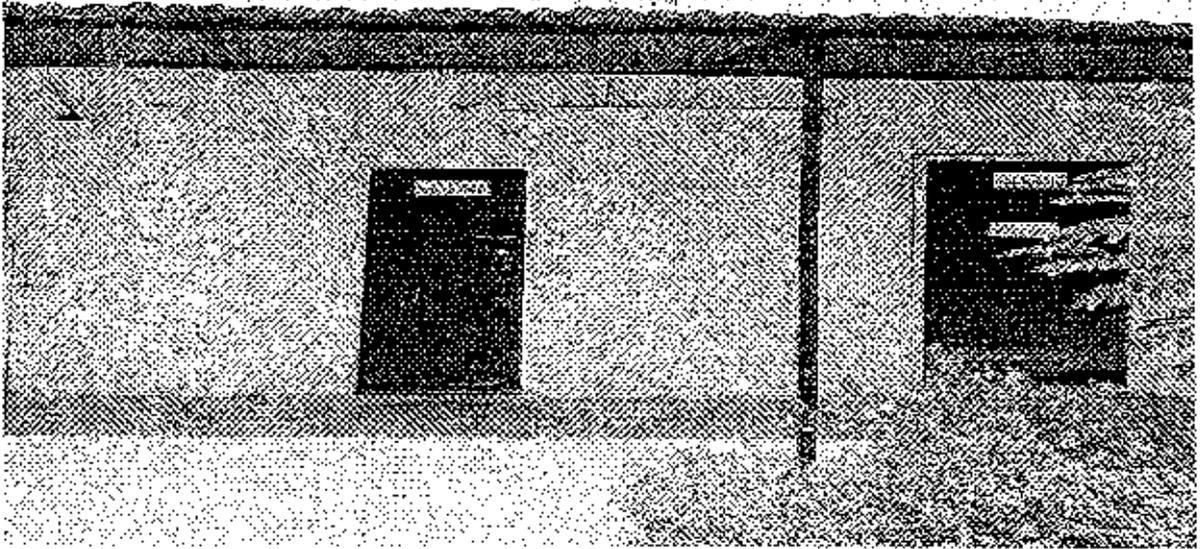

Photograph of sanitation facilities

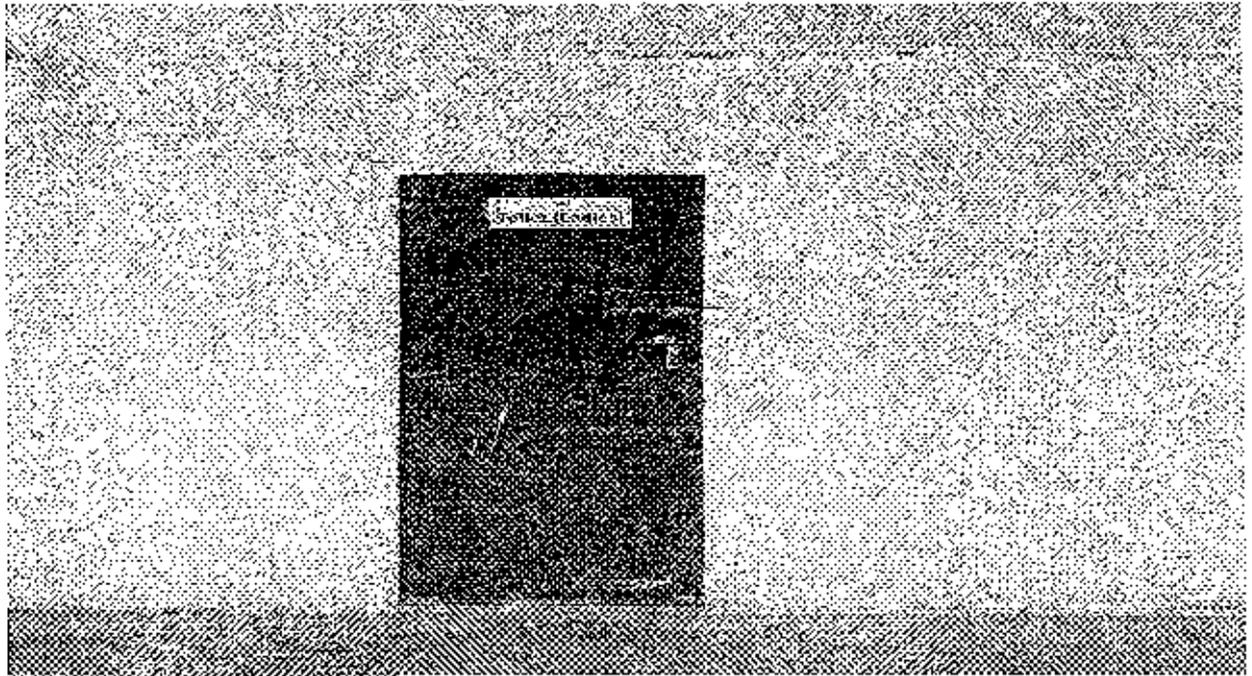

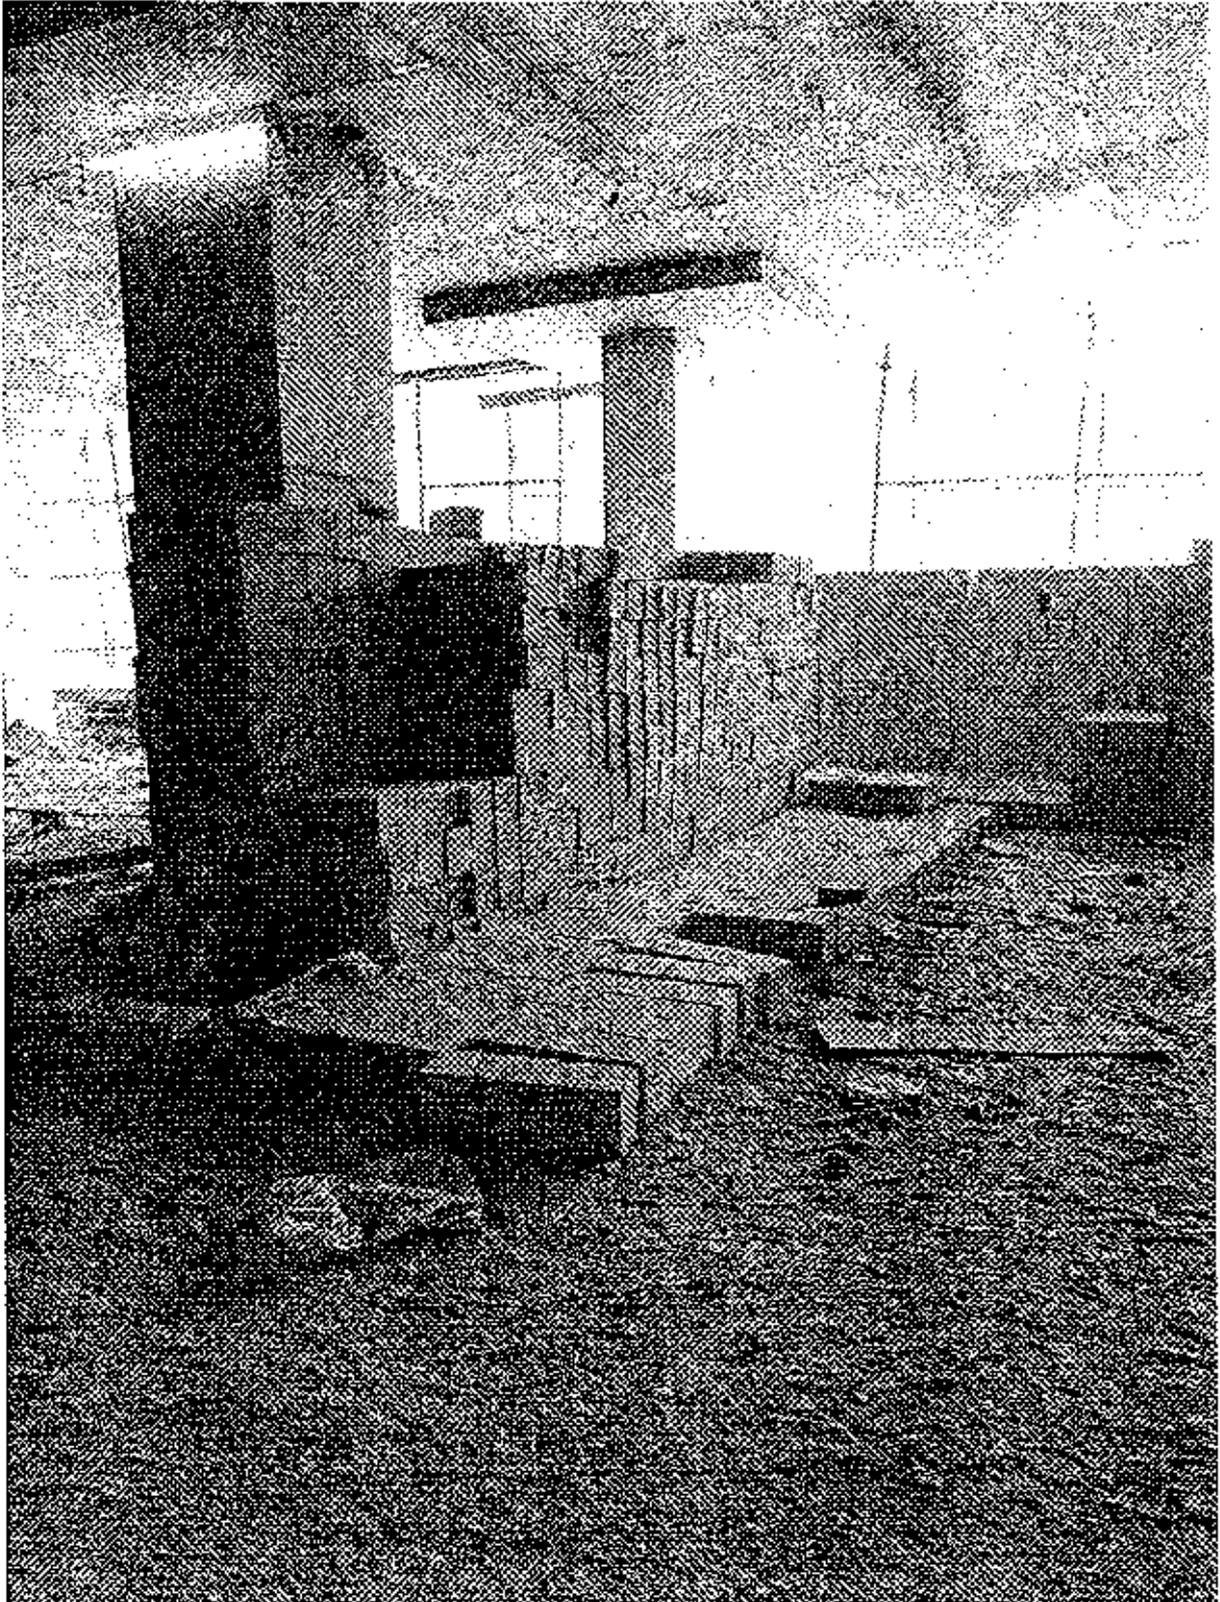

Photograph of AAC Blocks





ENVIRONMENTAL POLICY

ASF Group is extremely sensitive to protection of the environment and actively undertakes to continuously indóctrinate measures, existing and new, to conserve the environment. ASF Group strives to carry out it's Business activities and operations in a manner that not only diligently refrains from causing any adverse impact on the environment but also take preemptive measures to reduce & mitigate any adverse impact on environment owing to externalities associated with it's business/operations. We are conscious of our responsibility and uphold the philosophy to protect and conserve the environment with utmost accountability.

Our Policy will be to :

- strictly comply with all applicable environmental laws and regulations
- promote concept of Reduce, Recycle and Reuse
- maximize Green cover in our real estate projects

Our approach to achieve the guidelines of our policy :

- Submission of all the compliance reports with regard to air, water , noise pollution to the competent authorities
- Use of natural, recycled material to large extent
- Zero discharge of water through it's buildings by recycling and treatment of water
- Maximum provision of green cover with local species of shrubs , trees , plants
- Carrying out environment audits
- Adopting environmental friendly design of the buildings with it's orientation, use of façade glass, paints, block works, concrete , STPs etc.
- Use of efficient plant and machinery
- Using eco friendly cleaning agents in house keeping
- Use of renewable sources of power to extent possible
- Use of LED Light fixtures
- Promote use of environmental safeguards among our employees & stake holders

Anil Saraf
Chairman and Managing Director
ASF Insignia SEZ Pvt. Ltd

ASF INSIGNIA SEZ PRIVATE LIMITED

Sale Office : ASF Insignia SEZ IT/ITES, Village Gwalpahari, off Gurgaon-Faridabad Road, Gurgaon, Sohna-122003, Haryana
☎ +91 126 3777200 ☎ +91 126 6204110 ✉ corporate@asfinsigniastructure.com vs www.asfinsigniastructure.com
Regd. Office : 11, Babar Lane, Bengali Market, New Delhi-110001 ☎ +91 11 23355511 ☎ +91 1123739298
Corp. Office : ASF Centre, 362-363, Udyog Vihar, Phase-IV, Gurgaon-122016 (India)

CIN U45201DL2005PTAC120628

Creating Intelligent Spaces[®]

